
Capgemini | beazley

BEAZLEY
GPAS AND BILLING OPERATING MODEL

Ways of Working for GPAS Programme Delivery – DRAFT

Drafted: Mar-2024

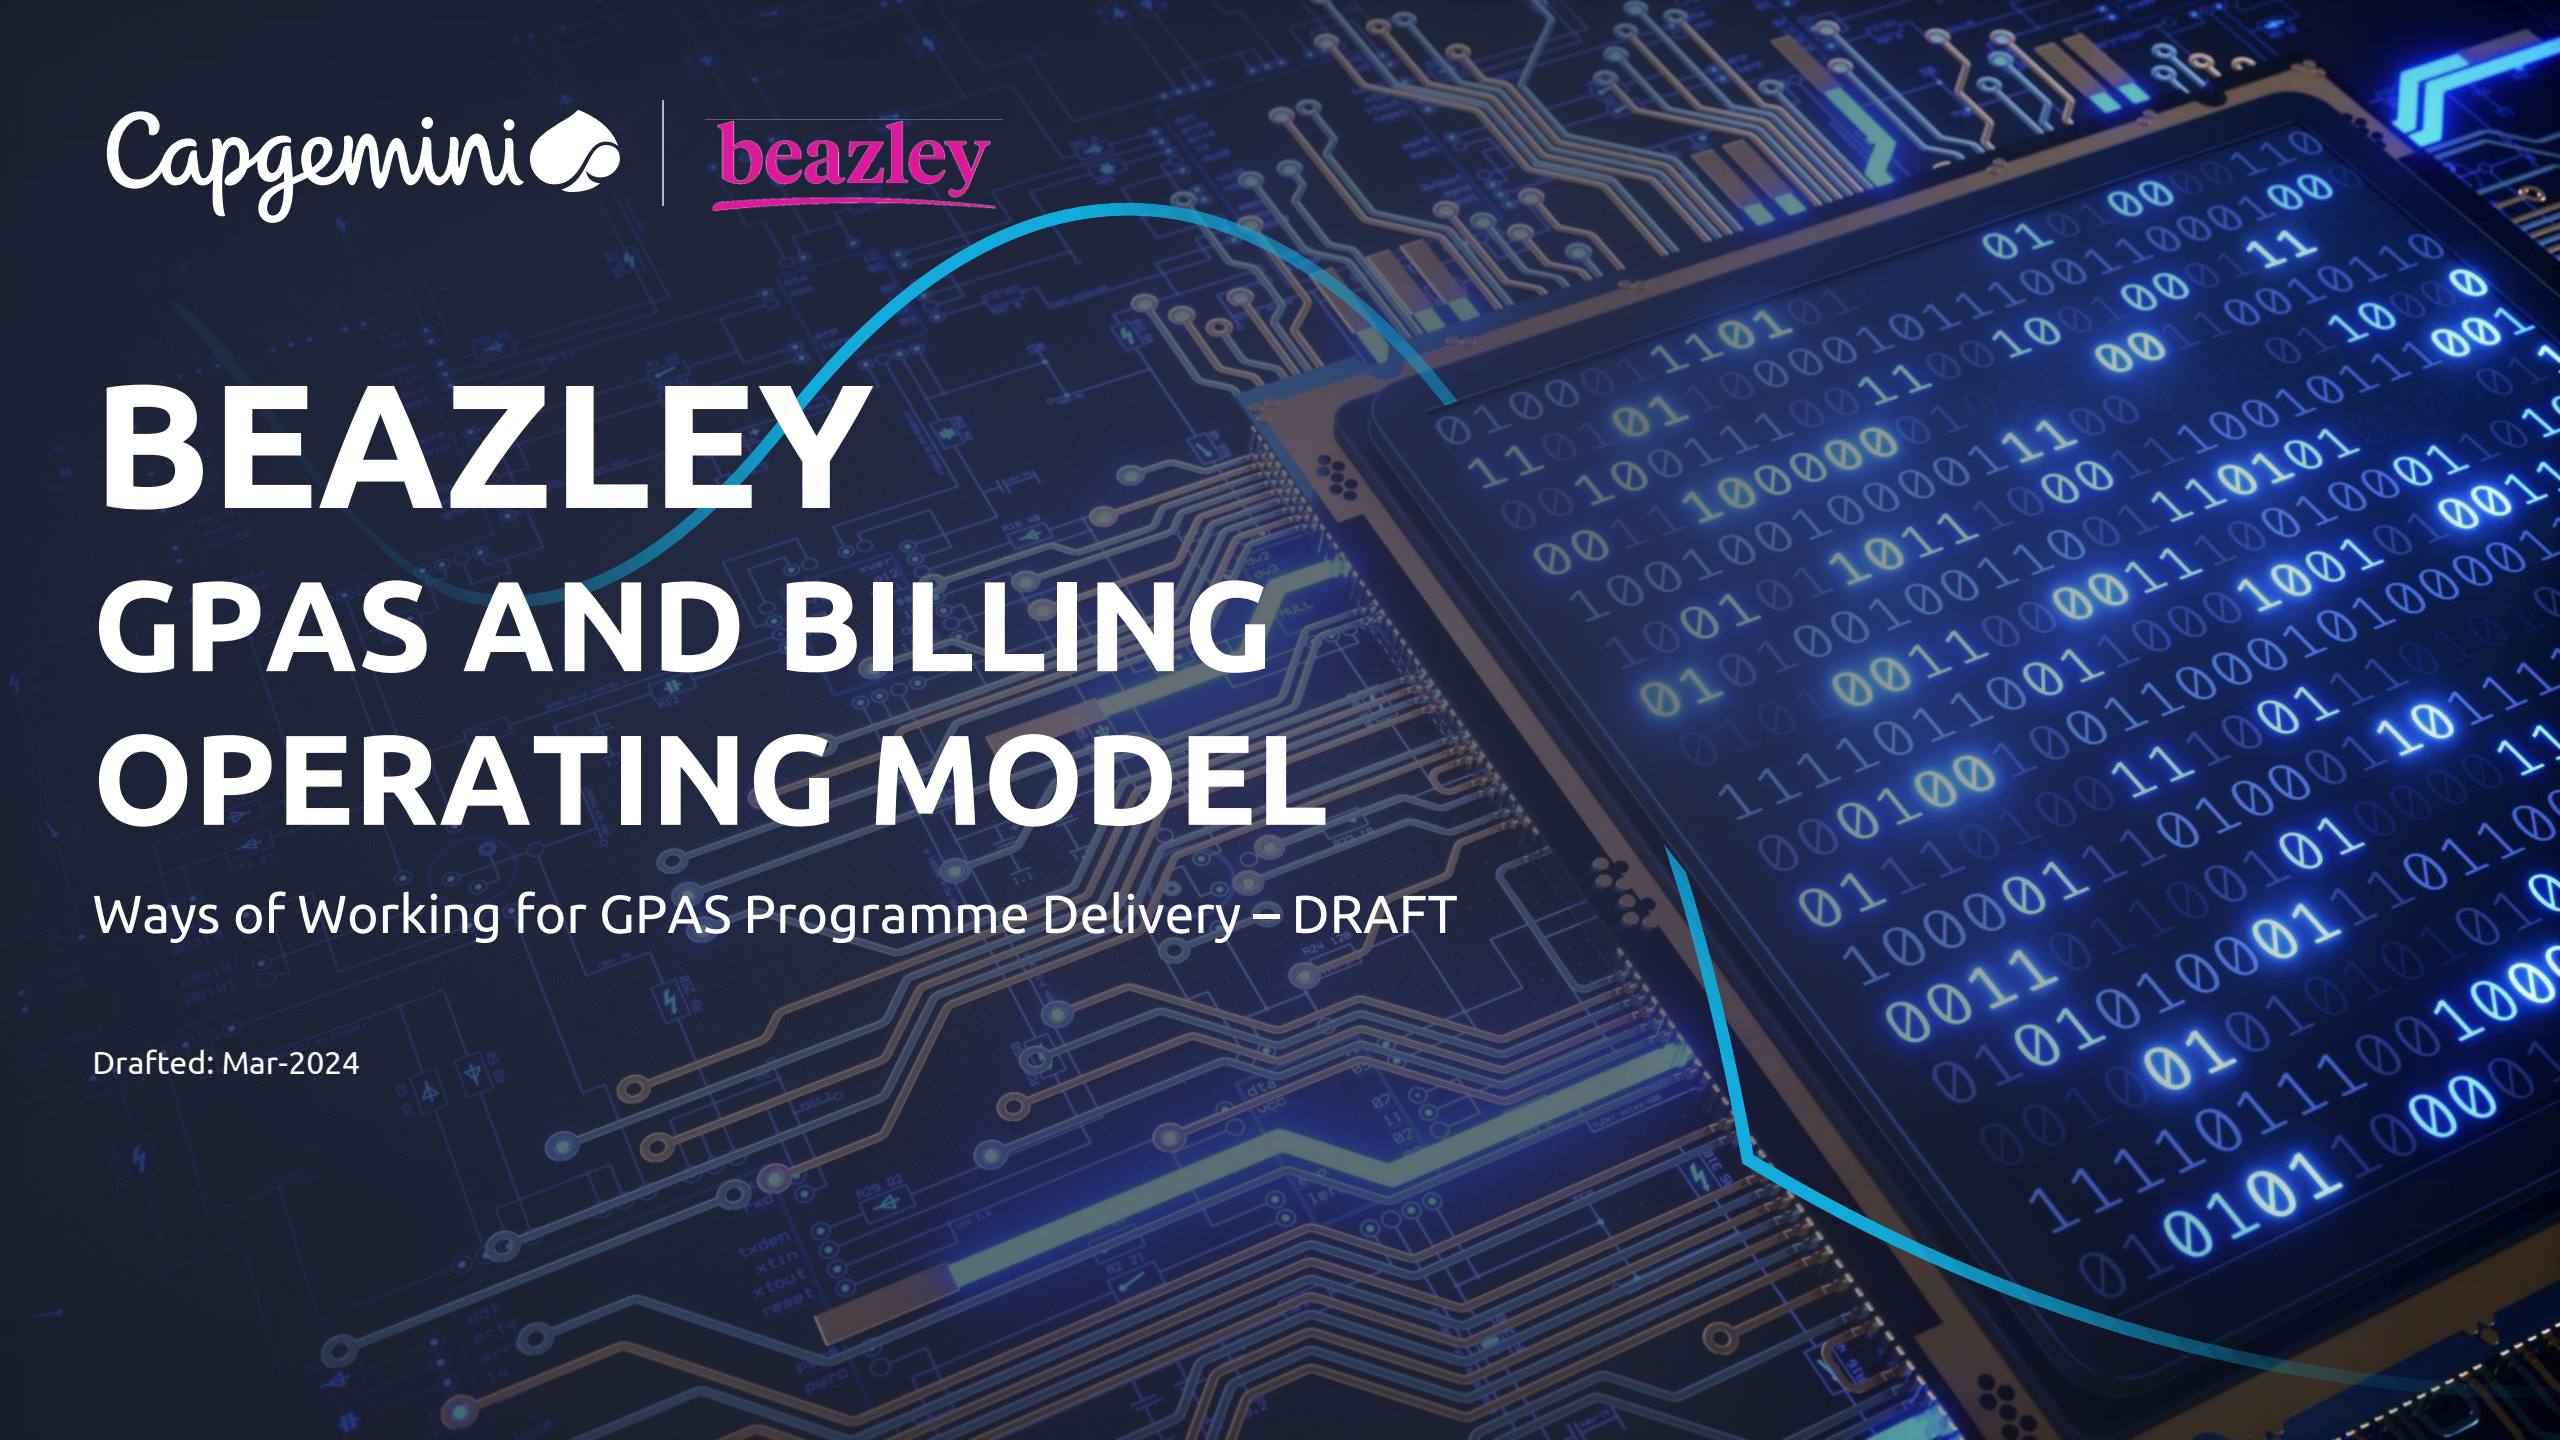

Document change history

S.No	Version	Month/Date	Changes made
1.	0.1	March-2024	First version of Ways of working, focused more at Inception phase method & processes
2	0.2	17th March 2024	Updates made basis feedback received from Warren – changes made to Team structure Warren to come back on Sign-off names from Beazley for Inception deliverables
3	0.3	19th March 2024	Updates to Core team based on Beazley feedback, text changes on context slide, Removed names against responsibilities for Beazley, Added GPAS and Billing in the RACI, New integration entry in RACI, Removed the approvers and sign-off to be updated later once Beazley confirms
4	0.4	25th March 2024	Updates to RACI, Two in a Box Structure and other minor changes
5	0.5	27th March 2024	Post call with Warren and Athik – Updates to two in a box slide, removed Inception team structure slide, Updates to key roles of Beazley, Updates to RACI, Add Lessons learnt from UWBB project
6	0.6	12th April 2024	Incorporated Faye's comments on Design principles and RACI – Delivery Management space
7	0.7	22nd April 2024	Updates to Structure, New slide to list Work streams, Changes to JIRA set-up slide, RAID management added, Key Role change for Beazley (added Subu)
8	0.8	23rd April 2024	Further updates to structure.
9	0.9	25th April 2024	Changes after the initial Inception workshop covering WoW document.

Company Confidential © Capgemini 2024. All rights reserved |

CONTEXT

Ways of working is a Capgemini recommended way of Program execution allowing all relevant parties and stakeholders to operate and collaborate towards achieving the common program goals. This document intends to target both processes and behaviours that form the building blocks of successful completion of GPAS


This Ways of working is specifically designed for GPAS and Billing scope of work only and for the scope of work owned by Capgemini. The processes, behaviours and recommendations outlined here may not be applicable outside GPAS to the wider Modernization program

The Ways of working document is expected to evolve iteratively, through Inception phase before it can be made final. However, throughout the GPAS program execution, the delivery method or process may undergo change in certain sections if all the influenced parties agree there is a need for improvement

Company Confidential © Capgemini 2024. All rights reserved |


WAYS OF WORKING

The immediate focus is to draft and agree on Ways of working applicable for the start of Inception phase covering activities, deliverables, methods and processes expected to be jointly built and done by Capgemini and Beazley. As a next step, this document will be extended to document methods and processes applicable to the Build phase.



To be built & agreed for start of Inception


- Scope of Inception phase
- Key Success factors
- Inception activities – week wise split
- Workshops – rules of engagement
- Inception phase deliverables
- Team Structure for Inception
- Design Principles
- RACI
- Key roles – Beazley and Capgemini
- Governance – Key roles, Cadence, Escalation, Change Control
- Tools for Inception
- JIRA set-up and governance



To be built & agreed in parallel to Inception for start of build

- Foundation & Waves Construct
- Backlog management process
- Sprint construct
- Cadence and ceremonies
- User story management
- Activities list
- DoD and DoR - Definition of Done and Definition of Ready
- Third party alignments and SLA
- Metrics & Reporting
- Collaboration and Tool sets

GPAS & BILLING – DRAFT HIGH LEVEL

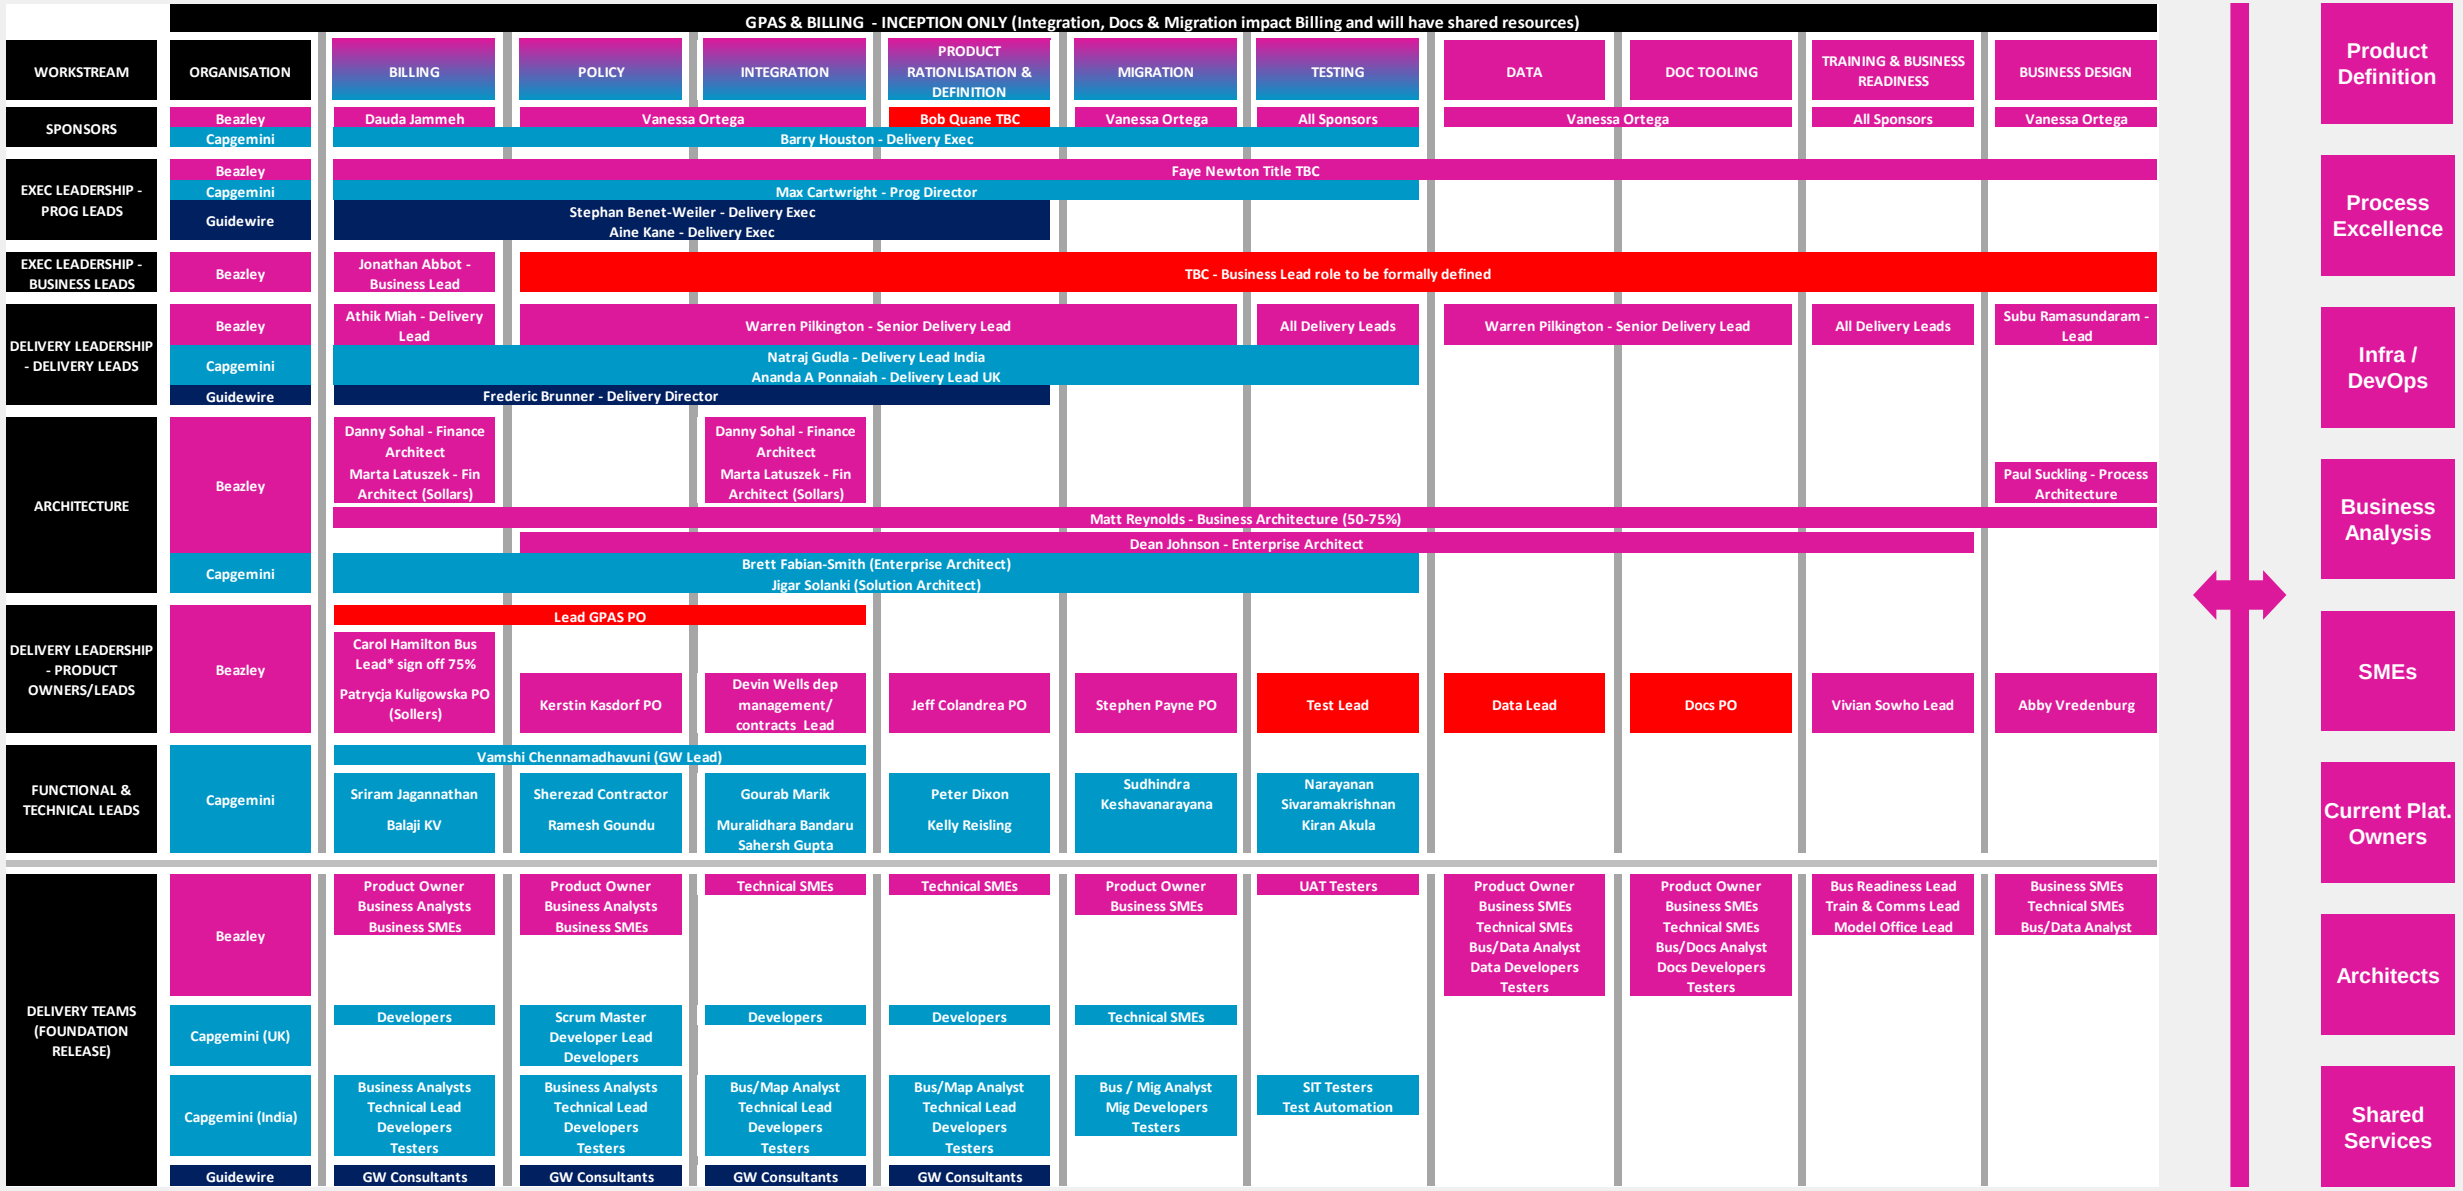

GPAS & BILLING PROGRAM WORK STREAMS

PROGRAM MANAGEMENT	• Responsible for Overall Program Governance that includes Planning, Monitoring execution to Budget, Mitigate Risks & Issues.
BILLING (Guidewire)	• Responsible to implement the new Billing system in Guidewire to handle Billing cycle of all new Policies to be initiated under the new Policy system
POLICY (Guidewire)	• Responsible to implement the new Policy system in Guidewire across all Beazley Product variations & Lines of Business in Scope
INTEGRATION	• Responsible to implement the in-scope integration elements necessary to ensure Guidewire operates as per business requirements.
PRODUCT RATIONALISATION	• Responsible to Rationalise product set for Foundation release and agree a framework for rationalising the remaining GPAS Products.
MIGRATION	• Responsible to Migrate all Legacy Policy data at renewal into the new Guidewire system.
TESTING	• Responsible to make sure we are deploying code to production that meets Business requirements & Program and Product quality standards
DATA	• Responsible to Build Data analytics on top of GPAS & Billing data meeting Business needs.
DOCS TOOLING	• Responsible to implement all necessary communications to support Beazley's business requirements.
TRAINING & BUSINESS READINESS	• Responsible to Design and Roll out the new system to Business users, handle training, comms, stakeholder Mgmnt., risks and issue mitigation.
BUSINESS DESIGN	• Responsible to create a centre of excellence for Beazley E2E process and journey design, ensuring consistency and quality.
ARCHITECTURE	• Responsible to create a System Architecture for the Program that is Robust, Industry standard, Scalable and meets Beazley's requirements
ENVIRONMENTS & INFRASTRUCTURE	• Responsible to provision all Infrastructure & Environments for a smooth Program execution e.g. Citrix machines, Scalable Dev, Test and Prod environments, DevOps support for continuous deployments & testing.
FINANCE	• Responsible to validate & sign-off Finance systems to the new GPAS & Billing implementation
LEGACY	• Responsible to support Data Migration workstream enabling smooth migration of all Legacy Policy records into the new system

Key: Defined Workstreams/Teams | TBC Workstreams/Teams


Company Confidential © Capgemini 2024. All rights reserved |

INCEPTION PHASE HELPS TO CREATE THE FOUNDATION AND VISION FOR THE TRANSFORMATION

A common 12-weeks Programme Inception phase to clarify and align the scope in all Products for a Foundation, followed by the implementation of the planned Releases.

Programme Inception → **Design and Build**

Programme Inception is focused on "**Designing the next winning proposition**"

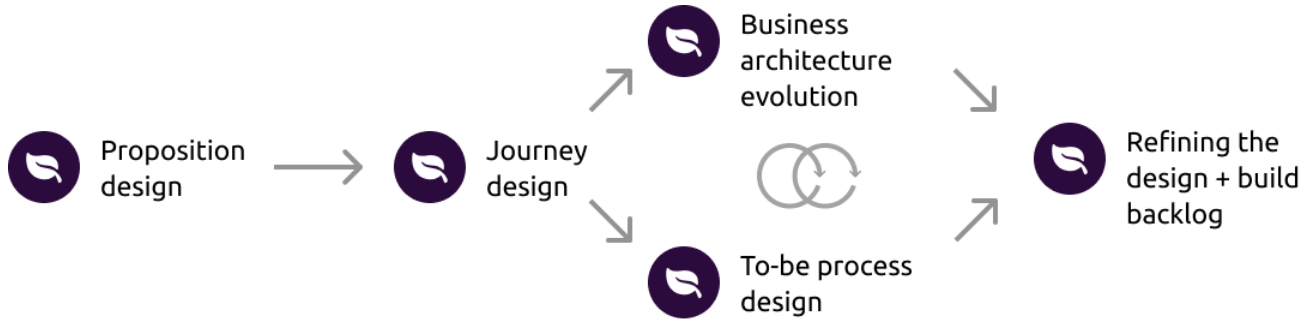

What you'll get:

1. Prioritized backlog
2. High Level Design
3. Foundation release plan
4. Key risks & assumptions
5. Dependencies detailed

- Foundation Release Mobilization is focused on enabling MVP Design and Build to start
- Build the foundation with core principles intact. – data/ automation / experience
- Collaborative pre-work on entry criteria to ensure rapid start and timely completion
- Transform the plan from the Inception to reality, transforming the business requirements to functional systems
- Plan for future Releases and LOB
- Confirm Roll-out Approach
- Key Design Decisions log

Company Confidential © Capgemini 2024. All rights reserved |

KEY SUCCESS FACTORS

Right Time

- Multi-day sessions
- Aligned workshops
- Covering India, UK and US time zone

Right Inputs

- Product / Process Design
- OOTB Guidewire Process Flows
- Interfaces

Right Team


- Product Owners, Business SME
- Right Capgemini team
- Collaboration is key

Right Enablers

- Guidewire Instance
- Collab Tools
- Reliable access to VDIs

Right Decisions

- Timely & accurate decisions
- On time escalations for help
- Lean thinking

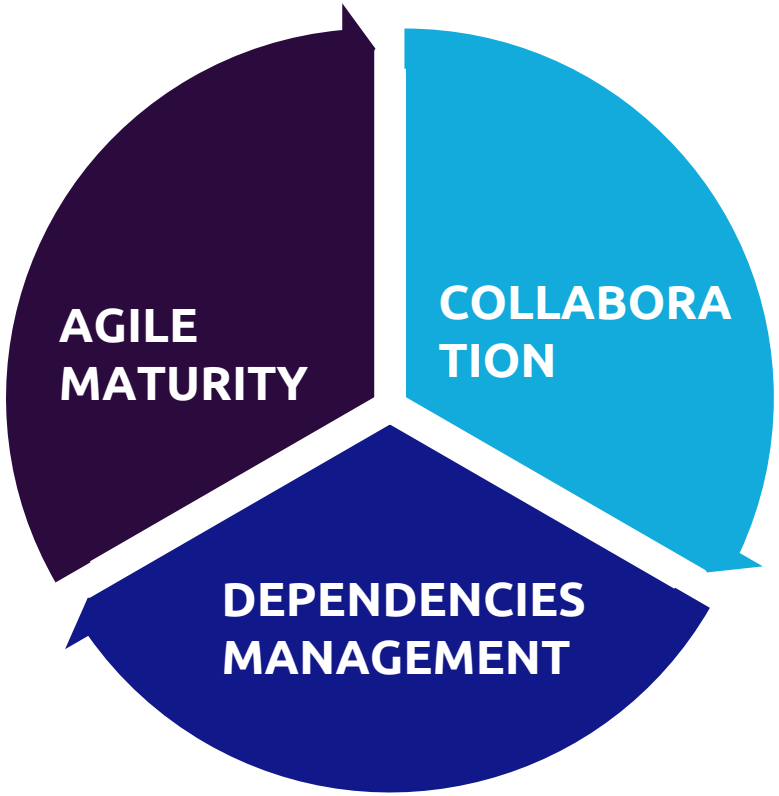

Inception Phase Principles

OOTB Conformance

Business Priority / Rationale

Design for Future

Outputs more focused at Foundation release

- GPAS Ways of working
- Prioritized Backlog
- Effort & Resourcing
- GPAS & Billing HLD and Delivery Plan
- LLD for Initial build phase
- Key Design Decisions
- Migration Strategy
- Integration Inventory
- Dependency tracker
- Test Strategy
- Rationalized Product set

Pebbles / Rocks / Boulders

Categorizing elements of solution for appropriate escalation to finalise scope

Company Confidential © Capgemini 2024. All rights reserved |


DESIGN PRINCIPLES

All key decisions to move through formal programme governance decision bodies

Does the decision?:

- Support the agreed Release scope
- Ensure the business is not in a worse position from before
- Support a move off existing systems
- Support flexibility and maintainability for future releases
- Conform to Beazley architectural principles
- Allow for scalability and is not closed off for future-states
- Complies to Beazley's Information Security requirements

Decision making process:

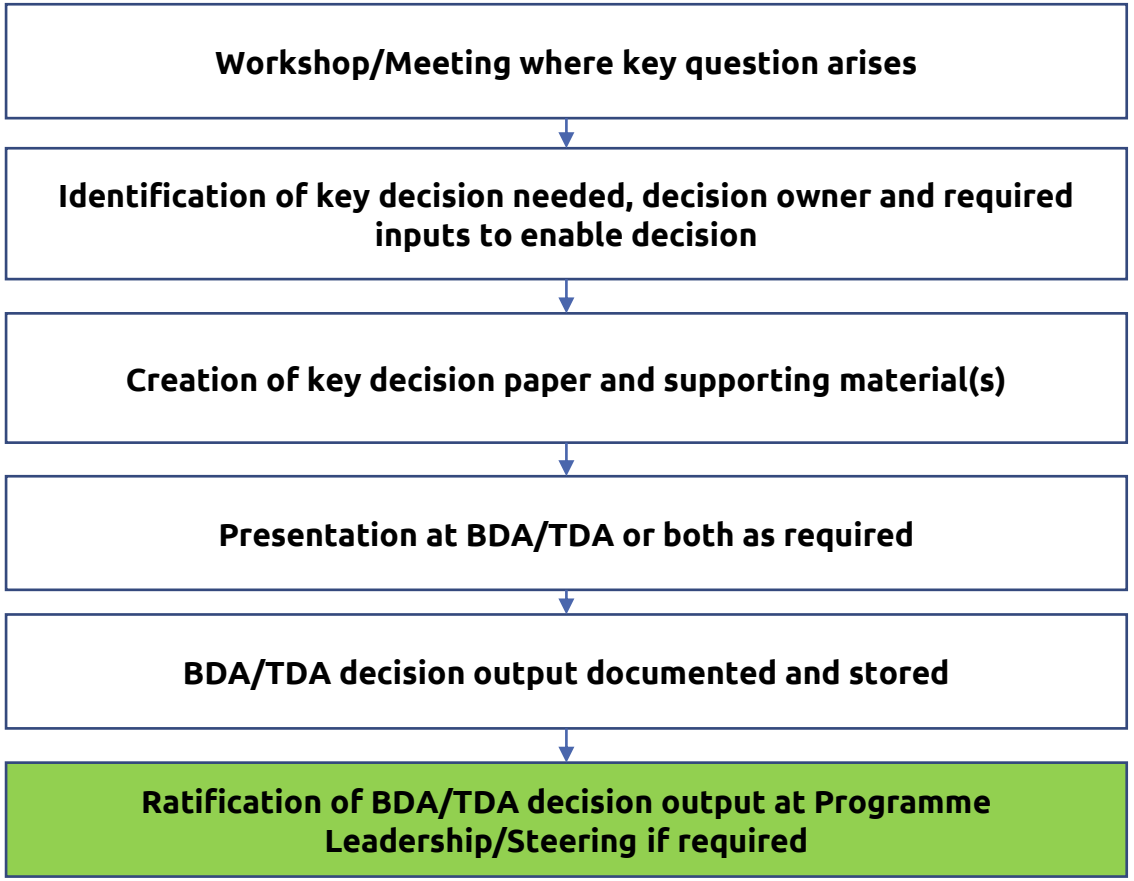


Company Confidential © Capgemini 2024. All rights reserved |

GUIDELINES FOR MEETINGS AND WORKSHOPS

Rules of Engagement

- All meeting and workshop invites to include:
  - Purpose of the meeting / Agenda
  - Input to the meeting
  - Expected output from the meeting
  - Deliverable(s) output (as required)
- Business attendees and availability to be confirmed by Beazley (Senior Product Owner/relevant Product Owner) before invitation is sent
- Parking lots/Decision logs to be captured and logged in the required trackers
- Critical decisions to go through appropriate Programme Governance forums and documentation
- On site and remote attendance options to be available
- Recording of sessions to be used where appropriate
- All sessions to be aligned to overall programme strategy
- All material to be utilised for Beazley programme purposes only









Company Confidential © Capgemini 2024. All rights reserved |

INCEPTION PROGRAMME DELIVERABLE OUTPUTS

Deliverables at programme level & expected signatories

Deliverables to be produced during Inception, ready for review and response feedback loop. All deliverables to have a wider review distribution which will be confirmed on the deliverable itself.

Deliverable Names	High level Description and Expectation	Review	Sign Off
PD1: GPAS Ways of Working	Detailed methodology, Governance model, Change control model, communication management, Reporting & meeting cadence, Initial team structure, RACI, Escalation approach, Tools for build & usage boundaries	Core GPAS Team	Steering Group GPAS/Billing
PD2: Prioritized Backlog (Foundation)	Documentation of Foundation Release Functional requirements, in scope Epics/Features. User Stories scope statement defined in excel format for uploading into JIRA	Core GPAS Team	Product Owners
PD3: Resourcing & Efforts (Foundation)	Breakdown of resourcing needs (by quarter) aligned to effort and bottom-up estimation of Epics and Features against the delivery plan. High level scope, budget, and resourcing/effort should reconcile.	Core GPAS Team	Delivery Leads
PD4: Delivery Structure & Plan (Foundation)	Phase & Workstream definitions, objectives and milestones. Verification and Acceptance. Plan detailing the Guidewire sprint plan, number of sprints, dates, and high-level proposed scope breakdown.	Core GPAS Team	Delivery Leads
PD5: GPAS High Level Design	Aligned to agreed architecture decisions and principles Detail how Policy and Billing Center will fit into Beazley ecosystem. Detail the key Integrations for the Foundation release	Core GPAS Team	Enterprise Architects
PD6: Migration Strategy	Approach to migration in terms of execution and timing. High-level data requirements at an entity level, from relevant business areas.	GPAS Steering Group	Strategic Design Authority
PD7: Integration Manifest	Inventory of integrations defining cardinality, service contract ownership, integration pattern or method, initial view on complexity. Definition of any intermediated services or gateways to influence design.	Product Owners Integration Lead	Enterprise Architects

Company Confidential © Capgemini 2024. All rights reserved |

INCEPTION PROGRAMME DELIVERABLE OUTPUTS

Deliverables at programme level & expected signatories

Deliverables to be produced during Inception, ready for review and response feedback loop. All deliverables to have a wider review distribution which will be confirmed on the deliverable itself

Deliverable Names	High level Description and Expectation	Reviewer	Sign Off
PD8: Detailed Dependency Tracker	Internal and External Dependencies detailed with dates and deliverables agreed with each of the related parties.	Core GPAS Team	Delivery Leads
PD9: Functional & Technical Principals	Functional and Technical Design principles documented.	Core GPAS Team	Delivery Leads
PD10: GPAS Test Strategy	High level scope of key test phases, gates and entry/exit criteria; view of resourcing. Input into Definition of Done (DoD) including acceptance criteria, automation definition. Definition of the GPAS environment requirements and when they will be required by to meet the timelines.	QA Lead Core GPAS Team	Delivery Leads
PD11: Product Set	Rationalised product set for foundation release Identification of any products requiring further analysis and key decision papers where necessary.	Core GPAS Team Product Definition Workstream (UW)	Strategic Design Authority
PD12: Perform a Jutro Proof of Concept.	Walkthrough of PoC which should demonstrate the applicability of Jutro to Build out UWWB screens. Options paper detailing the pros/cons of Jutro approach vs building it out in UWWb.	Reviewed and Agreed with Beazley EA (GPAS & Billing)	Beazley EA
PD13: Perform a cash matching Proof of Concept for Billing	Walkthrough of PoC which should demonstrate that cash matching requirements can (or cannot) be assigned from backlog	Reviewed and Agreed with Beazley PO (Billing)	Product Owner (Billing)

To maximise efficiency and protect our plans, we will work with a '2 review plus sign off' approach to deliverable sign off. Initial review (3 working days), second review (2 working days) and sign off (1 working day). Expectation is that the second review includes feedback from 1st review updates only. A tracker will be used to help track and manage progress.

Company Confidential © Capgemini 2024. All rights reserved |

KEY AREAS – RACI [1]

Area	Beazley	Capg	Guidewire
Modernization Program Activities	A/R	C	I
Program planning & delivery			
Ways of working for all Programs under Modernization			
Procurement Management			
Program communications and stakeholder management			
SteerCo & Leadership reporting			
PMO	A/R	C	I
Risk and Issue Management tracking			
Dependency Mangement tracking			
Programme Metrics & Milestone tracking			
Programme Budget & Invoicing payments tracking			
Project infra needs set up coordination & tracking			
Deliverables tracking			
Requirements Gathering and Management (GPAS & Billing)	A	R	C
Product Backlog refinement and Business process mapping			
User story refinement with business rules and acceptance criteria			
Requirements sign-off			
Prototyping and mock-ups			
Workshops schedule, execution & follow-up			
Architecture and Technical Management (GPAS and Billing)	A/R	R	R
Confirm Architecture and Design Principles			
High level designs			
Create and maintain Technical Design Decisions			
Low level design			
Data Migration Strategy			
Environments and Infrastructure	A/R	C	R
Infrastructure and environments planning and provisioning			
Deployments, maintainence and supplier issues resolution			
Capacity planning & scalability			
Security and Compliance implementation			
Monitoring, management & performance optimisation			

Area	Beazley	Capg	Guidewire
GPAS and Billing Delivery	C	A/R	C
Delivery Management - sprint plan and execution, status reporting, risks/issue logging, risks/issue mitigation within Cap control, recording and monitoring Cap specific dependencies, problem management within Cap control, stakeholder management, change control management affecting Cap scope of work			
Develop user stories adhering to Guidewire Cloud standards			
Unit testing adhering to Guidewire Cloud Standards			
Sprint plan and raising dependencies			
Resolve Guidewire Cloud standard assessment observations			
Sprint progress reporting			
E2E Testing	A/R	C	I
End to End Test Strategy and Execution			
JIRA and Confluence set-up			
Metrics and Reporting			
Risks and Issues management			
Defects resolution specific to GPAS & Billing components	C	A/R	C
GPAS and Billing Sprint Testing	A	R	I
Functional test plan and execution			
Risks, Issues and Dependencies status reporting			
JIRA and Confluence set-up			
Metrics and Reporting using JIRA			
Release Management	A/R	C	C
End to end release plan roadmap for the Program			
Strategy, Processes and teams for deployments, check points			
Third party coordination for all environments			
Cutover, Go-live and Post Go-live Support	A/R	R	R
Cut-over plan and Implementation Management			
Establish post Go-live Support Model			
Infrastructure and environments set-up			
Service Design and PGLS Plan			
Incident fixes specific to GPAS & Billing during warranty	C	A/R	C

Key

A	Accountable	Authority and decision making
R	Responsible	Responsible for actualisation of the task
C	Consulted	Engaged stakeholder, consulted in decisions, delivery and approach to enable their input
I	Informed	Informed stakeholder receiving updates and outputs only

RACI

Company Confidential © Capgemini 2024. All rights reserved |

KEY AREAS – RACI [2]

Area	Beazley	Capg	Guidewire
Business Change Management	A/R	C	I
Change Impact assessment and readiness			
Business roll-out plan			
Communications and reporting			
Legacy	A/R	C	I
Management of legacy party stakeholders			
Delivery of dependencies as per Program plan			
Management of design, build and testing required by GPAS & Billing			
Communication on Legacy changes that impact GPAS & Billing			
Status updates and reporting			
Finance	A/R	C	I
Management of Finance party stakeholders			
Delivery of dependencies as per Program plan			
Management of design, build and testing required by GPAS & Billing			
Communication on Finance changes that impact GPAS & Billing			
Status updates and reporting			
Documents - Beazley to confirm platform selection and requirements, post which this section to be revised as it is highly likely Capgemini will be asked to do the build	A/R	C	I
Document supplier and platform management			
Deliver Document platform dependencies as per Program plan			
Documents design			
Document template requirements, build and test			
Environment and Infrastructure management			
Data & Analytics	A/R	I	I
Data Management Strategy			
Data & Analytics build and test			
Analytics Reporting requirements & build			
Dependency management with rest of the Program			
App Events - Capgemini to do the assessment on effort required, to be done in parallel to inception			
CDA		R	

Area	Beazley	Capg	Guidewire
Third Parties (Integrations & Guidewire)	A/R	C	I
Third party management			
Third party deliverables alignment to Program plan			
Third party environments management			
Issues resolution with Third parties			
Status updates and reporting			
Policy Data Migration	A/R	C	I
E2E Oversight			
Legacy Data provisioning (for Dev, Test, SIT and Dry-run)			
Legacy Data management (incl. data profiling)			
Infrastructure provisioning (for Dev, Test, SIT and secure Data env for Dry-run)			
Policy Data Migration Strategy / High-level Design (HLD)		R	
Policy Data Migration technical solution			
Policy Data Migration mapping and Gap analysis (between Source & Target - GW)			
Policy Data Migration implementation and Go-live strategy			
UWWB (Underwriting Work Bench)	A	C	I
Requirements management			
Deliverables alignment to Program plan			
Environments management			
Issues resolution impacting Program			
Status updates and reporting			
GPAS and Billing Integration (Guidewire only) - External (third party) and Internal (Beazley systems)	A/R	R	I
Integrations design			
Integrations inventory			
High Level Design			
Low Level Design			
Technical mapping document			
Plan, Build and unit test integrations			

Key

A	Accountable	Authority and decision making
R	Responsible	Responsible for actualisation of the task
C	Consulted	Engaged stakeholder, consulted in decisions, delivery and approach to enable their input
I	Informed	Informed stakeholder receiving updates and outputs only

Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES – BEAZLEY

Role	Named Resource	Responsibilities
Business Owner/ Sponsor	Vanessa Ortega Dauda Jammeh	• Approve scope, target design and execution plans for the PAS initiative. • Accountable for delivery against OKRs, business outcomes and benefit realisation. • Commits or helps facilitate appropriate resources (e.g. SMEs) and support issue resolution for the PAS initiative. • Approve and oversee key initiative decisions as adviser • Steer solution design and build based on business needs
Program Director	Faye Newton	○ Be the Single point of Ownership from Beazley on the Program ○ Program Manage execution of the GPAS & Billing Business requirements ○ Mitigate Program Risks and Issues from time to time ○ Provide leadership and Direction to motivate teams towards successful program completion ○ Collaborate with involved stakeholders for success of the Program
PAS Delivery Lead / Billing Delivery Lead	Warren Pilkington Athik Miah	• Develop the initiative objectives, scope, high-level implementation roadmap, resource requirements and investment estimates. • Working with the delivery partners, create and manage the PAS delivery plans. • Manage the delivery teams inc. resource management, supply & demand, technical capability and skills • Manage inbound and outbound dependencies needed for the delivery of the component • Management of risks and issues impacting progress • Responsible for status reporting of the project
Global PAS Technical/Functional Lead	Jeff Colandrea	• Helps define the PAS Product Strategy, Vision and Roadmaps alongside the Product Owners in the PAS initiative. • Managing and prioritising the PAS Portfolio Backlog taking care to ensure alignment with business architecture, data teams and existing BAU environments. • Delivering Value by ensuring the PAS solutions are complete from the user perspective (including operations, change etc.) and deliver meaningful business value. • Point of escalation and coaching for squad-level Product Owners.
Solution Architect Lead	TBD	• Work with squads to define target technical solutions. • Gain approval through Design Authority for technical solutions. • Monitor technical risk and mitigation control. • Define technical guardrails for delivery squads. • Embed technical work into backlogs of delivery squads.
Product Owner	As per the structure chart / in progress	There will be different Product Leads depending on the release/wave of PAS implementation. For example, Cyber and D&O in Foundation release. • Understand and be able to describe the end-to-end solution in a high level, the use cases and related business drivers. • Attend decision making sessions, feeding input regarding the product and its interaction with other components, acting as a point of reference for the product required features and behaviour. • Understand business demands and requirements and translate these into solutions that are refined iteratively and present them to the team. • Prioritise requirements of the product and make adjustments as needed after each release. • Define the future goal of the product (the 'product vision') • Maintain and own the product backlog. • Accepting or rejecting suggested improvements. • Report progress, involvement in governance arrangements.

Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES – BEAZLEY

Role	Named Resource	Responsibilities
Quality Assurance Testing Lead	TBD	• Ultimately accountable for the quality of the overall end to end solution • Provides overall QA oversight for test design and execution, striving for commonality where appropriate • Accountable for defining Program level test strategies and approaches for all test phases • Accountable for planning and oversight of all test phases, including UAT • Provides testing oversight and direction, drives execution of testing strategies and manages testing related objectives and issues across the Program
Release Quality	Stephen Payne	• Partnering with Product Manager • Assisting in management of risks, issues and any potential roadblocks • Responsible for resolving contingencies and complicated issues, provide leadership to project teams, and act as a consultant/coach to management • Responsible for DevOps and improvement of workflow
Business Architecture Lead	Subu Ramasundaram (Business Design Framework) Matt Reynolds Marta Latuszek	• Accountable for developing the business architecture strategy • Applying structured business architecture approach and methodology • Drives and facilitates the right discussions with business leaders to identify business capabilities in relation to current and future business objectives • Responsible for presenting recommendations and solutions clearly and concisely • Accountable for a specific LOB, business pillar or multiple segments, and high level of complexity and attributes
Change Management Lead	TBD	• Responsible for managing all types of change • Evaluates the impact of change • Supports development of communications relevant to change initiatives • Accountable for defining success metrics and measuring performance against these
Training / Communication	TBD	• Coordinating the development, execution, refinement, and measuring the impact of programme outreach, communications, and knowledge management strategies • Responsible for coordinating development of training / learning materials • Accountable for the organization, coordination of workshops and events • Responsible for supporting communications, knowledge management, and training activities
Data Lead	TBD	Accountable & Responsible for • Data and Analytics requirement, vision & strategy and approach • Coordinate the creation of a design for data loads and downstream data use • Coordinate with Program stakeholders upstream and downstream to fulfil data reporting requirements
Migration Lead	TBD	Accountable & Responsible for • Project Management of End-to-End Migration strategy and implementation • Leading teams capable of handling data sourcing, profiling, rectification and reconciliation tasks • Finalizing a migration design and business exception handling

Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES - CAPGEMINI

Role	Named resource	Description	
Delivery Executive	Barry Houston	○ Responsible for overall Services quality and delivery ○ Assist in the resolution of issues and change controls	○ Prepare for and support Steering/Policy Executive Advisory Group Meetings ○ Monitor program progress
Program Director	Max Cartwright	○ Responsible for in-scope Program activities ○ Provide Program status reporting on a regular basis to Beazley Program and Executive Leadership	○ Responsible for overall Services quality and delivery of the Program ○ Responsible for day-to-day management and tracking of the in-scope Program activities
Engagement Manager	Ananda Arasu Pommaiah	○ Manage the detailed Program plan in collaboration with Beazley Leadership Team ○ Provide Program Status reporting on a regular basis to Beazley Program Leadership	○ Facilitate Decisions, Issues and Risk management across the core program and escalate to Beazley in advance of the materialization of potential risks and issues that may delay the program. ○ Assist the resolution of issues and change controls
India Delivery Executive	Natraj Gudla	○ Manage the detailed Program plan in collaboration with Beazley Leadership Team ○ Provide Program Status reporting on a regular basis to Beazley Program Leadership	○ Facilitate Decisions, Issues and Risk management across the core program and escalate to Beazley in advance of the materialization of potential risks and issues that may delay the program. ○ Assist the resolution of issues and change controls
Product Rationalisation	Peter Dixon Kelly Riesling	○ Provide subject matter specialist advice with regard to overall business requirements and product backlog ○ Provide input on solving business problems within the defined application landscape by working with the business and Technical resources.	○ Coordinate with Functional Lead and Technical architect to help define implementation scope of work.
Enterprise Architect	Brett Fabian-Smith	○ Provide leadership and architectural expertise across a broad set of technologies, including integration & middleware technologies ○ Consult with and advise the Program team on technology and strategic decisions	○ Identify architectural constraints for the architectural level (project, domain, application) based on technical and organizational requirements ○ Provide subject matter specialist advice with regard to overall solution architecture and technology
PolicyCenter Functional Lead	Sherezad Contractor	○ Provide Policy subject matter experience ○ Work with Beazley business leadership to drive overall business requirements	○ Provide leadership and direction for elaboration and RSWs ○ Provide joint review and approval of deliverables
BillingCenter Functional Lead	Sriram Jagannathan	○ Provide Billing subject matter experience ○ Work with Beazley business leadership to drive overall business requirements ○ Provide leadership and direction for elaboration and RSWs	○ Provide joint review and approval of deliverables ○ Lead with the high-level implementation approach for complex functional requirements
PolicyCenter Technical Lead	Vamshi Chennamadhavuni	○ Provide subject matter specialist advice with regard to GW PC ○ Conduct configuration option analysis to support business requirements ○ Provide input on GW PC best practices, constraints, and effort during workshops, including pre-work	○ Provide input on effort and impact associated with potential configurations/customizations ○ Support the Policy Functional Lead with the high-level implementation approach for complex functional requirements
BillingCenter Technical Lead	Sriram Jagannathan	○ Provide subject matter specialist advice with regard to GW BC ○ Conduct configuration option analysis to support business requirements ○ Provide input on GW PC best practices, constraints, and effort during workshops, including pre-work	○ Provide input on effort and impact associated with potential configurations/customizations ○ Support the Policy
Integration Lead	Saharsh Gupta Gourab Marik	○ Provide integration and technical architecture guidance for GW ○ Lead analysis effort of interface specification documents	○ Lead the integration design effort for specified integration points ○ Provide direction and technical guidance

KEY ROLES - GUIDEWIRE


Role	Named resource	Description
Delivery Director	Frederic Brunner	
Delivery Executive	Stephan Benet-Weiler Aine Kane	

Company Confidential © Capgemini 2024. All rights reserved |

GOVERNANCE

The overall success of this engagement will be based on close collaboration between all parties, transparency and fact-based decision making. We will also use this Governance process to keep us all collectively honest and true to the Programme objectives.

Note: Under Review

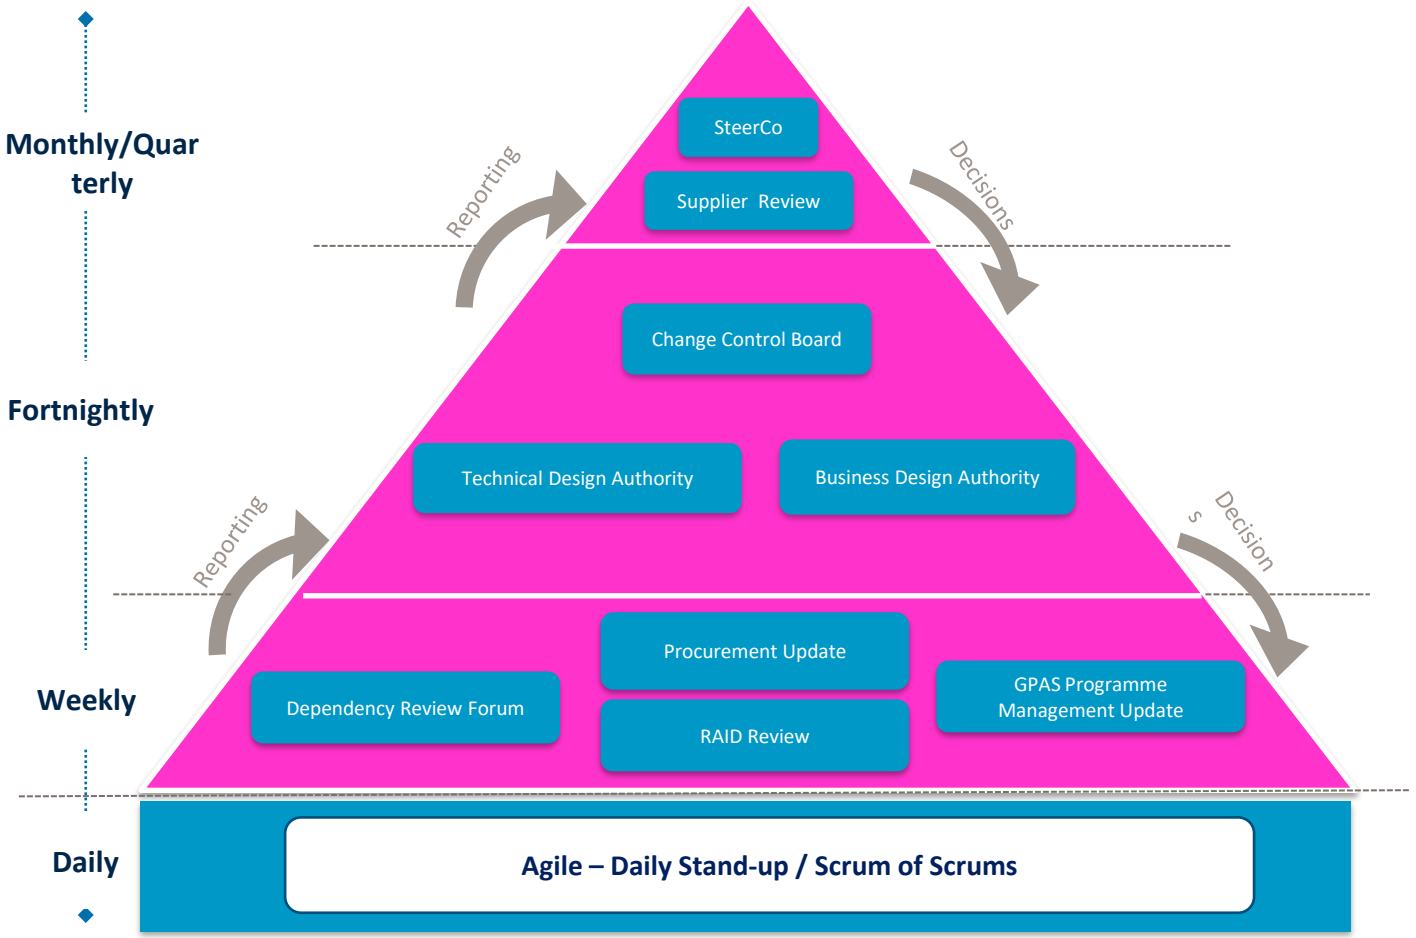

Company Confidential © Capgemini 2024. All rights reserved |

PROPOSED PROGRAMME CADENCE

Key

Daily	Weekly	Fortnightly	Monthly	Quarterly

*Supplier Review Meeting occurs following Friday of sprint closure


	Monday	Tuesday	Wednesday	Thursday	Friday
9.00 – 9.30	Daily Standups	Daily Standups	Daily Standups	Daily Standups	Daily Standups
10.00 – 10.45	Scrum of Scrums	Scrum of Scrums	Scrum of Scrums	Scrum of Scrums	Scrum of Scrums
11.00 – 12.00					
12.00 – 13.00					
13.00 – 14.00		Procurement Update			PMO RAID review
14.00 – 15.00		Dependency Forum	Change Board	Technical Design Authority	
15.00 – 16.00		Business Design Authority	Steer Co	Programme Management Update	Supplier Review*
16.00 – 17.00					

PROPOSED ROLES & CEREMONIES MATRIX

Roles & Ceremonies	Daily Standup (Workstream) (9:00 to 9:30)	Daily Scrum of Scrums (WS Leads) (10:00 to 10:45)	Dependency Forum (Tuesday) (14:00 to 15:00)	PMO RAID Review (Friday) (13:00 to 14:00)	Supplier Review Meeting (Friday) (15:00 to 16:00)	Programme Management update (Thursday) (15:00 to 16:00)	Change Board (Wednesday) (14:00 to 15:00)	Procurement Update (Tuesday) (13:00 to 14:00)	Business Design Authority (Tuesday) (15:00 to 16:00)	Technical Design Authority (Thursday) (14:00 to 15:00)	Steer Co **Monthly?** (Wednesday) (15:00 to 16:00)
Business Sponsors /Delivery Exec								x	x		x
Programme Director		x	x	x	x	x	x	x	x		x
Delivery Leads		x	x	x	x	x	x	x	x	x	x
Product Owner	x	x	x	x	x	x	x		x		x
Functional Leads	x	x	x	x		x	x		x		
Subject Matter Experts		x				x	x		x	x	
Architects	x	x	x	x		x			x	x	
Platform Owners		x	x	x	x	x	x	x	x	x	x
Technical Leads	x	x	x	x		x	x	x		x	
Test Managers	x	x	x	x		x	x				
Development Team	x					x					
Product Rationalization Team	x	x	x	x		x			x	x	x
Procurement Team		x	x	x	x	x		x			
DevOps Team	x	x	x	x		x				x	
PMO Team		x		x	x	x					

Company Confidential © Capgemini 2024. All rights reserved |

ESCALATION PROCESS

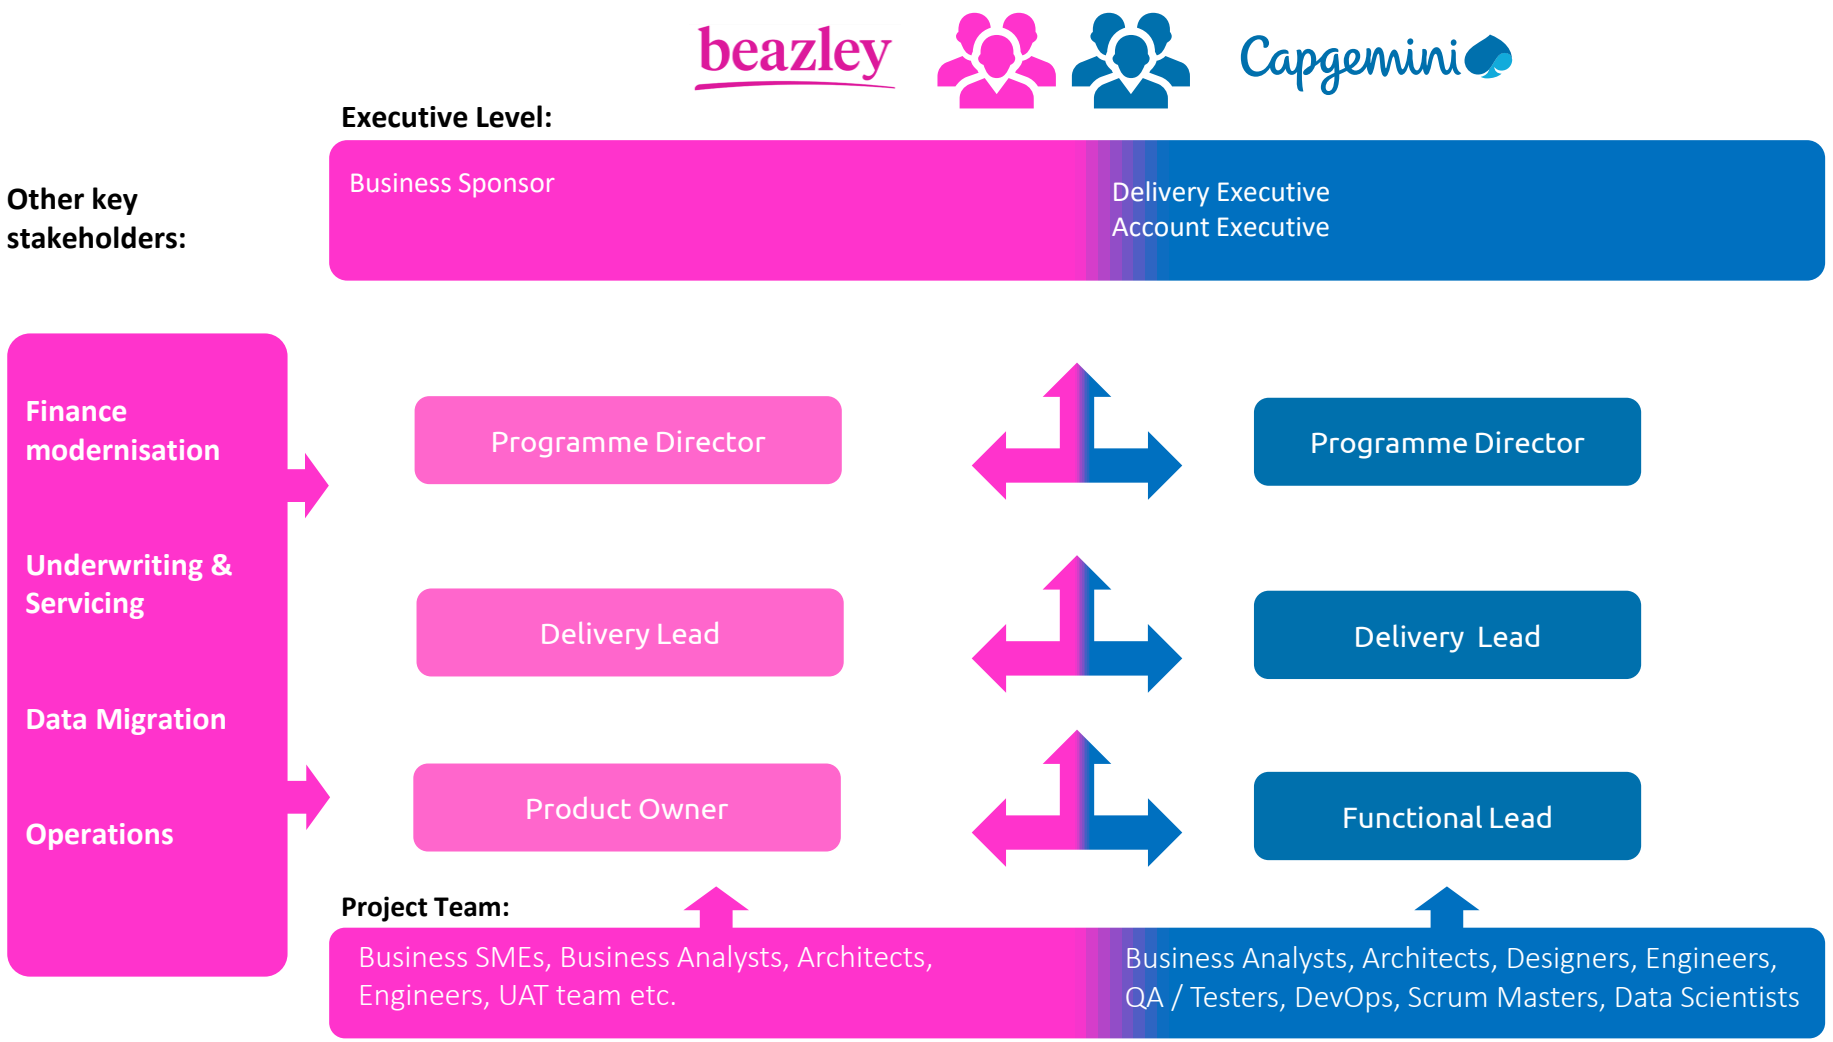

Escalation Etiquette:

Escalations are done jointly from Capgemini and Beazley representatives from one level to Capgemini & Beazley representatives at the next level up.

Prior to escalation, representatives will work together to:


1. Agree what they agree on
2. Agree what they disagree on
3. Prepare for the escalation, making clear:
   - The problem statement
   - The options for resolution and their pros and cons
   - The decision(s) and / or action(s) required
   - The date required by
   - The impact of doing nothing / missing the date

Company Confidential © Capgemini 2024. All rights reserved |

CHANGE CONTROL

Controlling change via an agreed process that acknowledges it is needed but manages its impact for the good of delivery is key to the success of this largescale programme delivery.

Note: CR tolerance is being agreed to expedite decision making

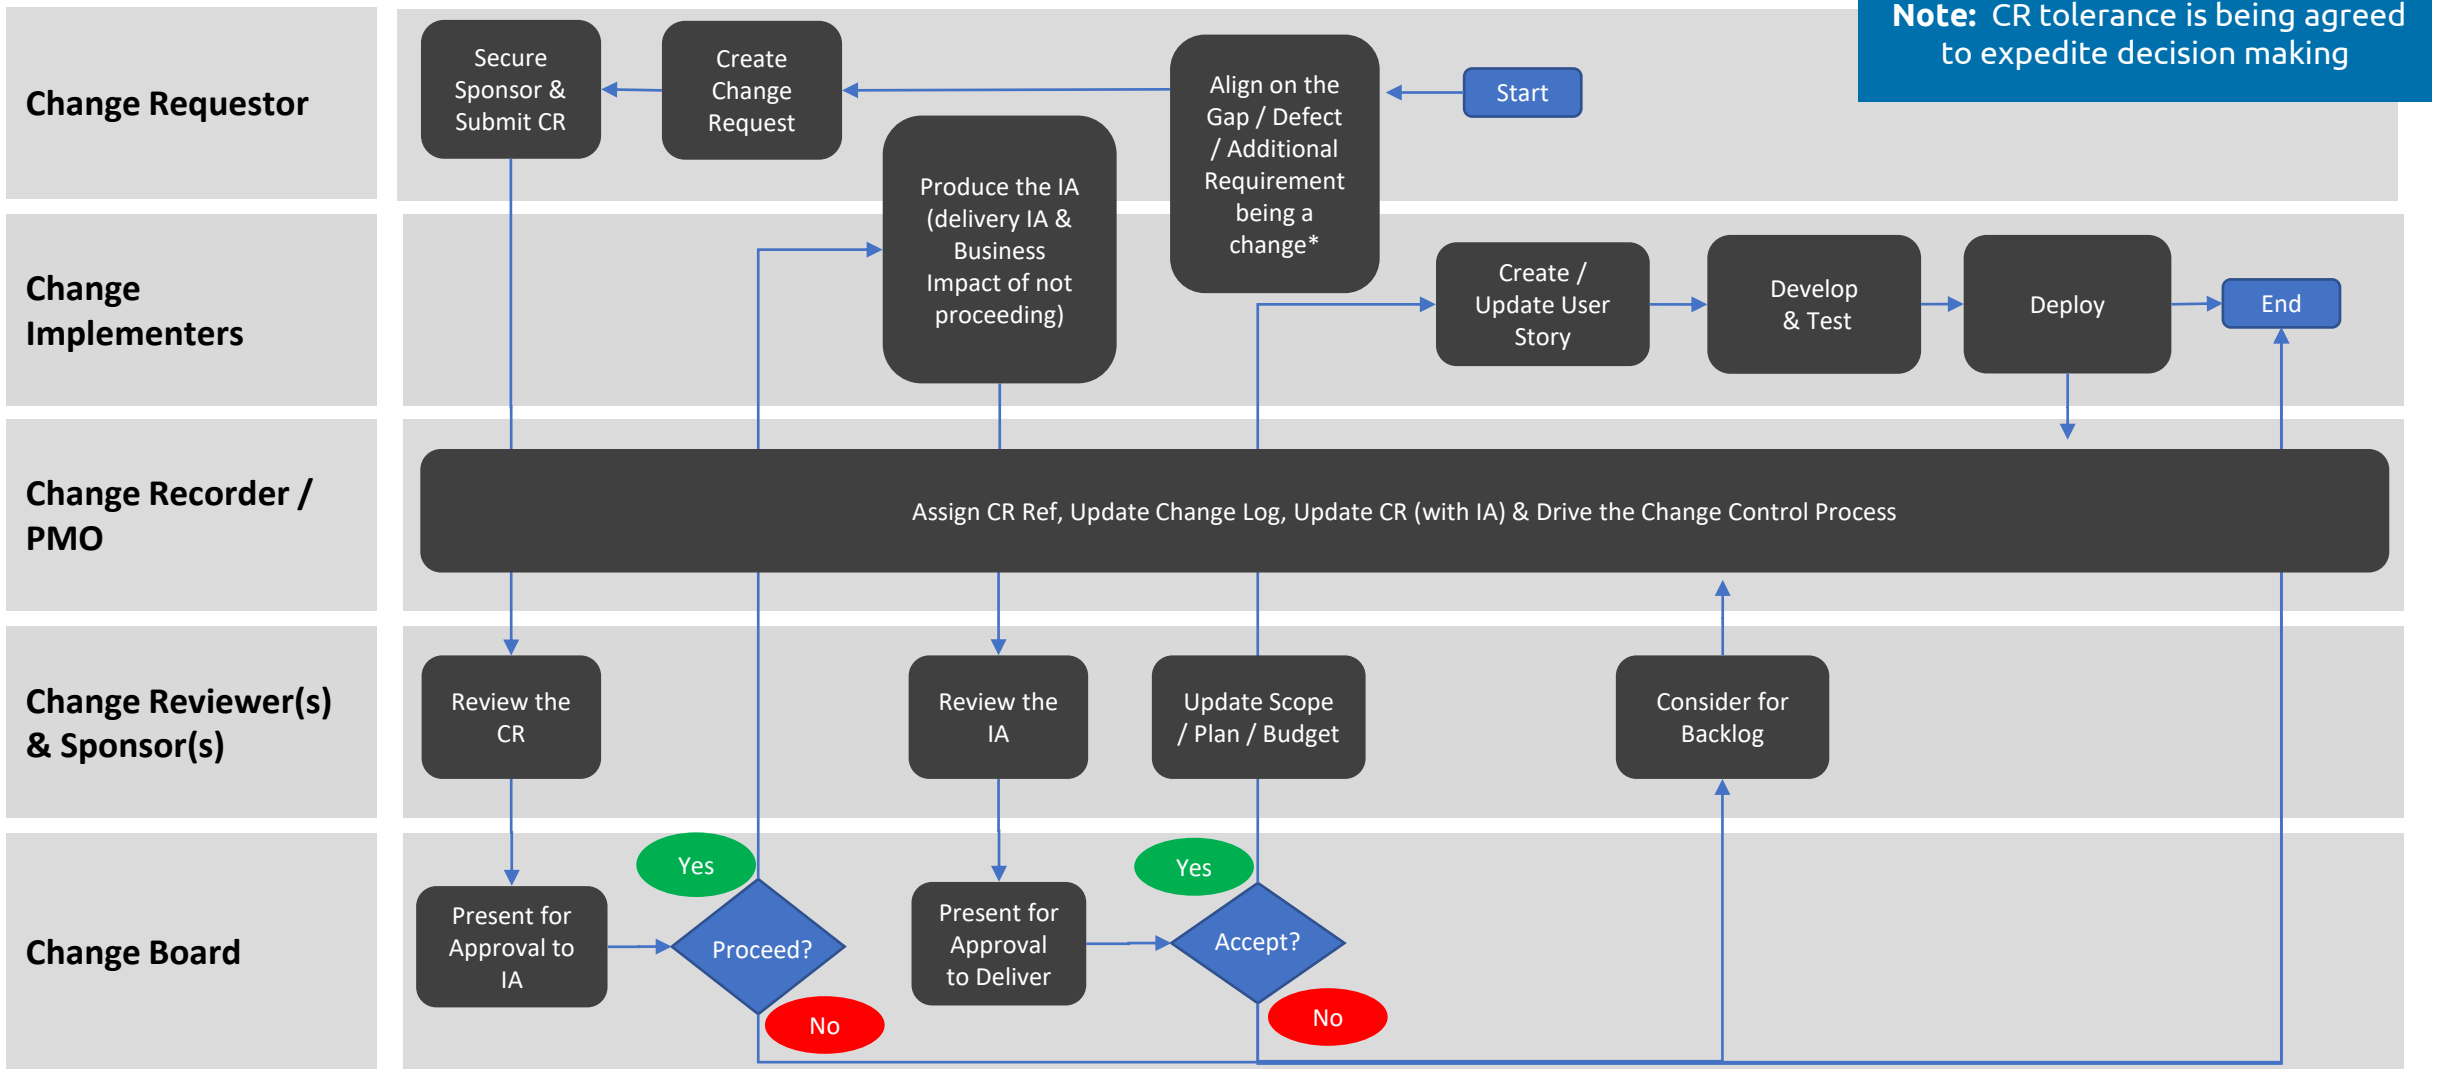

* To ensure we're aligned on a CR being a CR before it's presented as such i.e. does the functionality requested deviate from the scope of the programme and / or requirements / assumptions captured during Inception and / or signed off User Story.

Company Confidential © Capgemini 2024. All rights reserved |

RAID MANAGEMENT

We will identify, document, and review (fortnightly at least) Risks, Assumptions, Issues and Dependencies (RAID), which we will store in the overall programme RAID log on the Beazley network to ensure one version of the truth and to maintain full transparency. This will cover the following:

- **Risks** (and their mitigation actions, owners and due dates).
- **Assumptions** (and validation actions, owners and due dates).
- **Issues** (and resolution actions, owners and due dates). Note: We also strictly use the daily Scrum of Scrum (SOS) calls to log all blockers (on JIRA for visibility and to drive resolution) to give the necessary visibility across the programme in a bid to drive action.
- **Dependencies** upcoming and – if they exist – any overdue dependencies. Based on our experience, we consider strong dependency management a critical success factor, and so we will be implementing this throughout the Inception phase and beyond.

Company Confidential © Capgemini 2024. All rights reserved |

TOOLS FOR INCEPTION

Inception

Technical and Collaboration Tools

- VDIs and software installations
- Outlook, MS Teams
- Project planner
- Microsoft Office tools- word, excel, ppt
- Guidewire sandbox access
- JIRA
- Confluence
- Microsoft Visio/Biz Design/Gliffy
- Guidewire Cloud Console access

<----->

- Lewis Claxton (Beazley PMO)
- Raghava Kanduru (Capgemini PMO)


Managed by

Company Confidential © Capgemini 2024. All rights reserved |


JIRA SETUP

Process to setup projects in Jira with one scheme configuration and upload prioritized backlog during inception phase


Step1 – Create one Schema Configuration for all GPAS projects

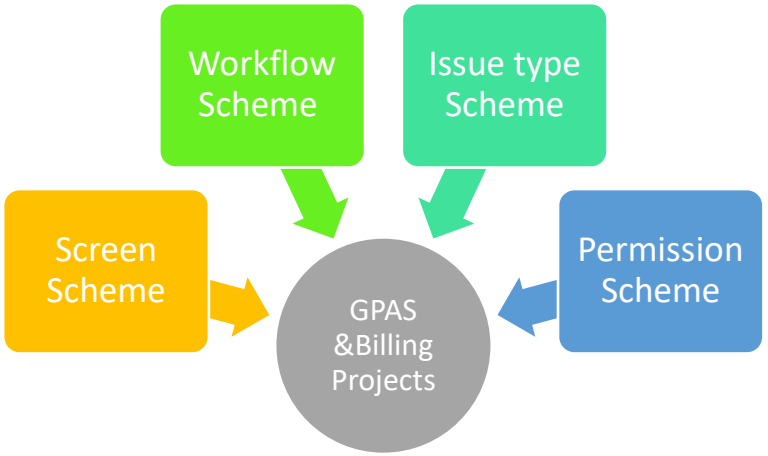

Step2 – Create Projects and set one scheme configuration

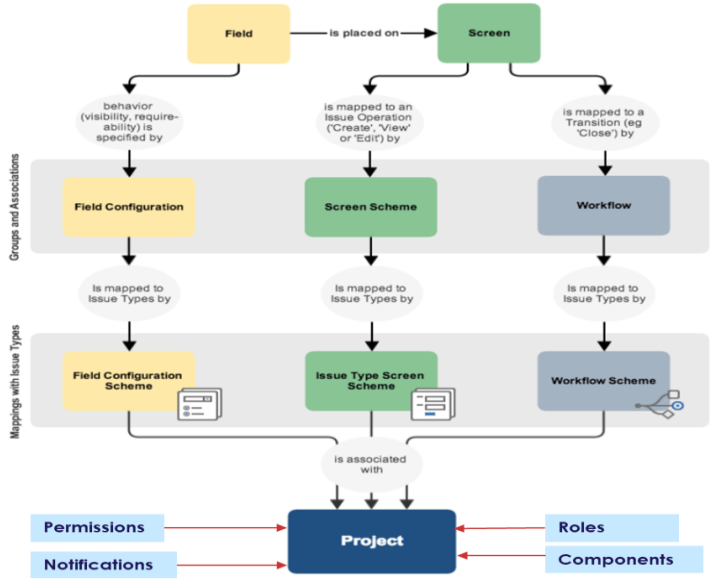

Step3 – Upload the prioritized backlog to GPAS projects

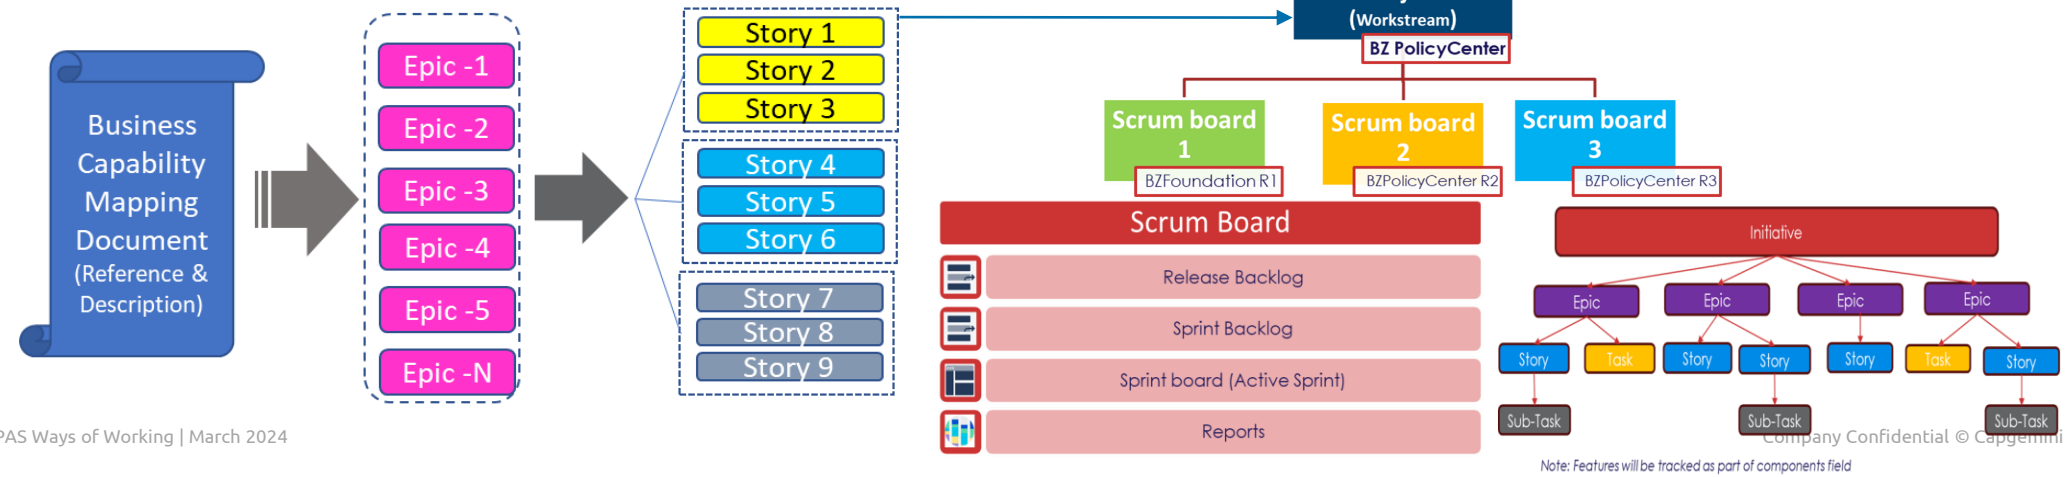

Company Confidential © Capgemini 2024. All rights reserved |

LESSONS LEARNED FROM UWWB PROJECT

General	• New/change-in scope to be channelled through Change management process • Direct access to Business SMEs by Cap Bas to clear any gaps in requirements • Misalignment between the requirements shared by the Beazley BAs vs Beazley Architect • E2E flow demos to be provided by the business that includes third party systems
Environment	• Environments to be in place before Build phase • Plan test data creation for Testing Team in advance to avoid test execution delay
JIRA Hygiene	• Adhering to DOD & DOR for moving story to next stage/status • Adhering to Sprint DOD & DOR to start the sprint in Jira • Having one workflow scheme configuration across workstreams within the programme • Updating ETA & latest status for dependent stories/task in Jira on regular basis • Adding latest comments to the issue as & when there are changes • Linked Issues to be effectively utilized esp. when dependency is identified
Logistics and Access	• Access to Beazley building & floor to work along with GPAS & Billing team • Access to GPAS & Billing team's calendar to plan meeting better

Company Confidential © Capgemini 2024. All rights reserved |



About Capgemini

Capgemini is a global leader in partnering with companies to transform and manage their business by harnessing the power of technology. The Group is guided everyday by its purpose of unleashing human energy through technology for an inclusive and sustainable future. It is a responsible and diverse organization of over 325,000 team members more than 50 countries. With its strong 55-year heritage and deep industry expertise, Capgemini is trusted by its clients to address the entire breadth of their business needs, from strategy and design to operations, fueled by the fast evolving and innovative world of cloud, data, AI, connectivity, software, digital engineering and platforms. The Group reported in 2021 global revenues of €18 billion.

Get the Future You Want | www.capgemini.com



This presentation contains information that may be privileged or confidential and is the property of the Capgemini Group.

Copyright © 2023 Capgemini. All rights reserved.
