

Beazley

Jira Ways of Working for GPAS & Billing Programme Delivery

Drafted: Apr-2024

The Jira Ways of Working depicted here is the proposed setup of all Capgemini owned work within GPAS & Billing components. This proposal will be fed into overall programme Jira ways of working.

Please read this document in conjunction with the Ways of Working document.

Please note that Jira's Way of Working document is –

- Guidance on how the Jira process is expected to run
- Teams are encouraged to suggest improvements


Company Confidential © Capgemini 2024. All rights reserved |

Table of Content

1. Jira Setup Overview
2. Jira Setup – Naming Convention
3. Jira Setup – One Scheme configuration
4. Jira Structure of a project
5. Jira Xray traceability view
6. Jira Workflow (Story, In sprint Defect, Stabilisation)
7. Linked issues
8. Tracking of Sprint Start & Closure
9. Jira Dashboards & Reports
10. Appendix
    - Sprint Preparation
    - Project Configuration
    - Jira Issue Creation

Jira Setup - Overview

Project Name: Beazley GPAS & Billing Programme

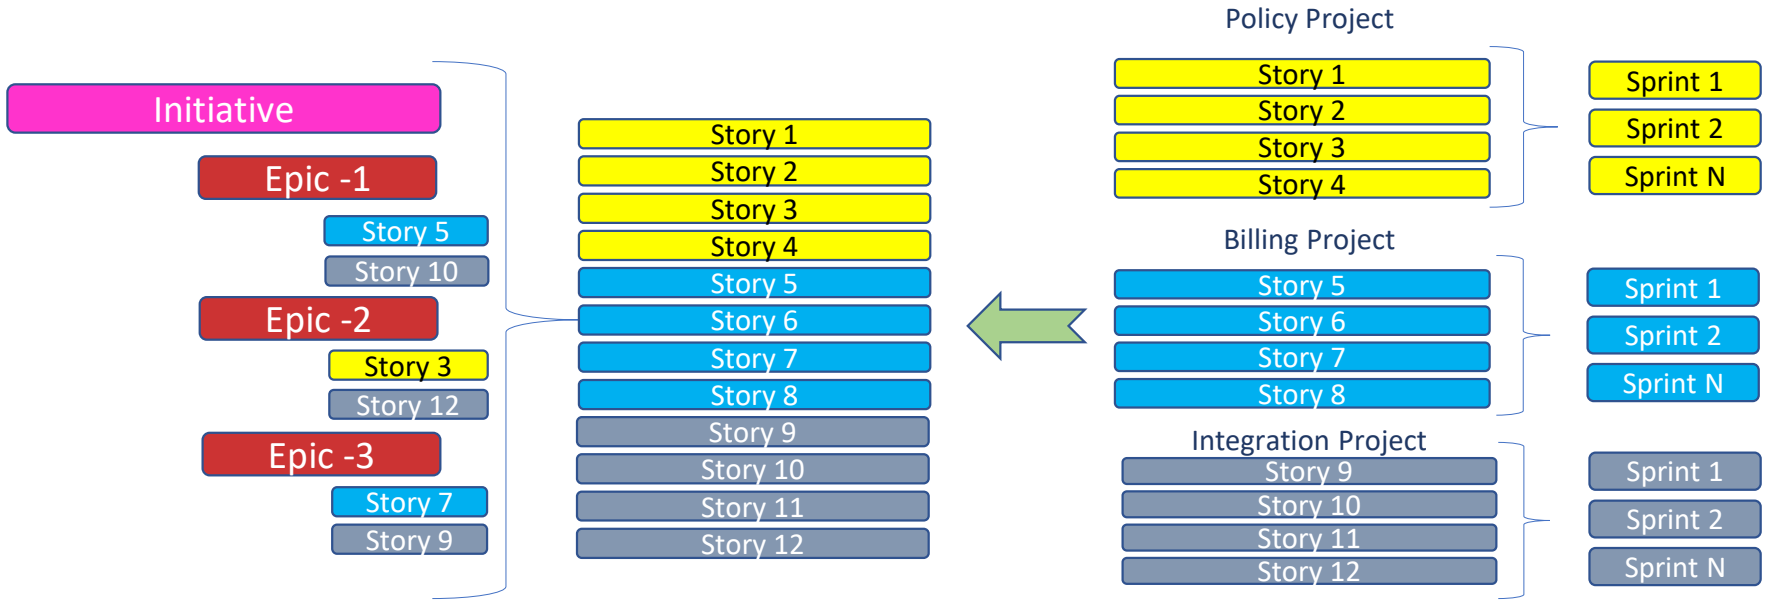

**Features will be tracked as part of components field*

Company Confidential © Capgemini 2024. All rights reserved |


Jira Setup – Naming Convention

Projects	Issue Key	Board
GPAS & BC Scrum of Scrums	BZSOS	Kanban
BZ PolicyCenter	BZPC	Scrum
BZ BillingCenter	BZBC	Scrum
BZ Integration	BZINT	Scrum
BZ System Integration Testing	BZSIT	Scrum
BZ User Acceptance Testing	BZUAT	Scrum
BZ Production	BZP	Scrum

Projects are not yet created in Jira

Company Confidential © Capgemini 2024. All rights reserved |

Jira Setup – One scheme configuration

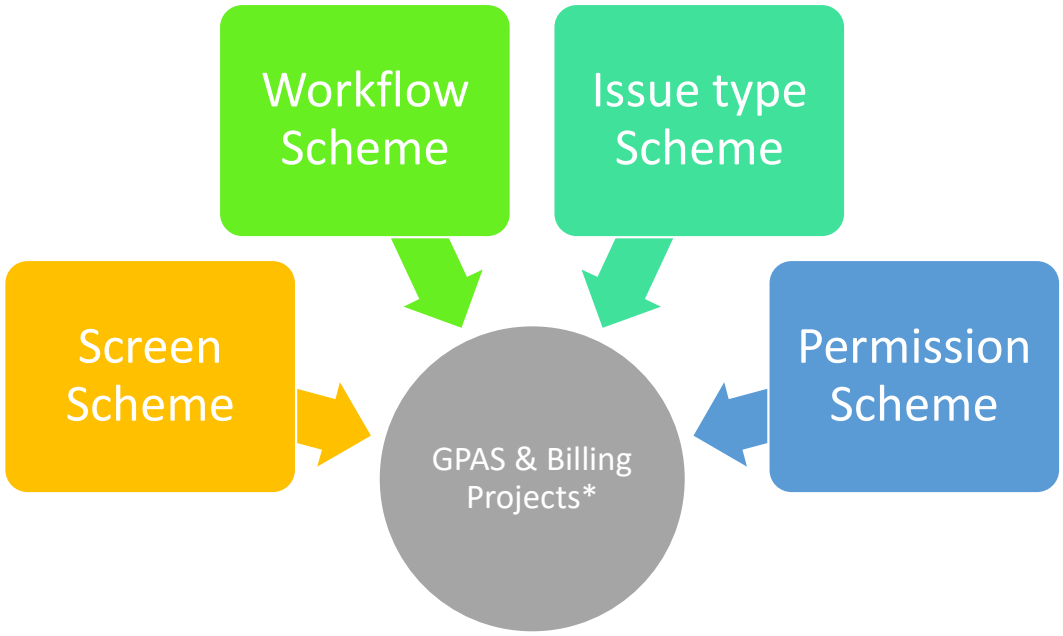

**Policy, Billing, Integration Projects*

Screen scheme – Where fields will be added to the screens (create, edit & view) and configured to the issue types


Workflow Scheme – Workflow will be created and configured to the issue types


Issuetype scheme – Defines which issue types are applicable for the project and configured to the project


Permissions scheme – Define what permission can be granted to user, roles or group in a project


Company Confidential © Capgemini 2024. All rights reserved |

Jira Structure of a project

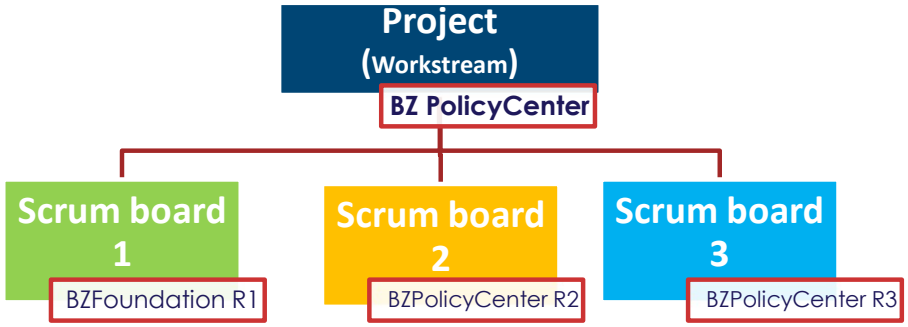

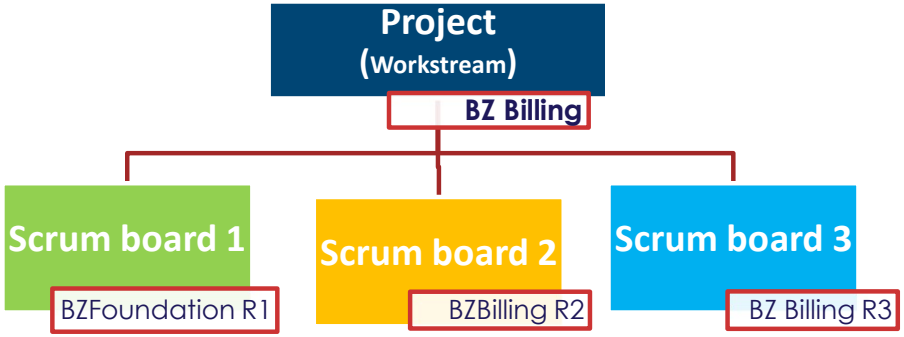

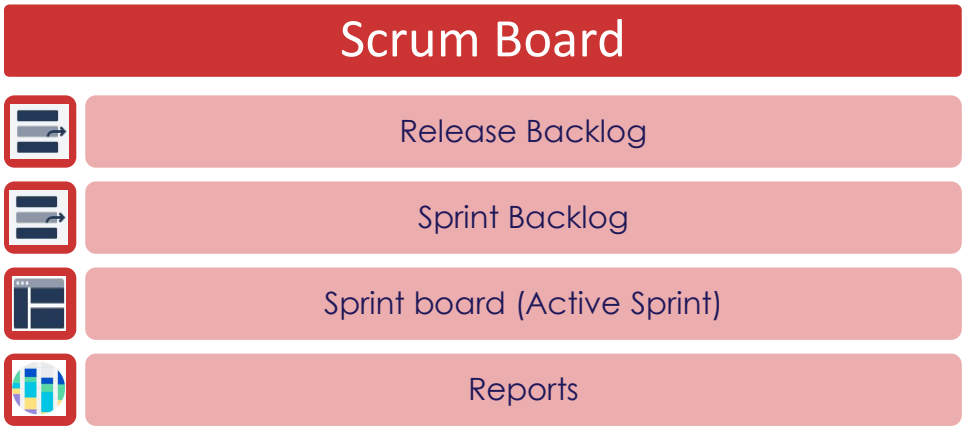


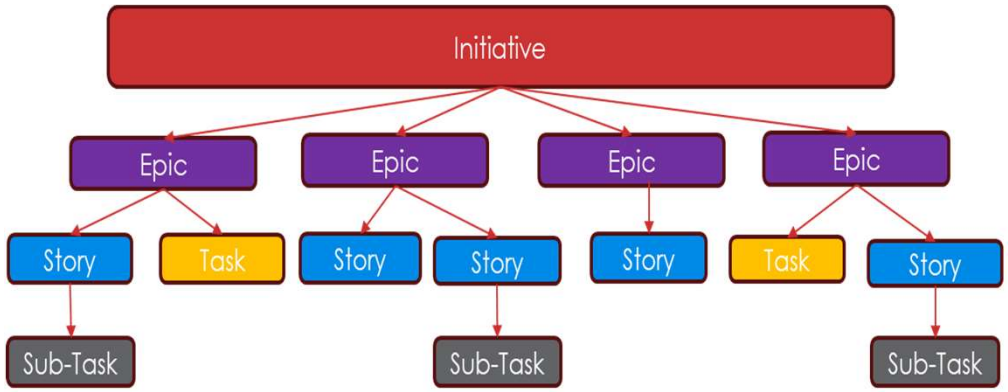


Note: Features will be tracked as part of components field

Company Confidential © Capgemini 2024. All rights reserved |

Jira Xray Traceability view

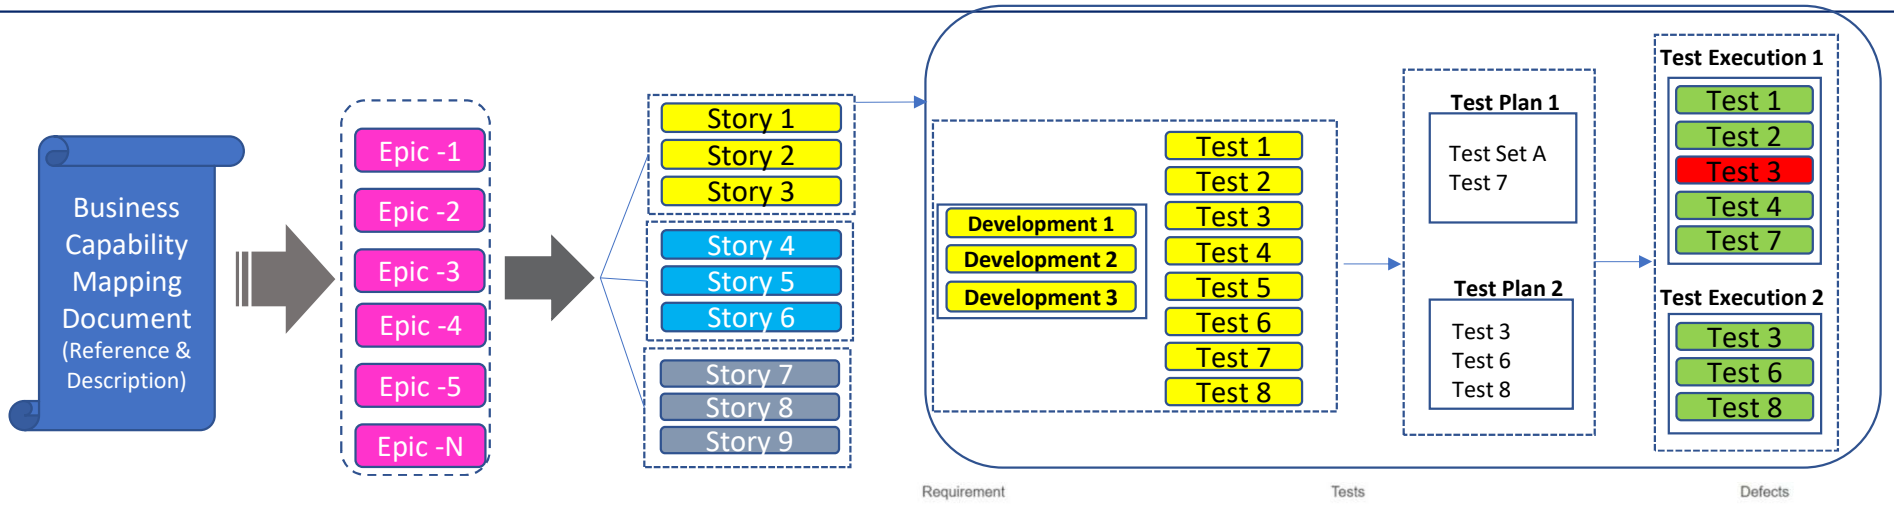

Jira Xray traceability report provides complete view of requirement status from Epic to Defects hierarchy

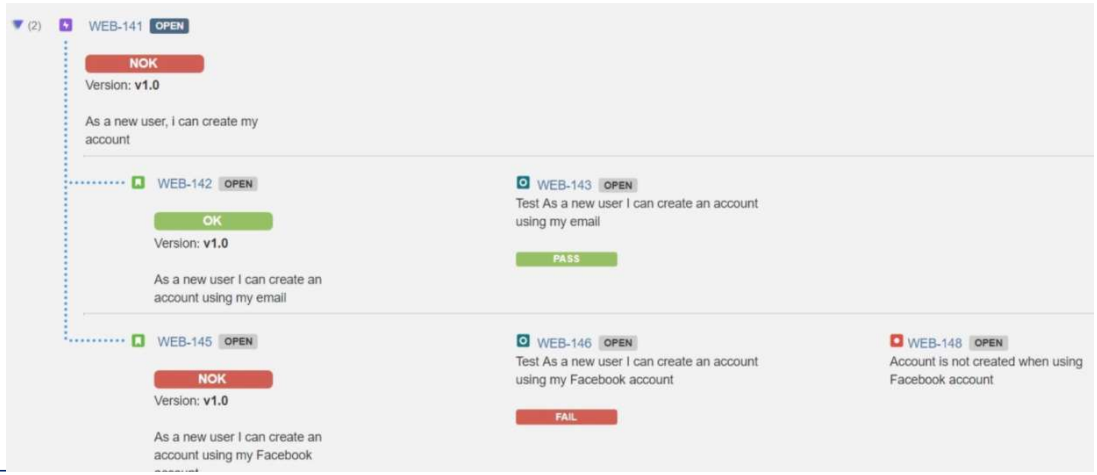

Company Confidential © Capgemini 2024. All rights reserved |

Jira Setup – Epic & Story Key Fields (User Story)


Epic
Project
Issue Type
Epic Name
Summary
Description
Priority
Reporter
LinkedIssues
Attachments
Labels

User Story	
Project	BCM Reference
Issue Type	BCM Description
Status	Fixversion
Summary	Dev Due Date
Description	Due Date
Acceptance Criteria *(Allows Rich Text)*	Components *(Feature tagging)*
BA Owner	Attachments
Assignee	Labels
Reporter	LinkedIssues
Sprint	
Story Points	
Time tracking (OE, RE, TimeSpent)	
Team	
Platform	
Parent	
Priority	

Note: Highlighted fields are new custom fields to created (Service request ID – RITM1135026)


Company Confidential © Capgemini 2024. All rights reserved |

Jira Initiative & Epic workflow

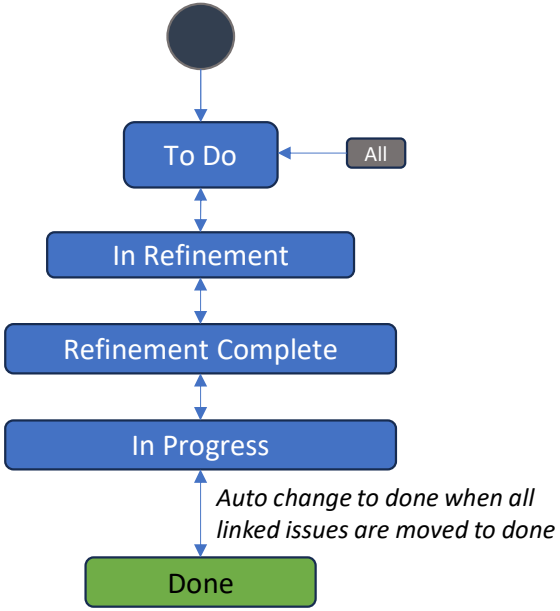

Company Confidential © Capgemini 2024. All rights reserved |


Jira User Story workflow

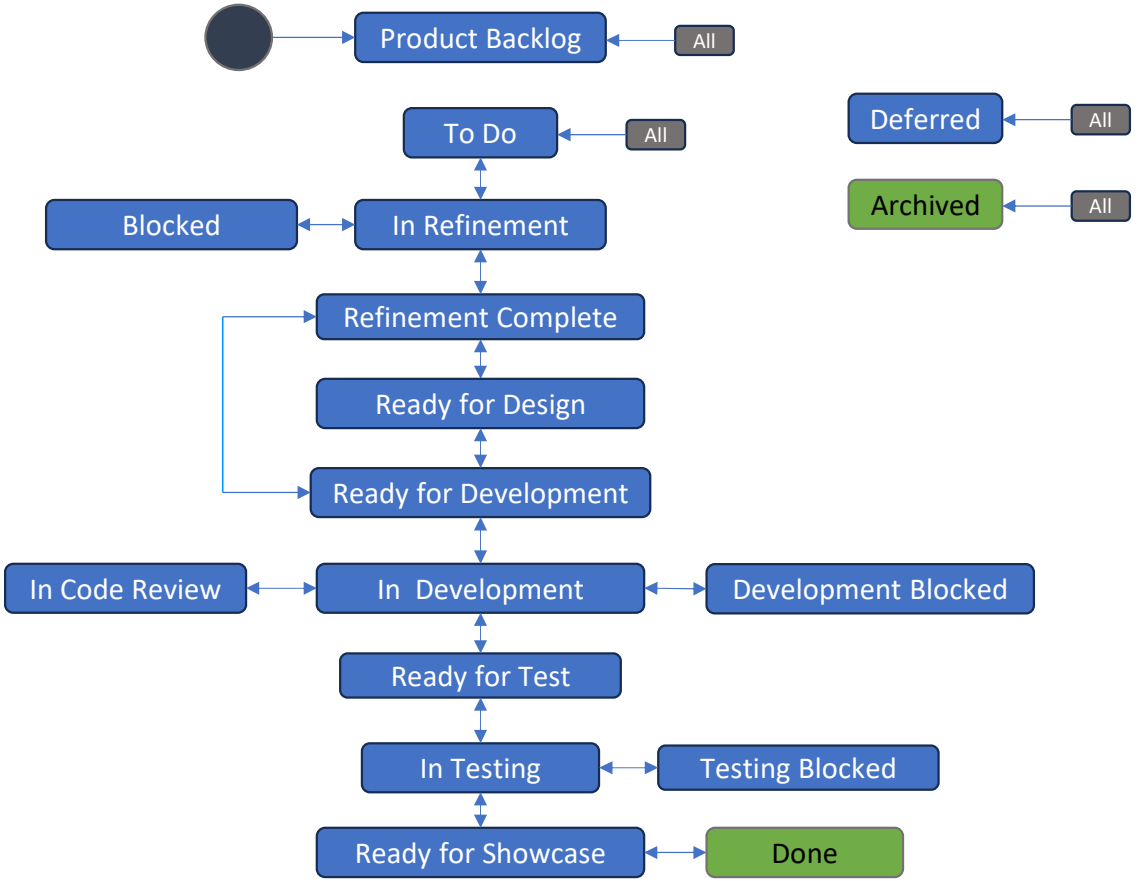

Service Ticket ID: RITM1137241


Company Confidential © Capgemini 2024. All rights reserved |

Jira Insprint Defect Workflows

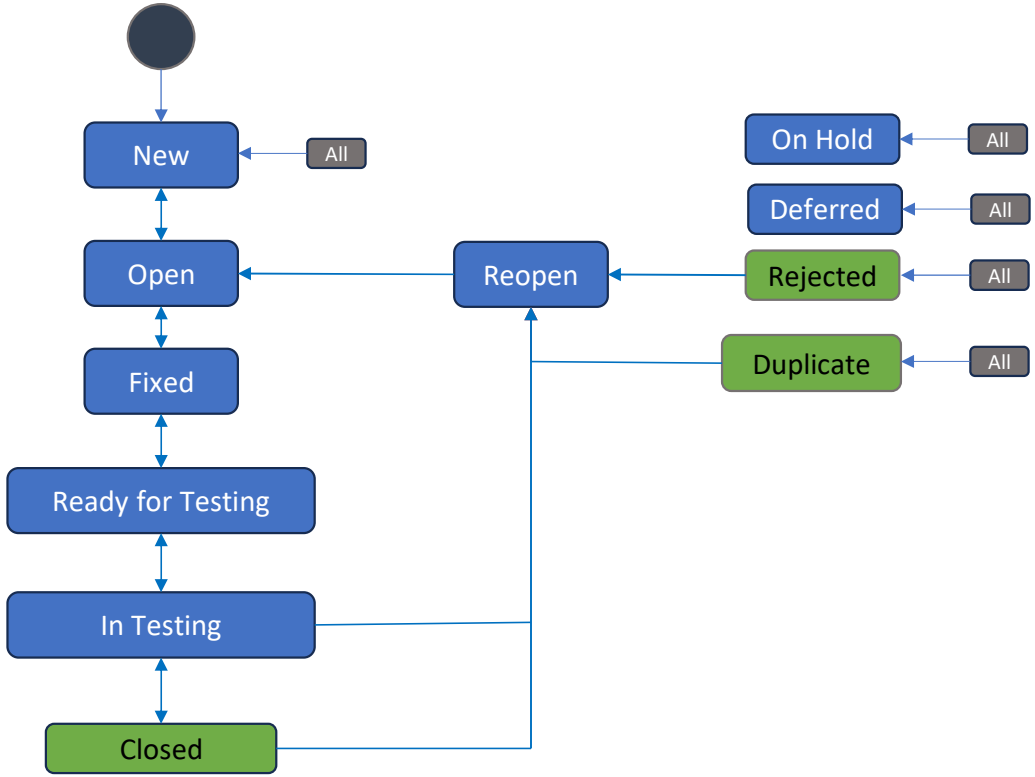


Company Confidential © Capgemini 2024. All rights reserved |

Jira Stabilization workflow -- Draft

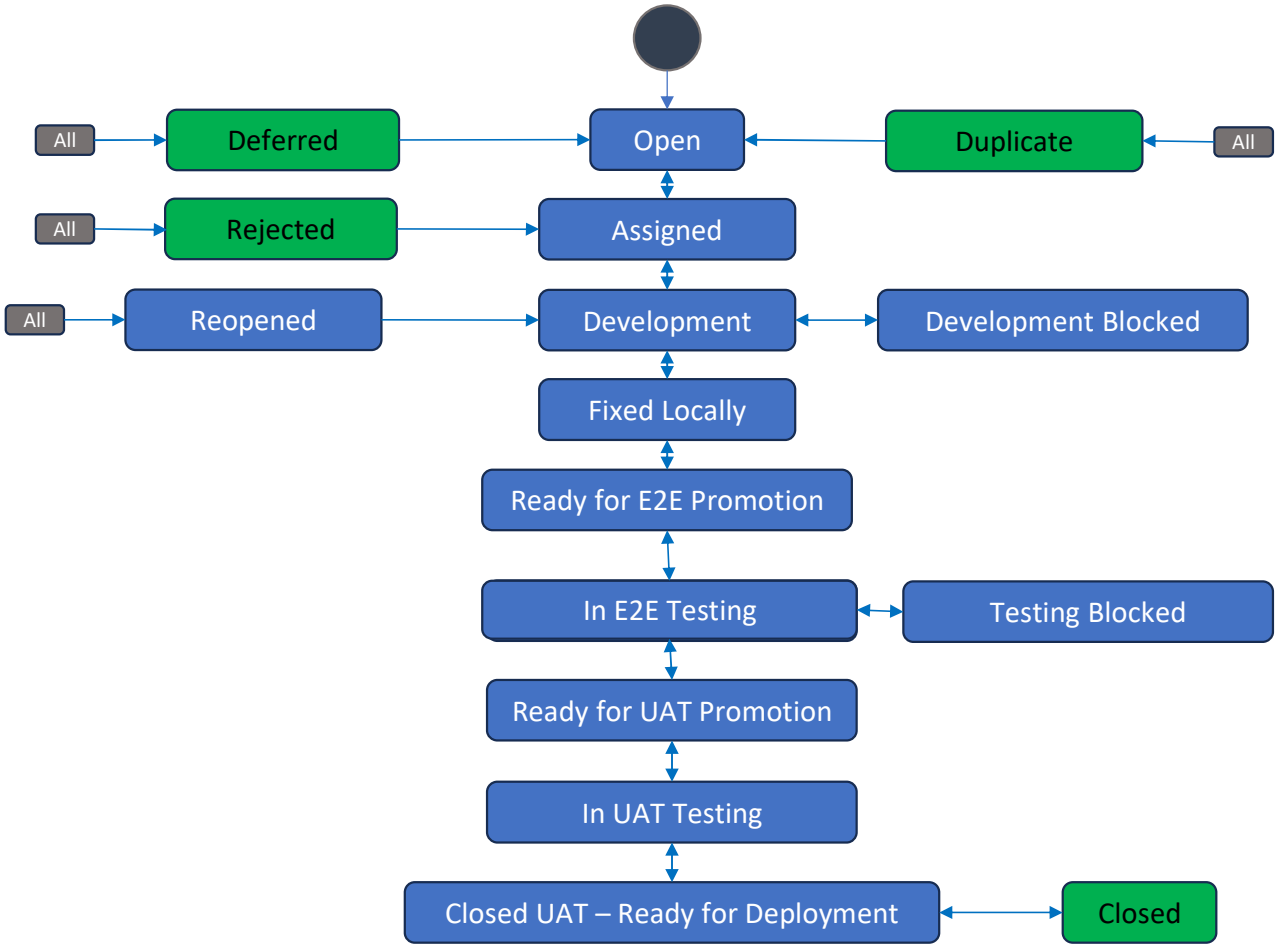

Company Confidential © Capgemini 2024. All rights reserved |

Jira SOS Project – Task workflow

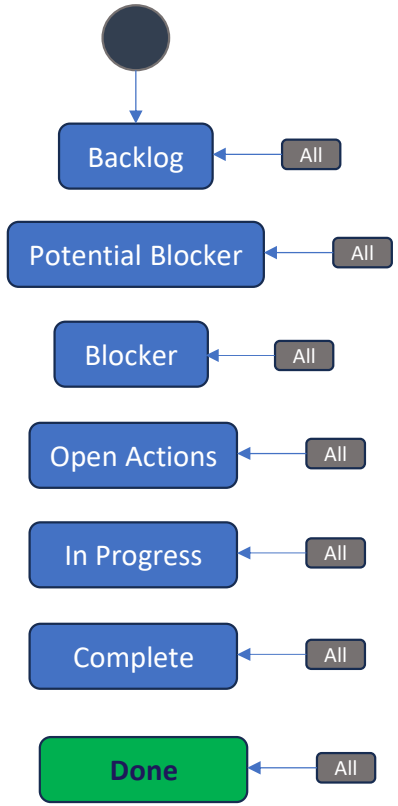


Service Ticket ID: RITM1137214

Company Confidential © Capgemini 2024. All rights reserved |

How Dependencies are handled


Linked Issues field signifies the relation of stories with

- Tests (tested by)
- Blockers (blocks/is blocked by)
- Dependent (Depends on)



Few other options available in Beazley Jira instance are -

- has to be done before
- has to be done after
- Must be delivered in parallel
- relates to



Dependent issue will be created for the stories that doesn't exist in Jira and then link it to the story.

Company Confidential © Capgemini 2024. All rights reserved |

Tracking of Sprint Start & Closure

Company Confidential © Capgemini 2024. All rights reserved |

Sprint DOR & DOD

Sprint DOR & DOD checklist will be added to the confluence for each sprint and WS Leads must update the checklist before start & end of the Sprint. This will be reviewed by both the parties and then take a collective decision to start/close the sprint in Jira.

Sprint - Definition of Ready					
Activities/Projects		**GPAS**	**Billing**	**Integration**	**Comments**
Sprint Backlog handoff complete	Techincal & Functional clarification With PO is complete				
	User Stories are in compliance with Definition of Ready				
Sprint backlog created based on sprint capacity	Dev & QA efforts considered & updated				
Reporting & Document templates are ready & available for Integration stories					
Signed off HLA made available by the architecture team whereever applicable					
All dependencies have been resolved. Dependency items are agreed for all third party (Internal & External)					
Environment configuration completed, and access setup done for Project members					

Company Confidential © Capgemini 2024. All rights reserved |

Sprint - Definition of Done				
Activities/Projects	**GPAS**	**Billing**	**Integration**	**Comments**
All user stories and subtasks with a userstory are in Done status				
Completed user stories are in compliance with the US Definition of Done or exception is agreed with Beazley				
Stories not in 'Done' status have be moved to Deferred status, with associate open defects				
Test Execution is complete in Jira with no test cases in 'To Do' status or if any exception is agreed with Beazley				
High Priority or Severity defects have been either closed or there is a mutually agreed fix plan with Beazley for the open defects				
Code has been checked-in accordance with DevOps pipeline				
Sprint completion reports has been shared with Beazley stakeholders - PO, Programme management team				
Automation testing (if applicable) has a coverage to the requirement level as defined in the test strategy (ex. API Testing for Integrations begun in later Sprints)				

Company Confidential © Capgemini 2024. All rights reserved |


Jira Dashboards for reporting

Dashboard Category	Dashboard Views
Workstream Backlog	Workstream backlog, Release backlog, Sprint(s) Backlog, Issues not tagged to Release or Sprint Backlog
Individual Sprint	Days Remaining, Sprint Progress, Story points planned, Stories vs status stats, Blocked stories view, Defect stats (different views) & burndown chart
Cross Release Workstream	Days Remaining, Story Points planned, Story points completed, Overall stories (workstreams) vs Status view, Blocked stories view, Defects (Work steams vs status) view, Outstanding issues (confluence page view)
Testing	Overall test (workstream vs test run) view, Defects vs status view, Defect priority vs status, Defect severity vs status.

Company Confidential © Capgemini 2024. All rights reserved |

Jira Scrum of Scrums Dashboard (Sample)

Pie Chart: Overall SOS Issues status

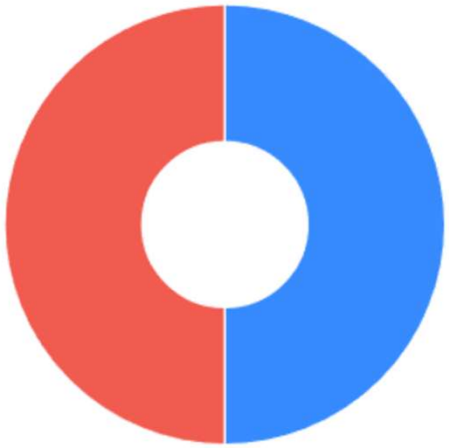

Status
Total Issues: **2**

Done	1
To Do	1

Two Dimensional Filter Statistics: Active SOS issue status

Assignee	TO DO	T:
Raghava Kanduru	1	1
Total Unique Issues:	1	1

Grouped by: Status

Showing **1** of **1** statistics.

3 minutes ago

Filter Results: Active SOS issue status

Key	Summary	P	Status	Assignee
BZSOS-2	Dummy SOS Blocker 1	=	TO DO	Raghava Kanduru


1–1 of 1


3 minutes ago

Company Confidential © Capgemini 2024. All rights reserved |

Jira Dashboard (Sample)

Dashboard are a way to present a customized view of projects. They can be created for individual use or to share with others on the team. Dashboard are made up of one or more gadgets. A gadget displays some aspect of the work of the projects.

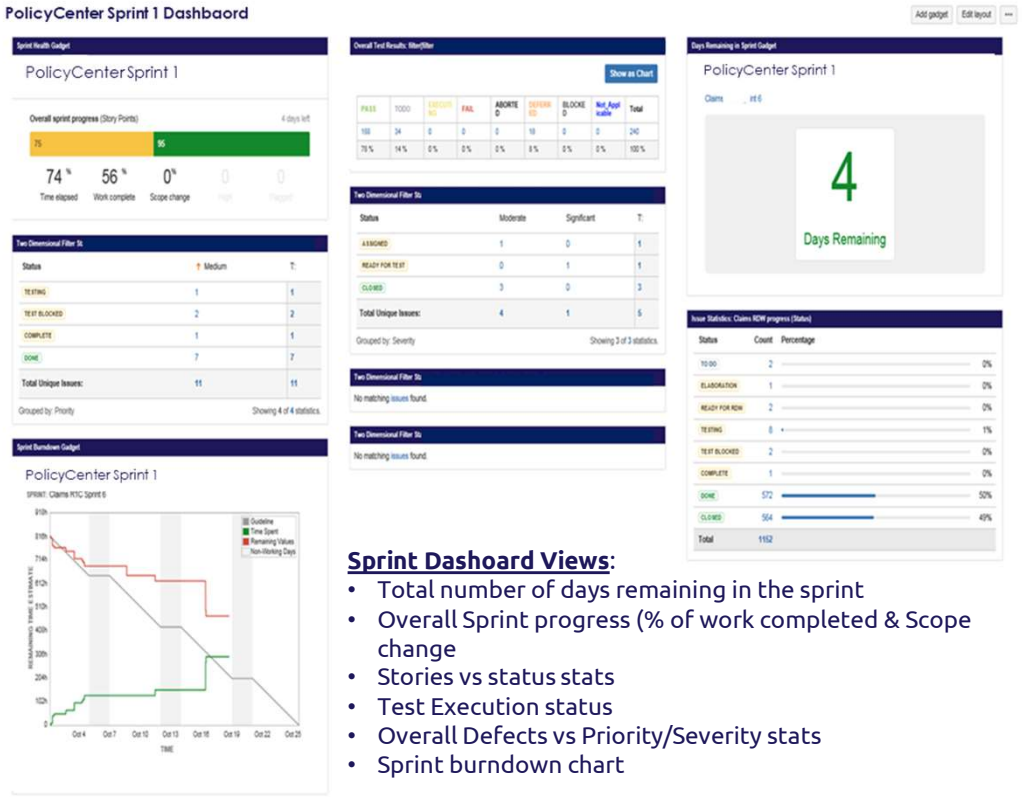

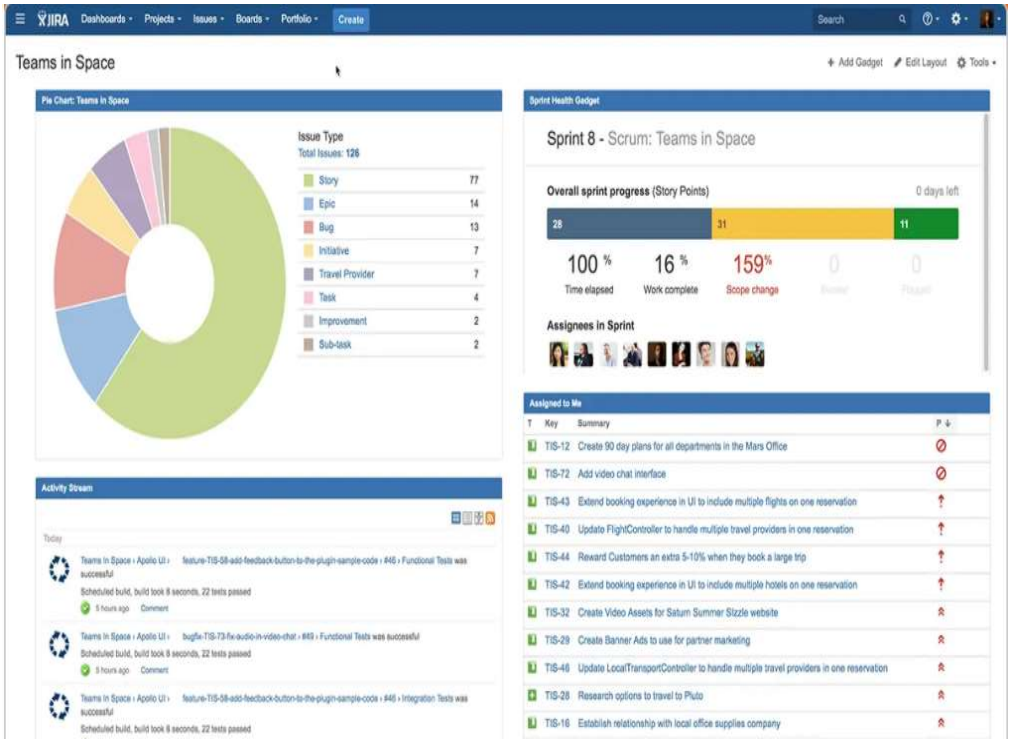

Sprint Dashoard Views:

- Total number of days remaining in the sprint
- Overall Sprint progress (% of work completed & Scope change
- Stories vs status stats
- Test Execution status
- Overall Defects vs Priority/Severity stats
- Sprint burndown chart

Company Confidential © Capgemini 2024. All rights reserved |

Jira Reporting

The following default charts/reports are available in Jira to track the progress. Sample view of chart and reports are shown in next slides

Category	Description	Frequency
Sprint Report	Shows the work completed or pushed back to the backlog in each sprint	End of each Sprint
Velocity Chart	Tracks the amount of work completed from sprint to sprint	End of each Sprint
Burndown Chart	Tracks the total work remaining, and projects the likelihood of achieving the sprint goal	Daily (during active sprint)
Epic Burndown	Tracks the projected number of sprints required to complete the epic.	End of each Sprint
Release Burndown	Tracks the projected release date for a version. This helps you monitor whether the version will release on time, so you can act if work is falling behind	End of each Sprint
Epic Report	Shows the progress towards completing an epic over time	End of each Sprint (or as needed)

Sprint Report, Velocity chart & burndown chart are most commonly used


Company Confidential © Capgemini 2024. All rights reserved |

Burndown & Velocity Report (Sample)

A burndown chart show the progress that the makes during a sprint. Chart can be plotted either Story points or Remaining Time estimate (in hrs)




Velocity chart shows the estimated and actual velocity of the team over time

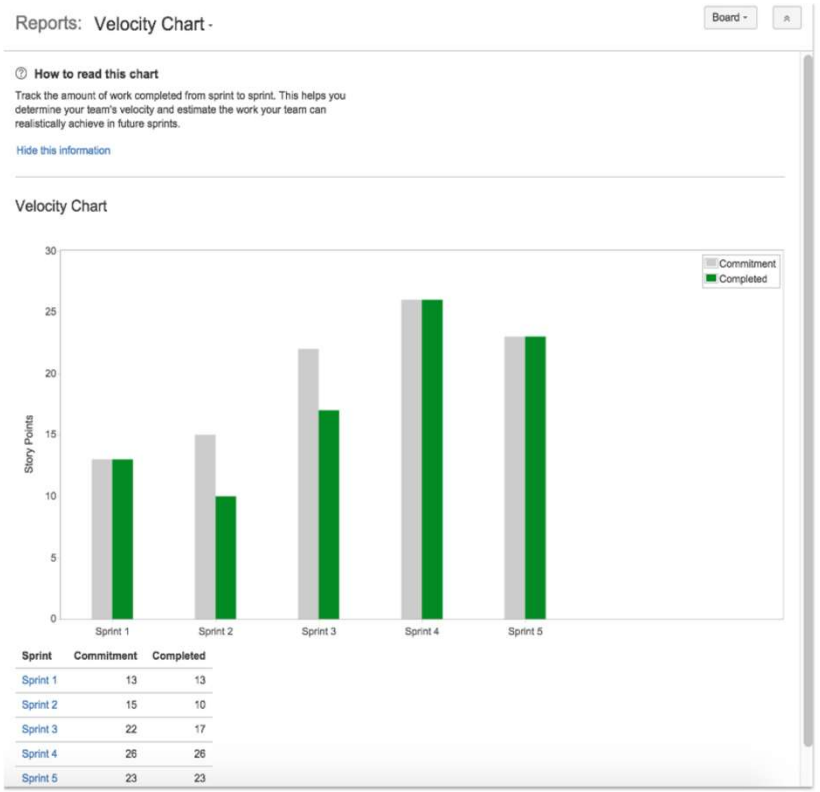

Sprint	Commitment	Completed
Sprint 1	13	13
Sprint 2	15	10
Sprint 3	22	17
Sprint 4	26	26
Sprint 5	23	23

Company Confidential © Capgemini 2024. All rights reserved |

Sprint Report (Sample)

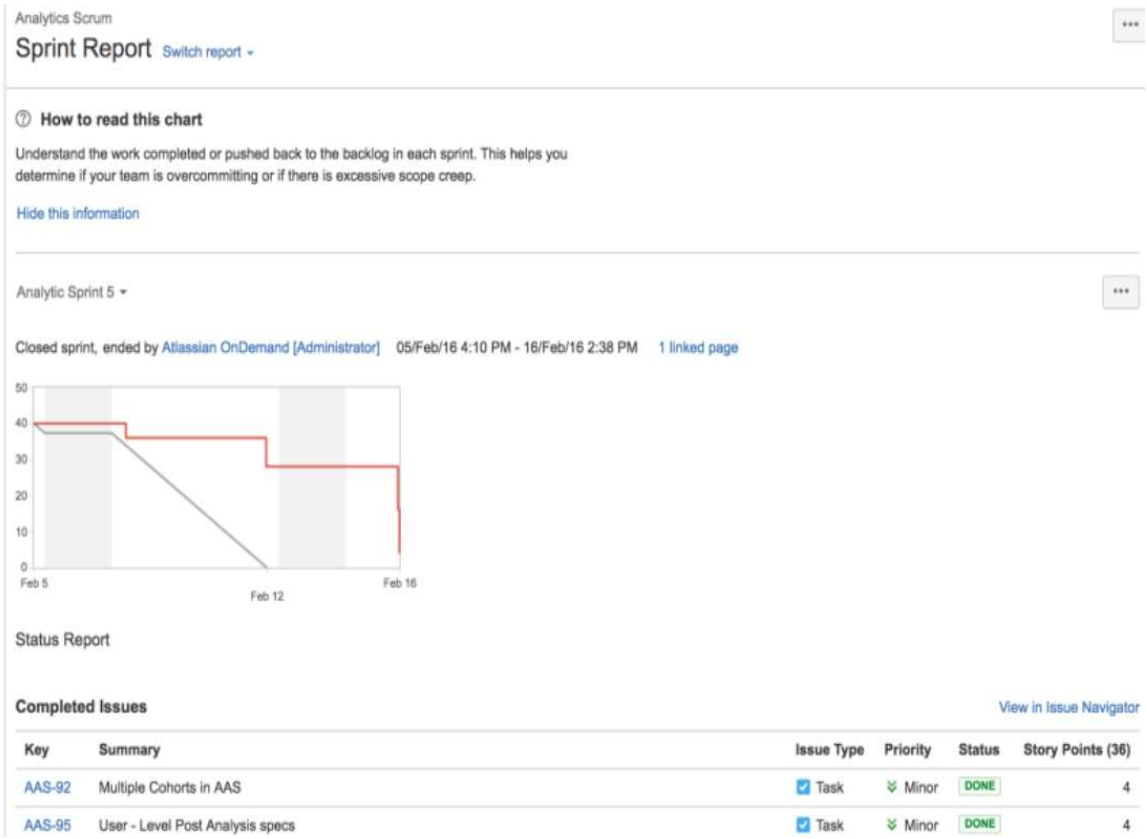

- The Sprint Report is board-specific – that is, it will only include issues that match your board's saved filter.

- Issues added after the sprint starts are indicated with an asterisk.


- An issue is considered to be 'To Do' when it is in a status that has been mapped to the left-most column of your board. Similarly, an issue is considered to be 'Done' when it is in a status that has been mapped to the right-most column of your board.

- The grey line is a guideline that's drawn from the total estimate of the issues at the start of the sprint, to 0 at the end of the sprint. The grey line stays flat during non-working days.

- The red line represents actual work done during the sprint — it's drawn from the total estimate of the issues at the start of the sprint, and it goes higher or lower as your team works on the issues in the sprint.

Company Confidential © Capgemini 2024. All rights reserved |

Epic Report (Sample)

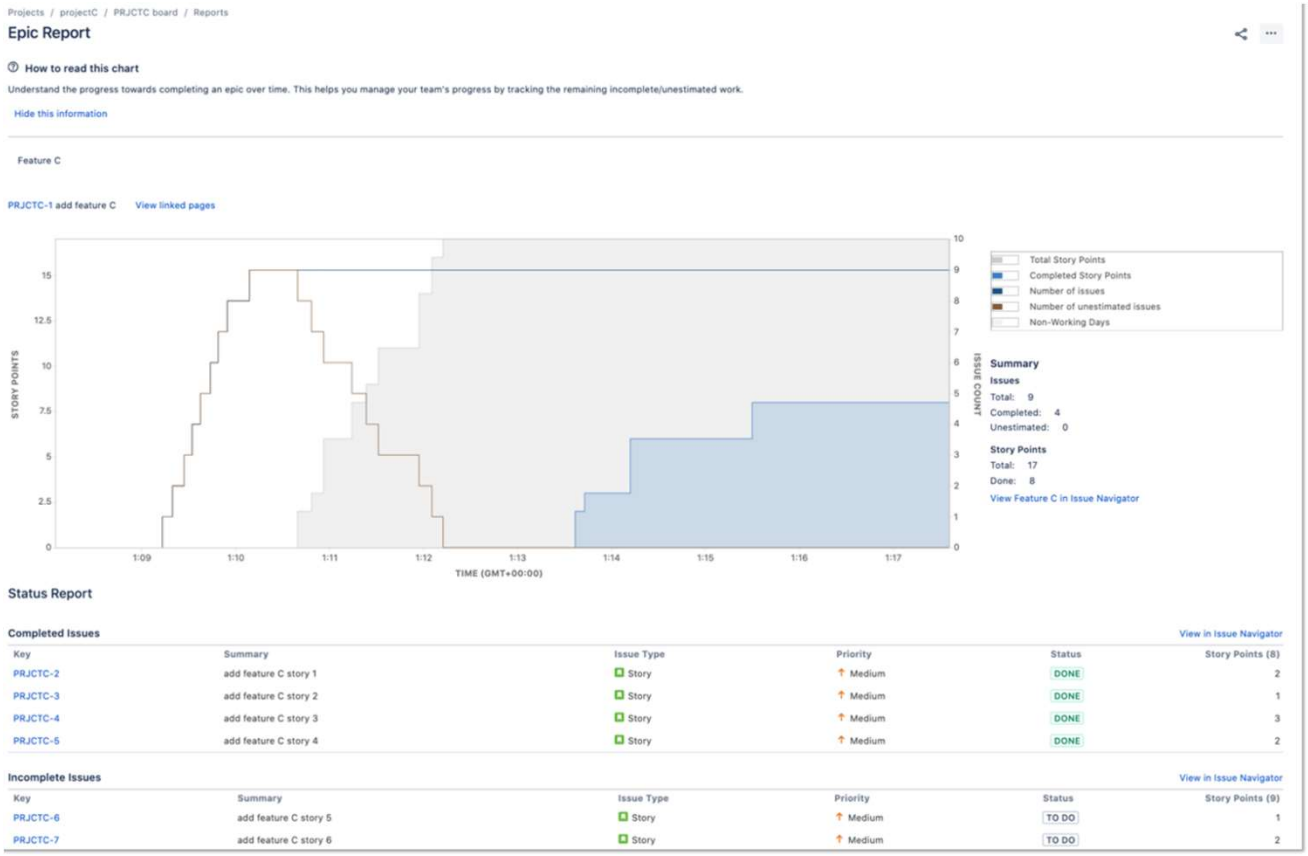

Projects / projectC / PRJCTC board / Reports

Epic Report

How to read this chart

Understand the progress towards completing an epic over time. This helps you manage your team's progress by tracking the remaining incomplete/unestimated work.

Hide this information

Feature C

PRJCTC-1 add feature C View linked pages

Summary

Issues
Total: 9
Completed: 4
Unestimated: 0

Story Points
Total: 17
Done: 8

View Feature C in Issue Navigator

Status Report

Completed Issues — View in Issue Navigator

Key	Summary	Issue Type	Priority	Status	Story Points (8)
PRJCTC-2	add feature C story 1	Story	Medium	DONE	2
PRJCTC-3	add feature C story 2	Story	Medium	DONE	1
PRJCTC-4	add feature C story 3	Story	Medium	DONE	3
PRJCTC-5	add feature C story 4	Story	Medium	DONE	2

Incomplete Issues — View in Issue Navigator


Key	Summary	Issue Type	Priority	Status	Story Points (9)
PRJCTC-6	add feature C story 5	Story	Medium	TO DO	1
PRJCTC-7	add feature C story 6	Story	Medium	TO DO	2

This shows the current status of the epic, as well as a list of the issues in the epic. This helps to determine approximately when the epic will be complete.

Company Confidential © Capgemini 2024. All rights reserved |

Epic & Release Burndown (Sample)



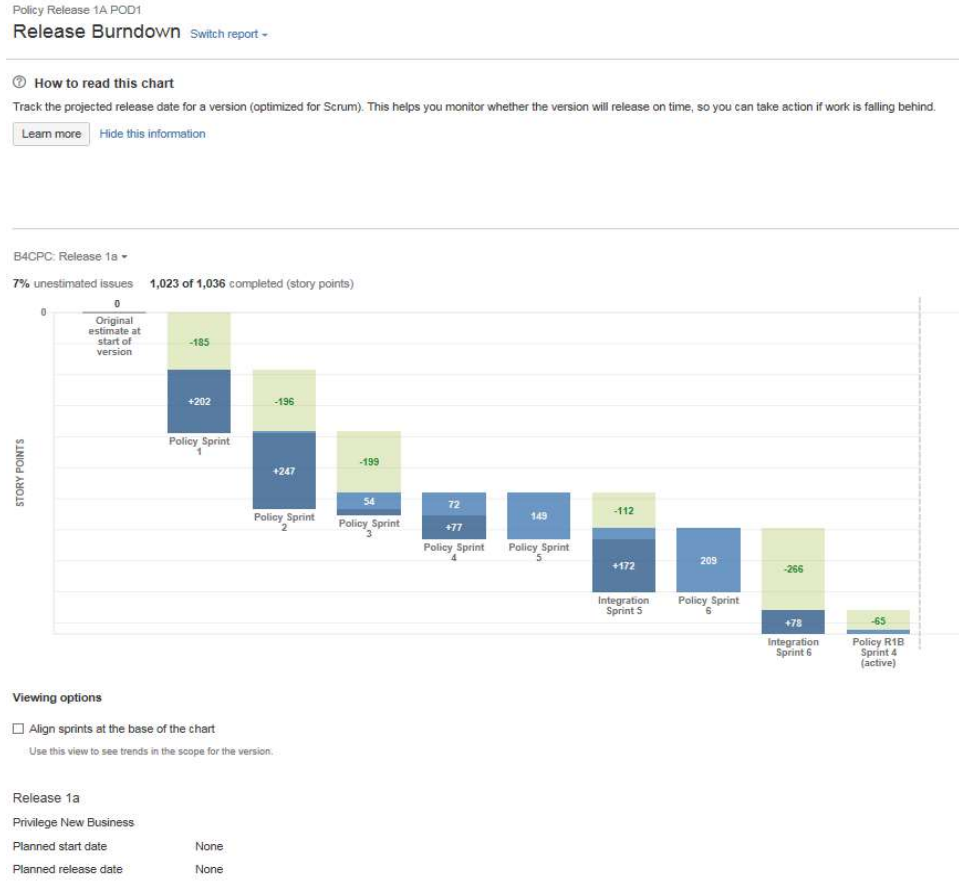

Company Confidential © Capgemini 2024. All rights reserved |

Sprint Closure pack *(Proposed)*

The Sprint Closure pack will be created & presented to Beazley at end of each sprint. The following areas will be covered as part of the pack –

- *Baseline vs Planned vs Delivered Story Points*
- *Sprint closure stats & Deferred stories data*
- *Overall active defects*
- *Release burndown*
- *DOD, DOR & Retrospective links*

Company Confidential © Capgemini 2024. All rights reserved |

Thank you!



People matter, results count.

This message contains information that may be privileged or confidential and is the property of the Capgemini Group.

Copyright© 2019 Capgemini. All rights reserved.

About Capgemini

A global leader in consulting, technology services and digital transformation, Capgemini is at the forefront of innovation to address the entire breadth of clients' opportunities in the evolving world of cloud, digital and platforms. Building on its strong 50-year heritage and deep industry-specific expertise, Capgemini enables organizations to realize their business ambitions through an array of services from strategy to operations. Capgemini is driven by the conviction that the business value of technology comes from and through people. It is a multicultural company of over 200,000 team members in more than 40 countries. The Group reported 2018 global revenues of EUR 13.2 billion.

Learn more about us at

www.capgemini.com
