GPAS & Billing
Ways of working

Extract for Guidewire consumption

Inception - Slide 2 to 4 agreed and approved with Beazley
Build - DRAFT version from Slide 5 onwards still under internal review

GPAS & Billing PROGRAM Release Trains

PROGRAM MANAGEMENT	• Responsible for Overall Program Governance that includes Planning, Monitoring execution to Budget, Mitigate Risks & Issues.
BILLING (Guidewire)	• Responsible to implement the new Billing system in Guidewire to handle Billing cycle of all new Policies to be initiated under the new Policy system
POLICY (Guidewire)	• Responsible to implement the new Policy system in Guidewire across all Beazley Product variations & Lines of Business in Scope
INTEGRATION	• Responsible to implement the in-scope integration elements necessary to ensure Guidewire operates as per business requirements.
PRODUCT RATIONALISATION	• Responsible to Rationalise product set for Foundation release and agree a framework for rationalising the remaining GPAS Products.
MIGRATION	• Responsible to Migrate all Legacy Policy data at renewal into the new Guidewire system.
TESTING	• Responsible to make sure we are deploying code to production that meets Business requirements & Program and Product quality standards
DATA	• Responsible to Build Data analytics on top of GPAS & Billing data meeting Business needs.
DOCS TOOLING	• Responsible to implement all necessary communications to support Beazley's business requirements.
TRAINING & BUSINESS READINESS	• Responsible to Design and Roll out the new system to Business users, handle training, comms, stakeholder Mgmnt., risks and issue mitigation.
BUSINESS DESIGN	• Responsible to create a centre of excellence for Beazley E2E process and journey design, ensuring consistency and quality.
ARCHITECTURE	• Responsible to create a System Architecture for the Program that is Robust, Industry standard, Scalable and meets Beazley's requirements
ENVIRONMENTS & INFRASTRUCTURE	• Responsible to provision all Infrastructure & Environments for a smooth Program execution e.g. Citrix machines, Scalable Dev, Test and Prod environments, DevOps support for continuous deployments & testing.
FINANCE	• Responsible to validate & sign-off Finance systems to the new GPAS & Billing implementation
LEGACY	• Responsible to support Data Migration Release train enabling smooth migration of all Legacy Policy records into the new system

Key: Defined Release trains/Teams | TBC Release trains/Teams

KEY AREAS – RACI [1]

Area	Beazley	Capg	Guidewire
Modernization Program Activities	A/R	C	I
Program planning & delivery			
Ways of working for all Programs under Modernization			
Procurement Management			
Program communications and stakeholder management			
SteerCo & Leadership reporting			
PMO	A/R	C	I
Risk and Issue Management tracking			
Dependency Mangement tracking			
Programme Metrics & Milestone tracking			
Programme Budget & Invoicing payments tracking			
Project infra needs set up coordination & tracking			
Deliverables tracking			
Requirements Gathering and Management (GPAS & Billing)	A	R	C
Product Backlog refinement and Business process mapping			
User story refinement with business rules and acceptance criteria			
Requirements sign-off			
Prototyping and mock-ups			
Workshops schedule, execution & follow-up			
Architecture and Technical Management (GPAS and Billing)	A/R	R	R
Confirm Architecture and Design Principles			
High level designs			
Create and maintain Technical Design Decisions			
Low level design			
Data Migration Strategy			
Environments and Infrastructure	A/R	C	R
Infrastructure and environments planning and provisioning			
Deployments, maintainence and supplier issues resolution			
Capacity planning & scalability			
Security and Compliance implementation			
Monitoring, management & performance optimisation			

Area	Beazley	Capg	Guidewire
GPAS and Billing Delivery	C	A/R	C
Delivery Management - sprint plan and execution, status reporting, risks/issue logging, risks/issue mitigation within Cap control, recording and monitoring Cap specific dependencies, problem management within Cap control, stakeholder management, change control management affecting Cap scope of work			
Develop user stories adhering to Guidewire Cloud standards			
Unit testing adhering to Guidewire Cloud Standards			
Sprint plan and raising dependencies			
Resolve Guidewire Cloud standard assessment observations			
Sprint progress reporting			
E2E Testing	A/R	C	I
End to End Test Strategy and Execution			
JIRA and Confluence set-up			
Metrics and Reporting			
Risks and Issues management			
Non Functional Testing			
Defects resolution specific to GPAS & Billing components	C	A/R	C
GPAS and Billing Sprint Testing	A	R	I
Functional test plan, test execution, defects severity and priority validations			
Risks, Issues and Dependencies status reporting			
JIRA and Confluence set-up			
Metrics and Reporting using JIRA			
User story demo sign-off			
API testing for Inbound and Outbound Integrations identified in the Integration Manifest			
Release Management	A/R	C	C
End to end release plan roadmap for the Program			
Strategy, Processes and teams for deployments, check points			
Third party coordination for all environments			
Cutover, Go-live and Post Go-live Support	A/R	R	R
Cut-over plan and Implementation Management			
Establish post Go-live Support Model			
Infrastructure and environments set-up			
Service Design and PGLS Plan			
Incident fixes specific to GPAS & Billing during warranty	C	A/R	C

Key

A	Accountable	Authority and decision making
R	Responsible	Responsible for actualisation of the task
C	Consulted	Engaged stakeholder, consulted in decisions, delivery and approach to enable their input
I	Informed	Informed stakeholder receiving updates and outputs only

Company Confidential © Capgemini 2024. All rights reserved |

KEY AREAS – RACI [2]

Area	Beazley	Capg	Guidewire
Business Change Management	A/R	C	I
Change Impact assessment and readiness			
Business roll-out plan			
Communications and reporting			
Legacy	A/R	C	I
Management of legacy party stakeholders			
Delivery of dependencies as per Program plan			
Management of design, build and testing required by GPAS & Billing			
Communication on Legacy changes that impact GPAS & Billing			
Status updates and reporting			
Finance	A/R	C	I
Management of Finance party stakeholders			
Delivery of dependencies as per Program plan			
Management of design, build and testing required by GPAS & Billing			
Communication on Finance changes that impact GPAS & Billing			
Status updates and reporting			
Documents - Beazley to confirm platform selection and requirements, post which this section to be revised as it is highly likely Capgemini will be asked to do the build	A/R	C	I
Document supplier and platform management			
Deliver Document platform dependencies as per Program plan			
Documents design			
Document template requirements, build and test			
Environment and Infrastructure management			
Data & Analytics	A/R	I	I
Data Management Strategy			
Data & Analytics build and test			
Analytics Reporting requirements & build			
Dependency management with rest of the Program			
App Events - Capgemini to do the assessment on effort required, to be done in parallel to inception			
Guidewire Data copy - CDA to Guidewire S3 bucket configuration		R	
Guidewire Data copy - Guidewire S3 bucket to Beazley S3 bucket		R	
Data movement- Beazley S3 bucket to Beazley Data Layer		I	

Area	Beazley	Capg	Guidewire
Third Parties (Integrations & Guidewire)	A/R	C	I
Third party management			
Third party deliverables alignment to Program plan			
Third party environments management			
Issues resolution with Third parties			
Status updates and reporting			
Policy Data Migration - The current scope of work for Capgemini is Policy Data Migration. The assumption for Policy Data Migration is on-renewal which will not need any work on Billing Migration. Incase of a change in assumption of on-renewal, Beazley to assess the need for additional scope on Billing Migration.	A/R	C / R	I
E2E Oversight			
Legacy Data provisioning (for Dev, Test, SIT and Dry-run)		C	
Legacy Data management (incl. data profiling)		C	
Infrastructure provisioning (for Dev, Test, SIT and secure Data env for Dry-run)		C	
Policy Data Migration Strategy / High-level Design (HLD)		R	
Policy Data Migration technical solution		R	
Policy Data Migration mapping and Gap analysis (between Source & Target - GW)		R	
Policy Data Migration implementation and Go-live strategy		R	
UWWB (Underwriting Work Bench)	A	C	I
Requirements management			
Deliverables alignment to Program plan			
Environments management			
Issues resolution impacting Program			
Status updates and reporting			
GPAS and Billing Integration (Guidewire only) - External (third party) and Internal (Beazley systems)	A/R	R	I
Integrations design			
Integrations inventory			
High Level Design			
Low Level Design			
Technical mapping document			
Plan, Build and unit test integrations			


Key

A	Accountable	Authority and decision making
R	Responsible	Responsible for actualisation of the task
C	Consulted	Engaged stakeholder, consulted in decisions, delivery and approach to enable their input
I	Informed	Informed stakeholder receiving updates and outputs only

Company Confidential © Capgemini 2024. All rights reserved |

THE 3-way collaboration for success

For the success of GPAS & Billing Program, It is critical for Capgemini-Beazley-Guidewire to work in close collaboration across phases of the Program execution.

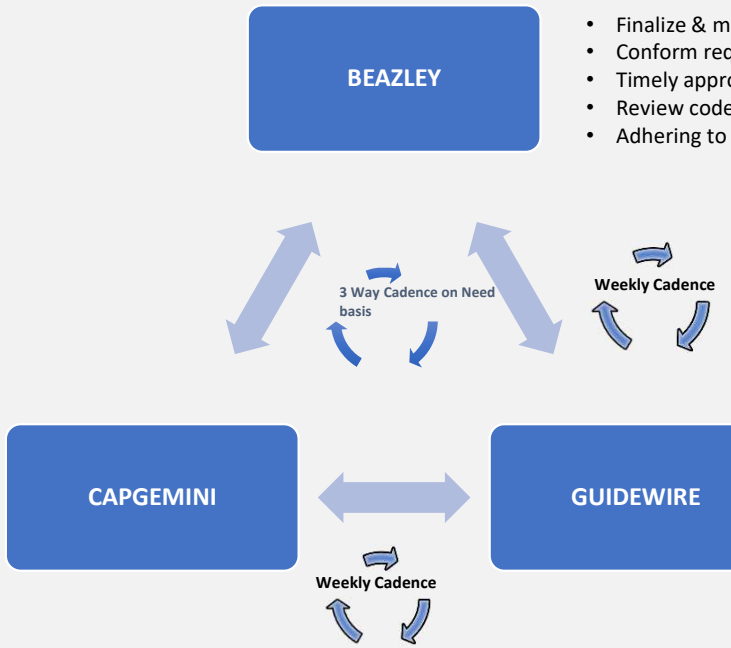

- Finalize & maintain Product contract with Guidewire
- Conform requirements to OOTB
- Timely approvals pending architecture or design considerations
- Review code assessment reports
- Adhering to the Release management prescribed by Guidewire

- Deploy certified technical team
- Build GPAS & Billing Code on SaaS platform
- Conform to Guidewire Cloud Coding standards
- Resolve Cloud assessment observations
- Collaborate for all major design decisions

- Provide SaaS platform to deploy GPAS & Billing solution
- Provide Dev and Prod environments
- Perform Code assessments & Design validations
- Updates on new product version releases
- Provide SME support as per the agreements with Beazley & Capgemini

KEY SUCCESS FACTORS


Align requirements to Product | Design and Build to standards | Collaborate on decisions

Date

Guidewire Cloud Assurance Assessment (CAA)

Cloud Assurance Program Goals are:

a. Assess and report adherence to Cloud Standards
b. Enforce remediation of Cloud Standards violations by the implementation team
c. Competency Assurance Periodic reviews conducted to ensure all Developers and Analysts are appropriately trained, certified and each workstream has the required Lead to Associate ratio (1:3). Managed by Guidewire Education team



All three components of Cloud Assurance are mandatory under the Guidewire Cloud Subscription

Overview:

- **Purpose:** Validate if developed code conforms to Guidewire Cloud standards
- **Frequency:** Monthly, at the end of each Sprint/Stabilization/Pre-Go-live

Assessment Methods:

- Automated Cloud Assurance is executed in TeamCity to run inspection on all Cloud Standards that have assessment type "Partial/Fully Automated".
- Additional manual code review of Cloud Standards that have assessment type "manual" are carried out by the Guidewire Cloud Assurance team

Outcome: Is a Cloud Assurance Report:

- GW provides report on custom code that violates Cloud Standards
- Provides suggested remediations in the Guidance section of the Cloud Assurance Report
- Capgemini and Beazley teams are provided access to the report

Review, Resolution & Reporting Process:

- **Issue Identification:**
  - Guidewire team identifies and documents issues in the Cloud Assurance Report
- **Assigning observations to developers**
  - All Cloud Assurance Report items are moved to JIRA board, assigned priority, and assigned to developers for fix
  - Any conversations on reported issues with Guidewire are completed by team ad-hoc and almost immediately
- **Reporting:**
  - The Guidewire observations fix status is reported via JIRA in the Sprint closure review provided to Beazley

Developer Workflow

Feature Branch Creation and Code Changes

- Developer creates a Feature Branch from the release branch and applies changes to the code.

Developer Code Inspection

- Developer runs the Guidewire Assurance plugin to find deviations from cloud standards.
- If any code standard issues are reported by the plugin: Developer fixes the issues and re-runs the Guidewire Assurance plugin.

Pushing to Bitbucket and CI/CD Pipeline


- Developer pushes the Feature Branch to the Bitbucket repository and waits for the TeamCity CI/CD pipeline to run.

Handling Test Failures

- If server or assurance tests fail in the TeamCity CI/CD pipeline: Developer rectifies the code in Guidewire studio , pushes the changes to the Feature Branch and continues this cycle until the server test and assurance test pass in TeamCity.

Pull Request and Code Review


- Developer raises a Pull Request (PR) to merge the Feature Branch into the release branch.
- Lead developer provides code review comments within the PR and creates a task for the developer to refactor the code.

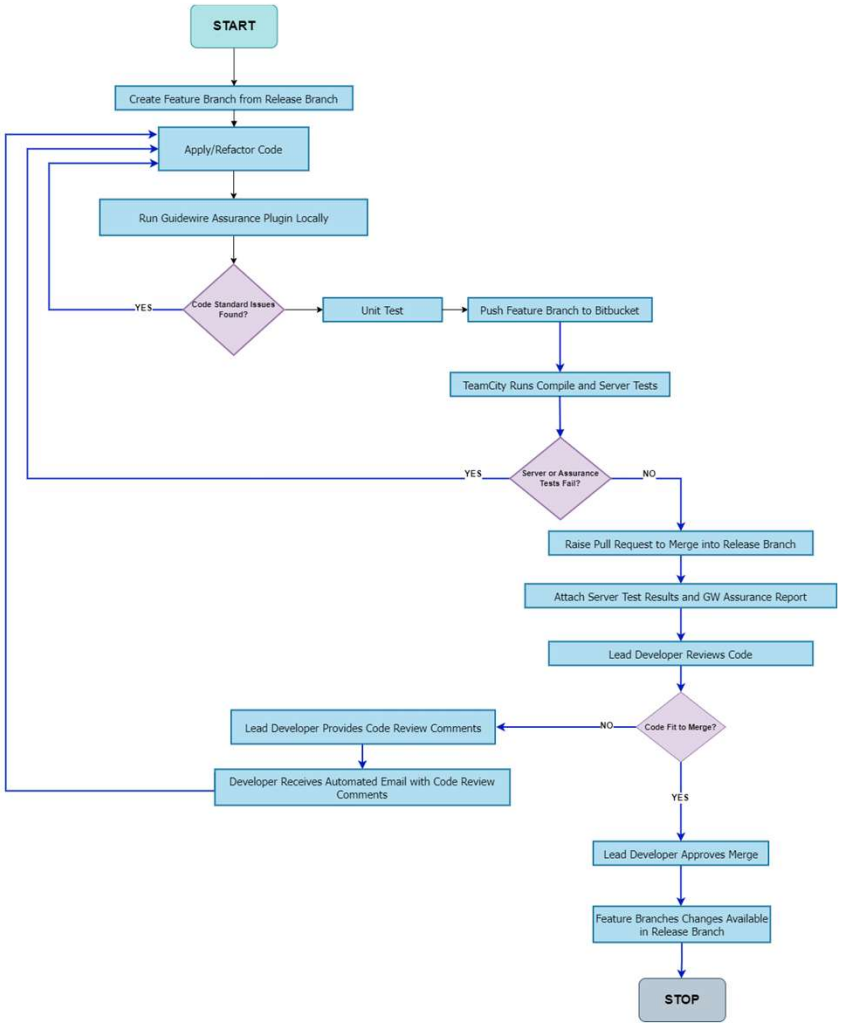

Git Branching and Merging Strategy

- **Guidewire Standard**: Follows *"Guidewire GW-MTH-1084 Branching Strategy for Guidewire Implementation Projects."*
  - Ensures robust, consistent process for managing parallel code changes within and across releases.
  - Intended for technical leads and implementation consultants.
  - Uses Git repositories for version control of source code and software artifacts
  - Managed using Guidewire-provisioned Bitbucket Server instance.
  - Implements the branching strategy described in the standard.

- **Branching Strategy Overview**:
  - **Production Branch (master)**:
    - Single production branch named master. Contains out-of-the-box product and configurations at project start.
    - Updated only during release activities or emergency fixes by senior developers.
  - **Product Release Branch (gw-releases)**:
    - Created off master at project start for new product versions and owned by Guidewire Customer and Cloud Operations.
  - **Mainline Branch (develop)**:
    - Single mainline branch named develop, created off master and contains all code across all releases.
    - Accessible to all team developers for merging.
  - **User-Story Branches**:
    - Created off develop or release branch for user stories.

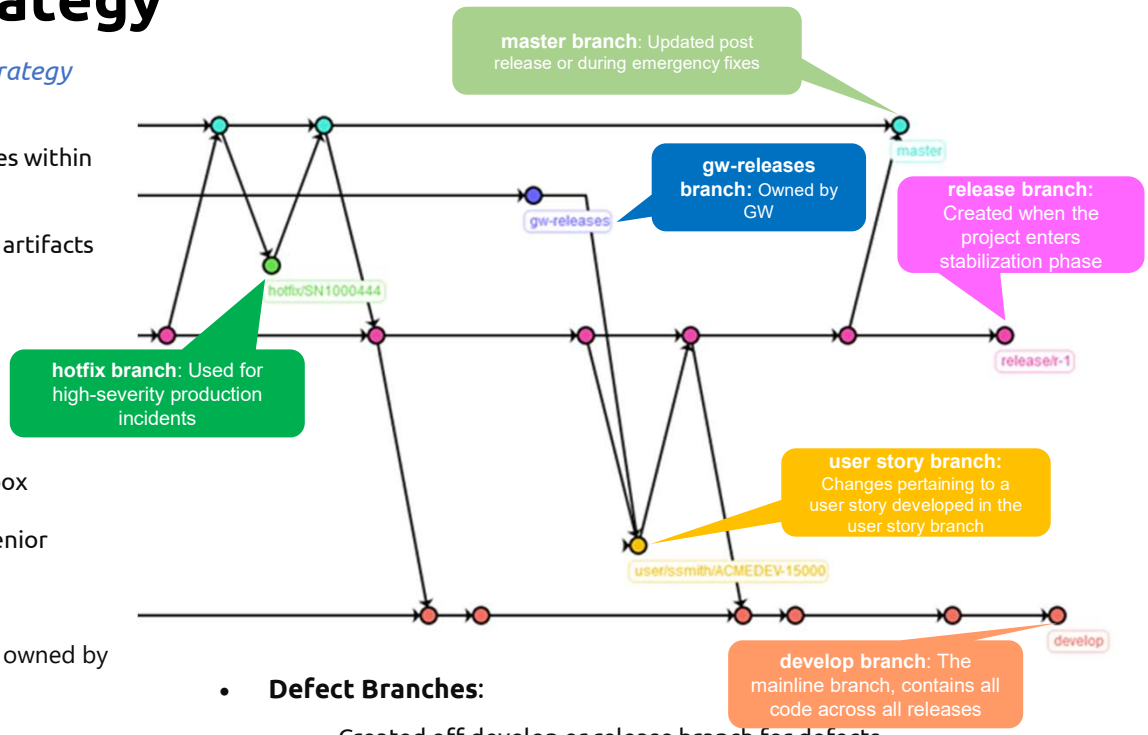

- **Defect Branches**:
  - Created off develop or release branch for defects.
- **Project Release Branches (release/r-*)**:
  - Used to stabilize code before moving to production and Named as **release/r-{release_number}**.
- **Hotfix Branches (hotfix/*)**:
  - For high-severity production incidents and created off master and named **hotfix/{id}** and merged back to master and other branches by authorized developers

Note:

1. Code management strategy will be revisited once the single instance vs multiple instance code base approach is finalized (US region and UK region specific)
2. For the initial foundation release, there will be a single branch (develop)

GUIDEWIRE UPDATES PROCESS

Capgemini's GUIDEWIRE UPDATES SCOPE

- Capgemini will Update Beazley's Foundation Release to have the latest GW v10 release of PC and BC components
- To best protect the release delivery timeline, Version Update will be taken-up during Sprint development phase and not in Stabilisation phase (E2E+UAT)
- To keep the Update efforts within the plan, Beazley implementation must stay within 10% customization limit
- Updated code base will undergo regression testing, deployments into higher environments & developer synch-up activities

GUIDEWIRE LAYER AND CUSTOMER LAYER

- The Guidewire layer and customer layer are defined to designate clear ownership of files that are contained within the InsuranceSuite artifact
- For every Version Update cycle, Guidewire will perform the Guidewire Layer update, followed by Capgemini doing the customer layer update and regression testing

Indicative timeline for each Update activity

- Updates by Guidewire – 1 to 2 weeks
- Updates by Capgemini for Beazley code base – 1 to 2 weeks
- Regression testing across dev & test environments within build phase – 1 to 2 weeks
- Final sign-off by development team & developer workspace synch-up – 1 week

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Sprint – DoR and DoD

Sprint Definition of Ready

- Sprint backlog hand off (technical and functional clarifications with PO/Business SME) is complete and user stories are in compliance with Definition of Ready
- Sprint backlog is based on the available sprint capacity (Build & QA hours available)
- Product Data Model requirements are finalized
- Signed off HLA made available by the architecture team wherever applicable (applicability of this is determined during elaboration of requirements)
- All dependencies have been resolved. Dependency items are agreed for all third-parties (internal and external)
- Environment configuration completed, and access setup done for workstream members

PO – Product Owner
ETL – Extract Transform & Load
HLA – High Level Architecture

Sprint Definition of Done

- All user stories and sub tasks within a user story are in Done status
- Completed user stories follow the User Story Definition of Done or any exception is agreed with Beazley
- Stories not in 'Done' status have an agreement between Capgemini and Beazley to be reassigned either to backlog or an identified sprint
- Test execution is complete in Jira with no test cases in 'To Do' status or if any exception is agreed with Beazley
- High priority or severity defects have been either closed or there is a mutually agreed fix plan with Beazley for the open defects
- Sprint completion reports are shared with Beazley stakeholders – Business SME/PO and Program Management team
- Sprint Retrospective conducted and agreements or actions are documented
- Automation testing (if applicable) has a coverage to the requirement level as defined in the test strategy

Please note that the Sprint DoD validation will happen in the week after the last week of the Sprint development
