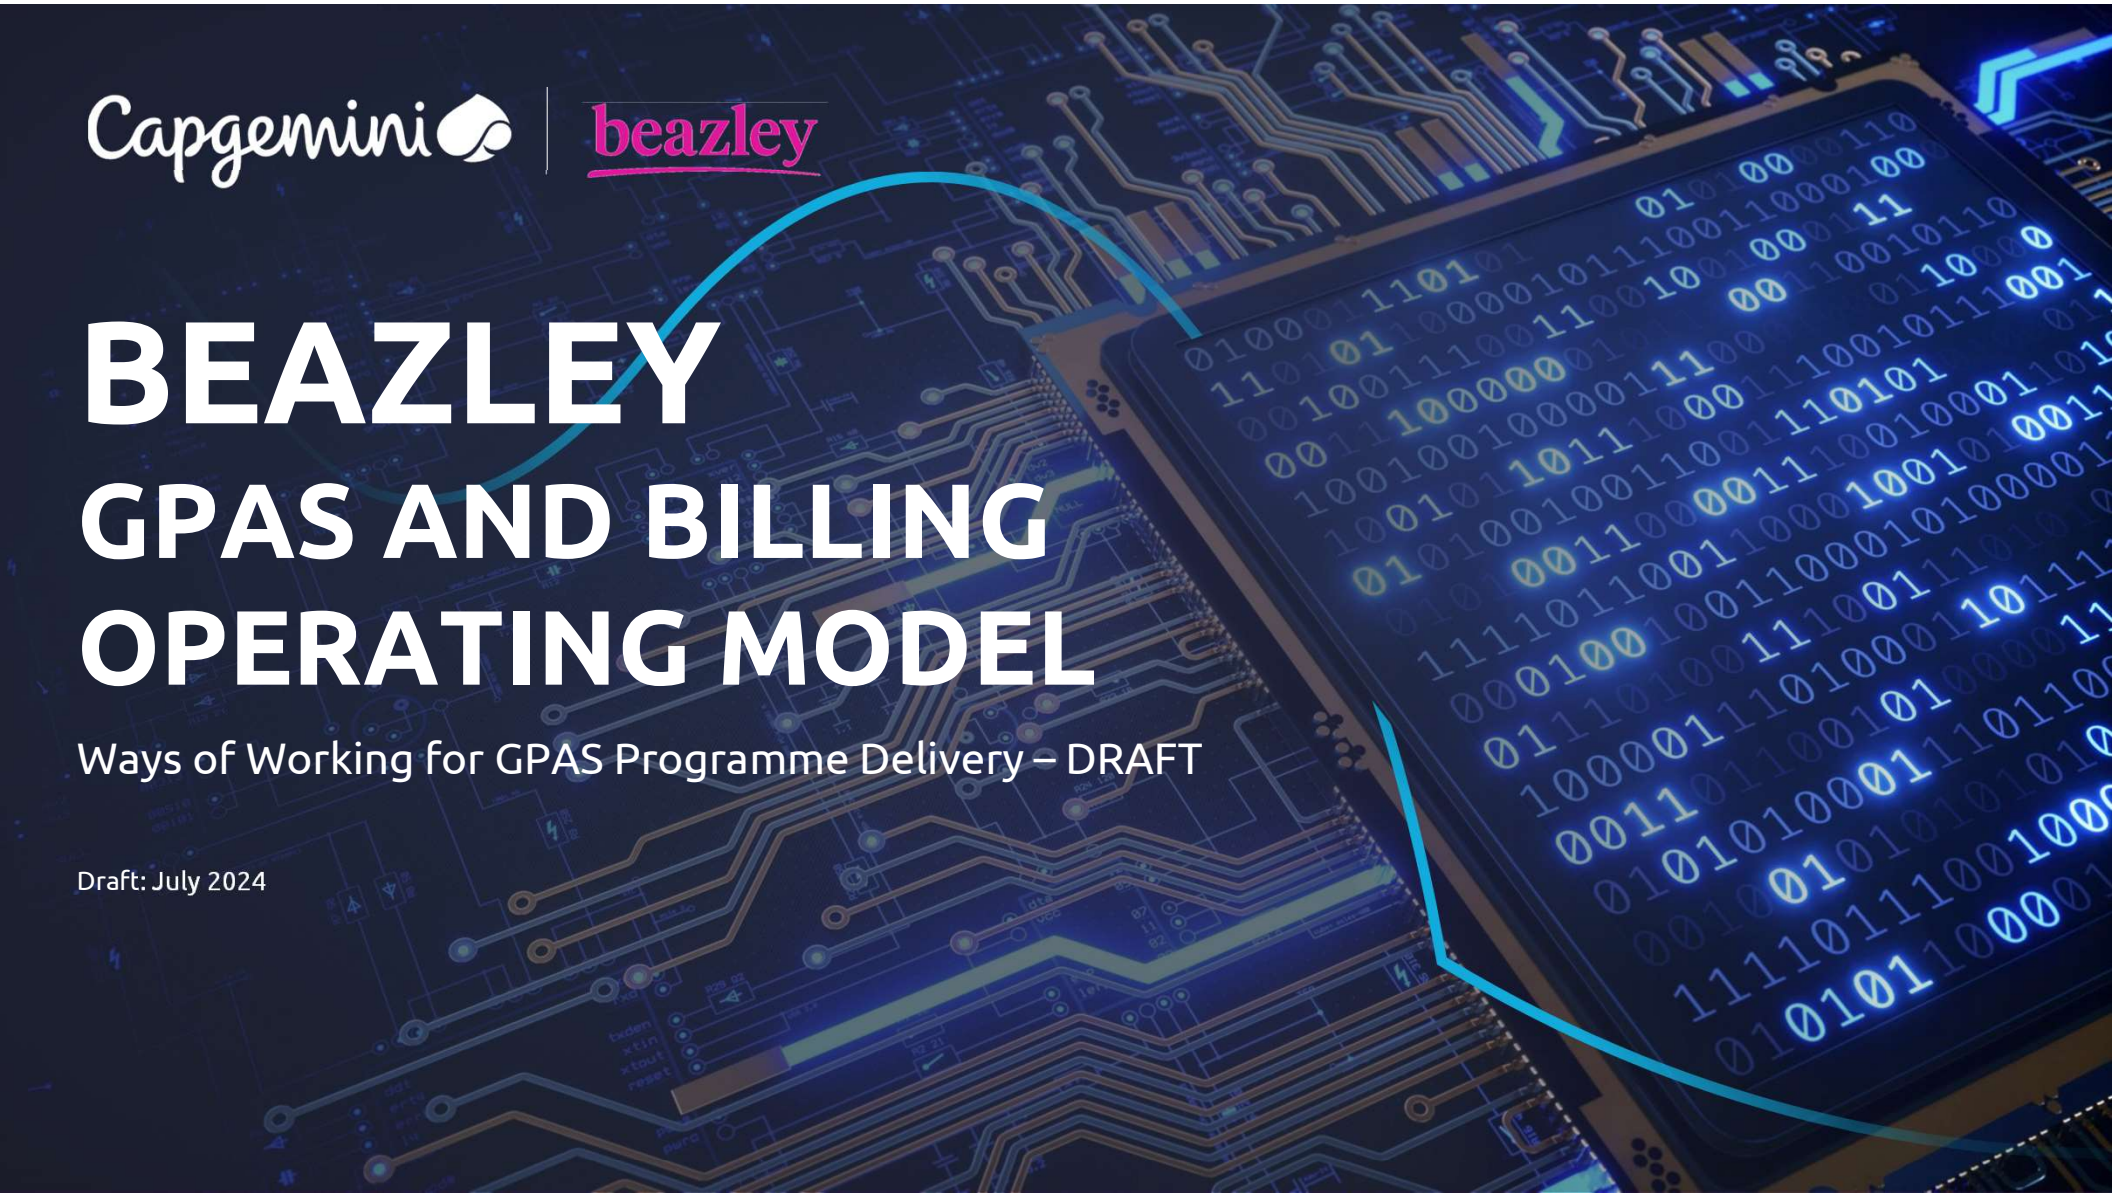


Capgemini | beazley

BEAZLEY
GPAS AND BILLING OPERATING MODEL

Ways of Working for GPAS Programme Delivery – DRAFT

Draft: July 2024

CONTEXT

Ways of working is a Capgemini recommended way of Program execution allowing all relevant parties and stakeholders to operate and collaborate towards achieving the common program goals. This document intends to target both processes and behaviours that form the building blocks of successful completion of GPAS


This Ways of working is specifically designed for GPAS and Billing scope of work only and for the scope of work owned by Capgemini. The processes, behaviours and recommendations outlined here may not be applicable outside GPAS to the wider Modernization program

The Ways of working document is expected to evolve iteratively, through Inception phase before it can be made final. However, throughout the GPAS program execution, the delivery method or process may undergo change in certain sections if all the influenced parties agree there is a need for improvement

Company Confidential © Capgemini 2024. All rights reserved |

WAYS OF WORKING

The immediate focus is to draft and agree on Ways of working applicable for the start of Inception phase covering activities, deliverables, methods and processes expected to be jointly built and done by Capgemini and Beazley. As a next step, this document will be extended to document methods and processes applicable to the Build phase.




To be built & agreed for start of Inception

- Scope of Inception phase
- Key Success factors
- Inception activities – week wise split
- Workshops – rules of engagement
- Inception phase deliverables
- Team Structure for Inception
- Design Principles
- RACI
- Key roles – Beazley and Capgemini
- Governance – Key roles, Cadence, Escalation, Change

Control

- Tools for Inception
- JIRA set-up and governance



Build Phase

- Sprint Timeline, Ceremonies, Reporting
- Standard Development Team Composition
- User story composition, Elaboration Cycle
- Cadence, Sprint Events RACI
- Scrum of Scrums, Retrospectives
- User Story Management – Different Scenarios
- Activities List – Elaboration, Design & Dev
- A Day in a life during Sprint Development
- DoD and DoR – User story & Sprint
- Working with Guidewire – 3 way collaboration


- Testing – Scope, Strategy, Governance, Activities, and Schedule
- Third party dependency management
- Sprint Progress tracking
- Sprint Closure report

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

GPAS & BILLING MODERNISATION ORGANISATION CHART

* The organization chart is placed in "Programme Structure Chart.xlsx " share point page for reference

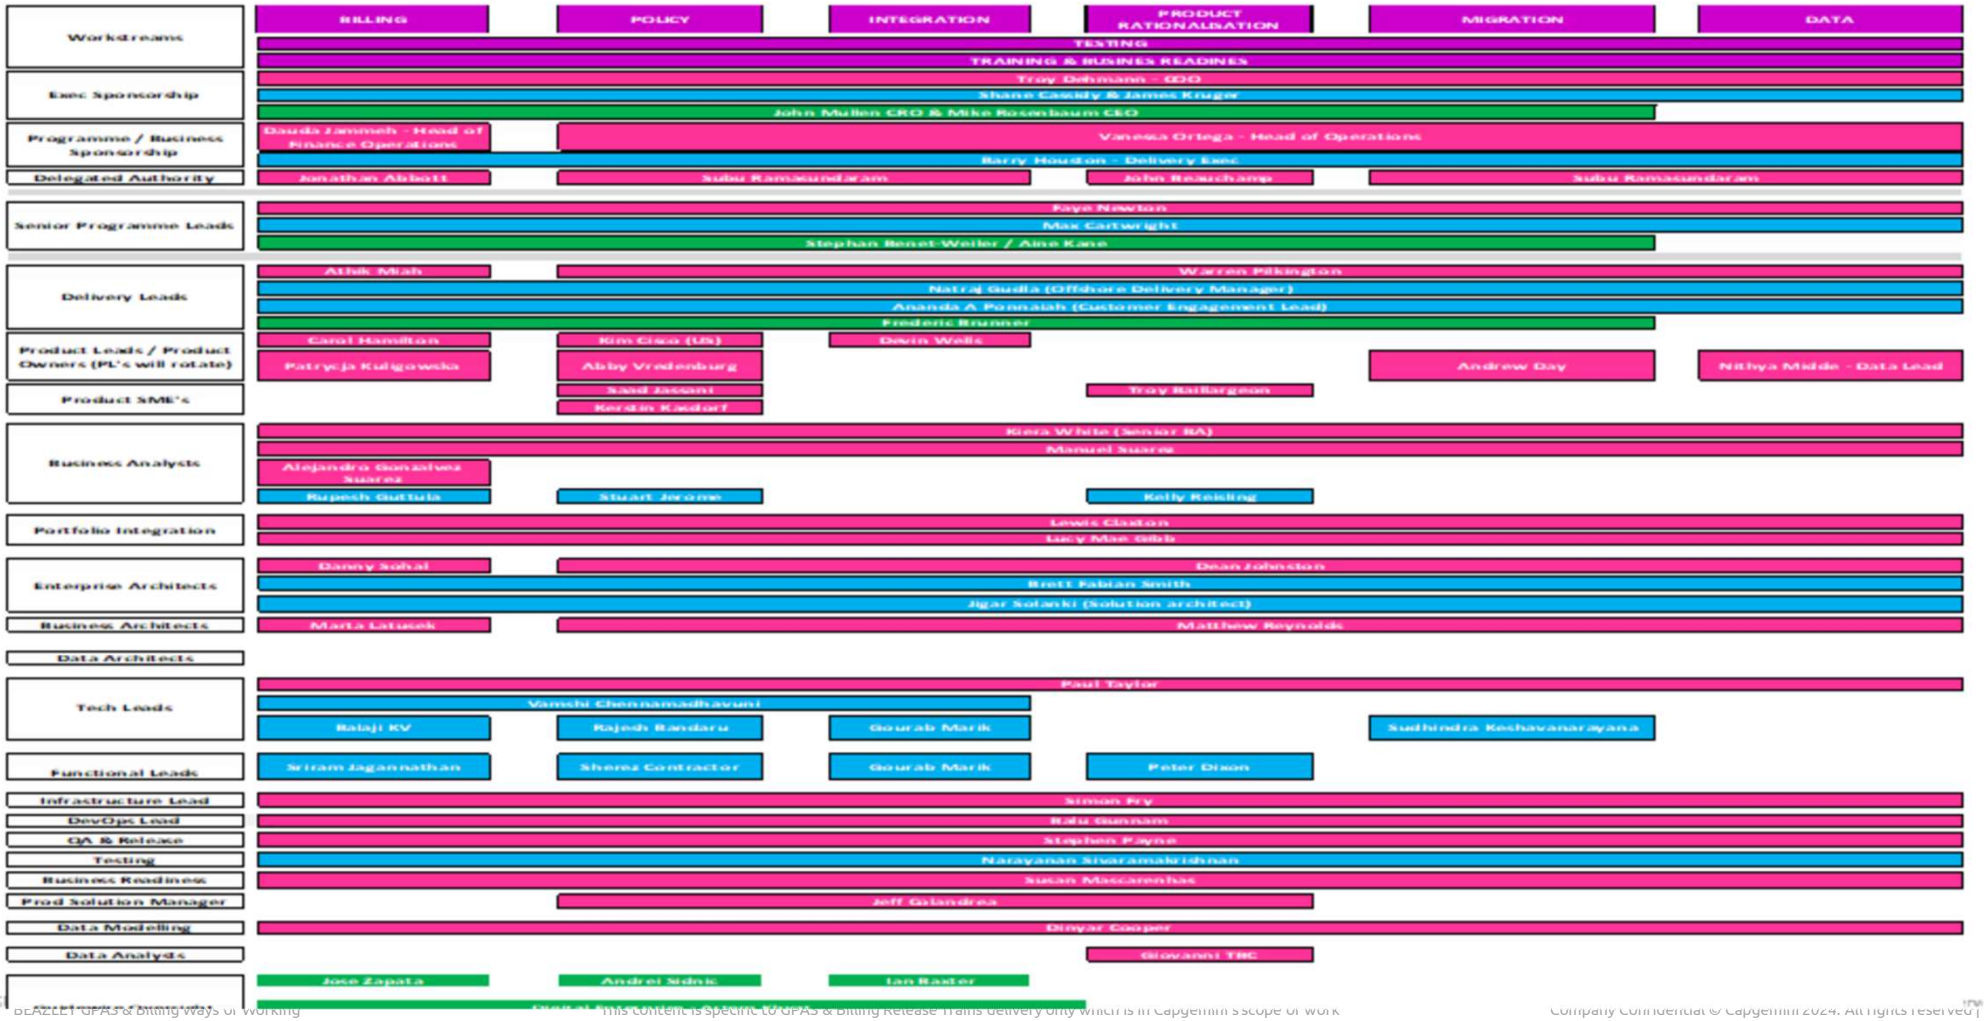

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved

GPAS & BILLING PROGRAM RELEASE TRAINS

PROGRAM MANAGEMENT	• Responsible for Overall Program Governance that includes Planning, Monitoring execution to Budget, Mitigate Risks & Issues.
BILLING (Guidewire)	• Responsible to implement the new Billing system in Guidewire to handle Billing cycle of all new Policies to be initiated under the new Policy system
POLICY (Guidewire)	• Responsible to implement the new Policy system in Guidewire across all Beazley Product variations & Lines of Business in Scope
INTEGRATION	• Responsible to implement the in-scope integration elements necessary to ensure Guidewire operates as per business requirements.
PRODUCT RATIONALISATION	• Responsible to Rationalise product set for Foundation release and agree a framework for rationalising the remaining GPAS Products.
MIGRATION	• Responsible to Migrate all Legacy Policy data at renewal into the new Guidewire system.
TESTING	• Responsible to make sure we are deploying code to production that meets Business requirements & Program and Product quality standards
DATA	• Responsible to Build Data analytics on top of GPAS & Billing data meeting Business needs.
DOCS TOOLING	• Responsible to implement all necessary communications to support Beazley's business requirements.
TRAINING & BUSINESS READINESS	• Responsible to Design and Roll out the new system to Business users, handle training, comms, stakeholder Mgmnt., risks and issue mitigation.
BUSINESS DESIGN	• Responsible to create a centre of excellence for Beazley E2E process and journey design, ensuring consistency and quality.
ARCHITECTURE	• Responsible to create a System Architecture for the Program that is Robust, Industry standard, Scalable and meets Beazley's requirements
ENVIRONMENTS & INFRASTRUCTURE	• Responsible to provision all Infrastructure & Environments for a smooth Program execution e.g. Citrix machines, Scalable Dev, Test and Prod environments, DevOps support for continuous deployments & testing.
FINANCE	• Responsible to validate & sign-off Finance systems to the new GPAS & Billing implementation
LEGACY	• Responsible to support Data Migration Release train enabling smooth migration of all Legacy Policy records into the new system

Key: Defined Release trains/Teams | TBC Release trains/Teams


This content is specific to GPAS & Billing Re... Company Confidential © Capgemini 2024. All rights reserved |

INCEPTION PHASE HELPS TO CREATE THE FOUNDATION AND VISION FOR THE TRANSFORMATION

A common 12-weeks Programme Inception phase to clarify and align the scope in all Products for a Foundation, followed by the implementation of the planned Releases.

Programme Inception → **Design and Build**

Programme Inception is focused on **"Designing the next winning proposition"**

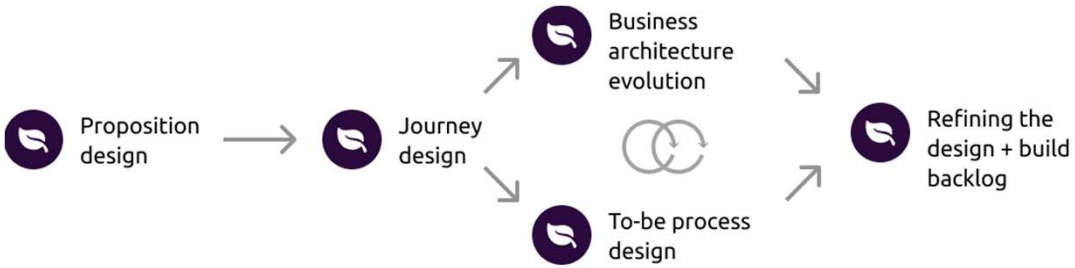

What you'll get:

1. Prioritized backlog
2. High Level Design
3. Foundation release plan
4. Key risks & assumptions
5. Dependencies detailed

- Foundation Release Mobilization is focused on enabling MVP Design and Build to start
- Build the foundation with core principles intact. – data/ automation / experience
- Collaborative pre-work on entry criteria to ensure rapid start and timely completion
- Transform the plan from the Inception to reality, transforming the business requirements to functional systems
- Plan for future Releases and LOB
- Confirm Roll-out Approach
- Key Design Decisions log

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

KEY SUCCESS FACTORS

Right Time

- Multi-day sessions
- Aligned workshops
- Covering India, UK and US time zone

Right Inputs

- Product / Process Design
- OOTB Guidewire Process Flows
- Interfaces

Right Team


- Product Owners, Business SME
- Right Capgemini team
- Collaboration is key

Right Enablers

- Guidewire Instance
- Collab Tools
- Reliable access to VDIs

Right Decisions

- Timely & accurate decisions
- On time escalations for help
- Lean thinking

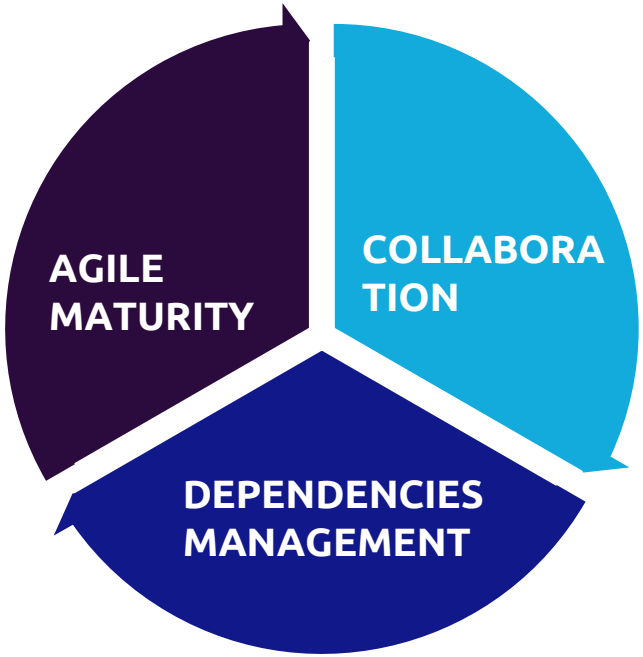

Inception Phase Principles

OOTB Conformance

Business Priority / Rationale

Design for Future

Outputs more focused at Foundation release

- GPAS Ways of working
- Prioritized Backlog
- Effort & Resourcing
- GPAS & Billing HLD and Delivery Plan
- LLD for Initial build phase
- Key Design Decisions
- Migration Strategy
- Integration Inventory
- Dependency tracker
- Test Strategy
- Rationalized Product set
- Foundation Release Plan

Pebbles / Rocks / Boulders

Categorizing elements of solution for appropriate escalation to finalise scope

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |


DESIGN PRINCIPLES

All key decisions to move through formal programme governance decision bodies

Does the decision?:

- Support the agreed Release scope
- Ensure the business is not in a worse position from before
- Support a move off existing systems
- Support flexibility and maintainability for future releases
- Conform to Beazley architectural principles
- Allow for scalability and is not closed off for future-states
- Complies to Beazley's Information Security requirements

Decision making process:

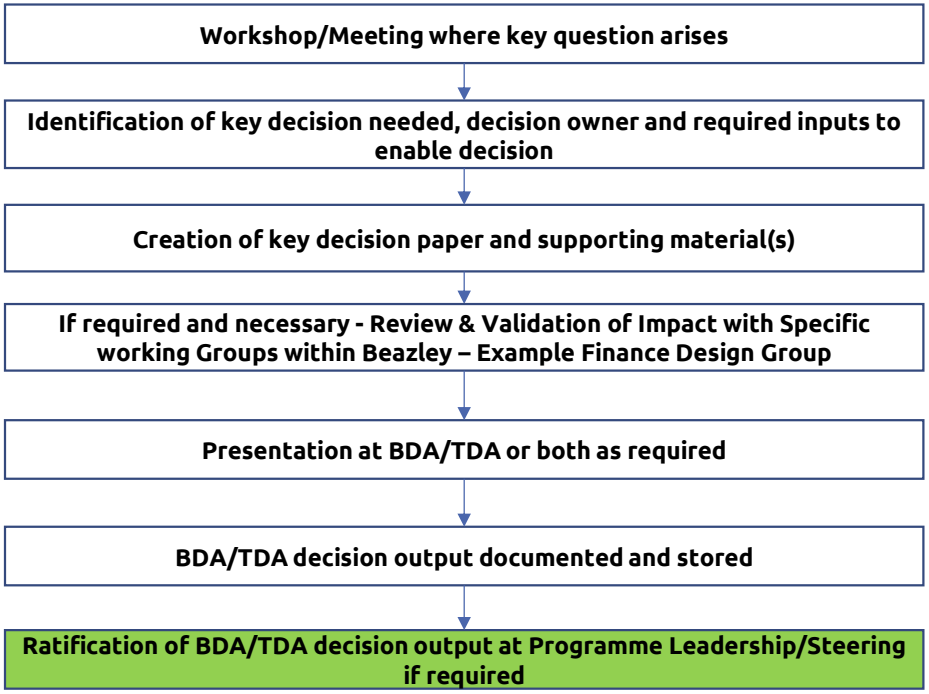

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

GUIDELINES FOR MEETINGS AND WORKSHOPS

Rules of Engagement

- All meeting and workshop invites to include:
  - Purpose of the meeting / Agenda
  - Input to the meeting
  - Expected output from the meeting
  - Deliverable(s) output (as required)
- Business attendees and availability to be confirmed by Beazley (Senior Product Owner/relevant Product Owner) before invitation is sent
- Parking lots/Decision logs to be captured and logged in the required trackers
- Critical decisions to go through appropriate Programme Governance forums and documentation
- On site and remote attendance options to be available
- Recording of sessions to be used where appropriate
- All sessions to be aligned to overall programme strategy
- All material to be utilised for Beazley programme purposes only



This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

HIGH LEVEL SCOPE ELEMENTS

The entries here are high-level and the initial understanding of the scope between different parties. Through the Elaboration phase all scope items will be discussed, expanded and requirement boundaries defined. The Prioritised backlog, Detailed Dependency tracker Inception deliverables that Capgemini will produce will detail the final scope for Foundation release (specific to Policy, Billing, Integration, Migration and Product Rationalization) and call out dependencies amongst different parties.

	BILLING	POLICY	INTEGRATION	MIGRATION	PRODUCT RATIONALISATION & DEFINITION	DATA	TESTING	TRAINING & BUSINESS READINESS
HIGH LEVEL OBJECTIVE	To implement the new Billing system in Guidewire to handle Billing cycle of all new Policies to be initiated under the new Policy system.	To implement the new Policy system in Guidewire across all Beazley Product variations & Lines of Business in Scope.	To implement the in-scope integration elements necessary to ensure Guidewire operates as per business requirements	To Migrate all Legacy Policy data at renewal into the new Guidewire system.	Create global view of Beazley products in a defined, easily maintained structure across Beazley & mastered in GW PC improving data quality & efficiency	To stream to relevant raw data for policy transactions and products into MDA	To make sure we are deploying code to production that meets Business requirements & Program & Product quality standards.	To Design and roll out the new system to Business users, handle training, comms, stakeholder management, risks & issue mitigation.
CAP INCEPTION DELIVERABLES	• Documentation of Foundation Release Functional requirements, in scope Epics. • User Stories scope statements defined in excel format for uploading into JIRA. • Plan detailing the Guidewire sprint plan, number of sprints, dates, and high-level proposed scope breakdown. • Documentation of GPAS and Billing scope and supporting assumptions. • Aligned to agreed architecture decisions and principles. Detail how Policy and Billing Center will fit into Beazley ecosystem. (e.g. ClaimsCenter) • Complete GPAS functional, technical and architecture KDDs (key design decisions) documented. • **BILLING:** Perform a cash matching Proof of Concept • **POLICY:** Perform a Jutro Proof of Concept		Detail the key Integrations for the Foundation release. Inventory of integrations defining cardinality, service contract ownership, integration pattern or method, initial view on complexity. Definition of any intermediary services or gateways to influence design.	Approach to migration in terms of execution and timing. High-level data requirements and dependencies at an entity level, from relevant business areas.	Rationalised product set for Foundation release. Agreed framework for rationalising the remaining GPAS Products.		High level scope of key test phases (UNIT/SIT/UAT), gates and entry/exit criteria; view of resourcing. Input into Definition of Done (DoD) including acceptance criteria, automation definition within sprint or sprint +1 adhering to Guidewire standards. Definition of the GPAS environment requirements and when they will be required by to meet the timelines.	
BEAZLEY DELIVERABLES **(Inception & onwards)**	• GW essential service oversight • Support cap in achieving agreed outcomes		Management of the internal and 3rd party workstreams to agree/plan/delivery of required integrations.	• Migration strategy defined during inception • Data extraction, profiling, modelling. • Work with cap to translate into new GW data structure	GW essential service oversight	Product reference data – off the back off prod rat work Once we start development, we will need to fed raw data for policy transactions into the MDA	• Test strategy defined during Inception • E2E/UAT, performance, pen and acceptance testing • GW essential service oversight	Immediate tasks Communications plan Business engagement and agreement for SME support at relevant points

Company Confidential © Capgemini 2024. All rights reserved |

INCEPTION PROGRAMME DELIVERABLE OUTPUTS

Deliverables at programme level & expected signatories

Deliverables to be produced during Inception, ready for review and response feedback loop. All deliverables to have a wider review distribution which will be confirmed on the deliverable itself.

Deliverable Names	High level Description and Expectation	Review	Sign Off
PD1: GPAS Ways of Working	Detailed methodology, Governance model, Change control model, communication management, Reporting & meeting cadence, Initial team structure, RACI, Escalation approach, Tools for build & usage boundaries	Core GPAS Team	Steering Group GPAS/Billing
PD2: Prioritized Backlog (Foundation)	Documentation of Foundation Release Functional requirements, in scope Epics/Features. User Stories scope statement defined in excel format for uploading into JIRA	Core GPAS Team	Product Owners
PD3: Resourcing & Efforts (Foundation)	Breakdown of resourcing needs (by quarter) aligned to effort and bottom-up estimation of Epics and Features against the delivery plan. High level scope, budget, and resourcing/effort should reconcile.	Core GPAS Team	Delivery Leads
PD4: Delivery Structure & Plan (Foundation)	Phase & Release train definitions, objectives and milestones. Verification and Acceptance. Plan detailing the Guidewire sprint plan, number of sprints, dates, and high-level proposed scope breakdown.	Core GPAS Team	Delivery Leads
PD5: GPAS High Level Design	Aligned to agreed architecture decisions and principles Detail how Policy and Billing Center will fit into Beazley ecosystem. Detail the key Integrations for the Foundation release	Core GPAS Team	Enterprise Architects
PD6: Migration Strategy	Approach to migration in terms of execution and timing. High-level data requirements at an entity level, from relevant business areas.	GPAS Steering Group	Strategic Design Authority
PD7: Integration Manifest	Inventory of integrations defining cardinality, service contract ownership, integration pattern or method, initial view on complexity. Definition of any intermediated services or gateways to influence design.	Product Owners Integration Lead	Enterprise Architects

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

INCEPTION PROGRAMME DELIVERABLE OUTPUTS

Deliverables at programme level & expected signatories

Deliverables to be produced during Inception, ready for review and response feedback loop. All deliverables to have a wider review distribution which will be confirmed on the deliverable itself

Deliverable Names	High level Description and Expectation	Reviewer	Sign Off
PD8: Detailed Dependency Tracker	Internal and External Dependencies detailed with dates and deliverables agreed with each of the related parties.	Core GPAS Team	Delivery Leads
PD9: Functional & Technical Principals	Functional and Technical Design principles documented.	Core GPAS Team	Delivery Leads
PD10: GPAS Test Strategy	High level scope of key test phases, gates and entry/exit criteria; view of resourcing. Input into Definition of Done (DoD) including acceptance criteria, automation definition. Definition of the GPAS environment requirements and when they will be required by to meet the timelines.	QA Lead Core GPAS Team	Delivery Leads
PD11: Product Set	Rationalised product set for foundation release Identification of any products requiring further analysis and key decision papers where necessary.	Core GPAS Team Product Definition Release train (UW)	Strategic Design Authority
PD12: Perform a Jutro Proof of Concept.	Walkthrough of PoC which should demonstrate the applicability of Jutro to Build out UWWB screens. Options paper detailing the pros/cons of Jutro approach vs building it out in UWWb.	Reviewed and Agreed with Beazley EA (GPAS & Billing)	Beazley EA
PD13: Perform a cash matching Proof of Concept for Billing	Walkthrough of PoC which should demonstrate that cash matching requirements can (or cannot) be assigned from backlog	Reviewed and Agreed with Beazley PO (Billing)	Product Owner (Billing)

To maximize efficiency and protect our plans, we will work with a **'2 review plus sign off'** approach to deliverable sign off. Initial review (**3 working days**), second review (**2 working days**) and sign off (**1 working day**). Expectation is that the second review includes feedback from 1st review updates only. A tracker will be used to help track and manage progress. This sign-off approach will be followed for other areas like Test Strategy, Test Scenarios, Migration Plan and similar documents or approaches that need Beazley sign-off throughout the Program duration.

Company Confidential © Capgemini 2024. All rights reserved |

KEY AREAS – RACI [1]

Area	Beazley	Capg	Guidewire
Modernization Program Activities	A/R	C	I
Program planning & delivery			
Ways of working for all Programs under Modernization			
Procurement Management			
Program communications and stakeholder management			
SteerCo & Leadership reporting			
PMO	A/R	C	I
Risk and Issue Management tracking			
Dependency Mangement tracking			
Programme Metrics & Milestone tracking			
Programme Budget & Invoicing payments tracking			
Project infra needs set up coordination & tracking			
Deliverables tracking			
Requirements Gathering and Management (GPAS & Billing)	A	R	C
Product Backlog refinement and Business process mapping			
User story refinement with business rules and acceptance criteria			
Requirements sign-off			
Prototyping and mock-ups			
Workshops schedule, execution & follow-up			
Architecture and Technical Management (GPAS and Billing)	A/R	R	R
Confirm Architecture and Design Principles			
High level designs			
Create and maintain Technical Design Decisions			
Low level design			
Data Migration Strategy			
Environments and Infrastructure	A/R	C	R
Infrastructure and environments planning and provisioning			
Deployments, maintainence and supplier issues resolution			
Capacity planning & scalability			
Security and Compliance implementation			
Monitoring, management & performance optimisation			

Area	Beazley	Capg	Guidewire
GPAS and Billing Delivery	C	A/R	C
Delivery Management - sprint plan and execution, status reporting, risks/issue logging, risks/issue mitigation within Cap control, recording and monitoring Cap specific dependencies, problem management within Cap control, stakeholder management, change control management affecting Cap scope of work			
Develop user stories adhering to Guidewire Cloud standards			
Unit testing adhering to Guidewire Cloud Standards			
Sprint plan and raising dependencies			
Resolve Guidewire Cloud standard assessment observations			
Sprint progress reporting			
E2E Testing	A/R	C	I
End to End Test Strategy and Execution			
JIRA and Confluence set-up			
Metrics and Reporting			
Risks and Issues management			
Non Functional Testing			
Defects resolution specific to GPAS & Billing components	C	A/R	C
GPAS and Billing Sprint Testing	A	R	I
Functional test plan, test execution, defects severity and priority validations			
Risks, Issues and Dependencies status reporting			
JIRA and Confluence set-up			
Metrics and Reporting using JIRA			
User story demo sign-off			
API testing for Inbound and Outbound Integrations identified in the Integration Manifest			
Release Management	A/R	C	C
End to end release plan roadmap for the Program			
Strategy, Processes and teams for deployments, check points			
Third party coordination for all environments			
Cutover, Go-live and Post Go-live Support	A/R	R	R
Cut-over plan and Implementation Management			
Establish post Go-live Support Model			
Infrastructure and environments set-up			
Service Design and PGLS Plan			
Incident fixes specific to GPAS & Billing during warranty	C	A/R	C

Key

A	Accountable	Authority and decision making
R	Responsible	Responsible for actualisation of the task
C	Consulted	Engaged stakeholder, consulted in decisions, delivery and approach to enable their input
I	Informed	Informed stakeholder receiving updates and outputs only

** **In-Sprint Integration testing -** Integrations finalized in the Integration Manifest, will need to arrive at the sprint schedule in line with the sprint plan. Any deviations to this will need to be impact assessed. If these deviations can be accommodated without impacting the overall in-sprint testing schedule, Capgemini will seek to accommodate them, however, this cannot be guaranteed

Company Confidential © Capgemini 2024. All rights reserved |

KEY AREAS – RACI [2]

Area	Beazley	Capg	Guidewire
Business Change Management			
Change Impact assessment and readiness	A/R	C	I
Business roll-out plan			
Communications and reporting			
Legacy			
Management of legacy party stakeholders	A/R	C	I
Delivery of dependencies as per Program plan			
Management of design, build and testing required by GPAS & Billing			
Communication on Legacy changes that impact GPAS & Billing			
Status updates and reporting			
Finance			
Management of Finance party stakeholders	A/R	C	I
Delivery of dependencies as per Program plan			
Management of design, build and testing required by GPAS & Billing			
Communication on Finance changes that impact GPAS & Billing			
Status updates and reporting			
Documents - Beazley to confirm platform selection and requirements, post which this section to be revised as it is highly likely Capgemini will be asked to do the build	A/R	C	I
Document supplier and platform management			
Deliver Document platform dependencies as per Program plan			
Documents design			
Document template requirements, build and test			
Environment and Infrastructure management			
Data & Analytics	A/R	I	I
Data Management Strategy			
Data & Analytics build and test			
Analytics Reporting requirements & build			
Dependency management with rest of the Program			
App Events - Capgemini to do the assessment on effort required, to be done in parallel to inception			
Guidewire Data copy - CDA to Guidewire S3 bucket configuration		R	
Guidewire Data copy - Guidewire S3 bucket to Beazley S3 bucket		R	
Data movement- Beazley S3 bucket to Beazley Data Layer		I	

Area	Beazley	Capg	Guidewire
Third Parties (Integrations & Guidewire)	A/R	C	I
Third party management			
Third party deliverables alignment to Program plan			
Third party environments management			
Issues resolution with Third parties			
Status updates and reporting			
Policy Data Migration - The current scope of work for Capgemini is Policy Data Migration. The assumption for Policy Data Migration is on-renewal which will not need any work on Billing Migration. Incase of a change in assumption of on-renewal, Beazley to assess the need for additional scope on Billing Migration.	A/R	C	I
E2E Oversight			
Legacy Data provisioning (for Dev, Test, SIT and Dry-run)			
Legacy Data management (incl. data profiling)			
Infrastructure provisioning (for Dev, Test, SIT and secure Data env for Dry-run)			
Policy Data Migration Strategy / High-level Design (HLD)		R	
Policy Data Migration technical solution			
Policy Data Migration mapping and Gap analysis (between Source & Target - GW)			
Policy Data Migration implementation and Go-live strategy			
UWWB (Underwriting Work Bench)	A	C	I
Requirements management			
Deliverables alignment to Program plan			
Environments management			
Issues resolution impacting Program			
Status updates and reporting			
GPAS and Billing Integration (Guidewire only) - External (third party) and Internal (Beazley systems)	A/R	R	I
Integrations design			
Integrations inventory			
High Level Design			
Low Level Design			
Technical mapping document			
Plan, Build and unit test integrations			

Key

A	Accountable	Authority and decision making
R	Responsible	Responsible for actualisation of the task
C	Consulted	Engaged stakeholder, consulted in decisions, delivery and approach to enable their input
I	Informed	Informed stakeholder receiving updates and outputs only

Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES – BEAZLEY

Role	Named Resource	Responsibilities
Business Owner/ Sponsor	Vanessa Ortega Dauda Jammeh	• Ensure alignment to overall Modernisation/Beazley strategic goals • Drive senior accountability across the programme • Approve scope, target design and execution plans for the PAS initiative. • Accountable for delivery against OKRs, business outcomes and benefit realisation. • Commits or helps facilitate appropriate resources (e.g. SMEs) and support issue resolution for the PAS initiative. • Approve and oversee key initiative decisions as adviser • Steer solution design and build based on business needs • Drive agreement of dependencies at sponsorship/exec level, if required. • Approvals (or noting) of vendor outcomes/deliverables
Program Director	Faye Newton	○ Be the Single point of Ownership from Beazley on the Program ○ Program Manage execution of the GPAS & Billing Business requirements ○ Mitigate Program Risks and Issues from time to time ○ Provide leadership and Direction to motivate teams towards successful program completion ○ Collaborate with involved stakeholders for success of the Program ○ Responsible for overall Services quality and delivery of the Program
PAS Delivery Lead / Billing Delivery Lead	Warren Pilkington Athik Miah	• Develop the initiative objectives, scope, high-level implementation roadmap, resource requirements and investment estimates. • Working with the delivery partners, create and manage the PAS delivery plans. • Manage the delivery teams inc. resource management, supply & demand, technical capability and skills • Manage inbound and outbound dependencies needed for the delivery of the component • Management of risks and issues impacting progress • Responsible for status reporting of the project • Lead by example, driving the right behaviours across the programme
Senior Technical Partners / Business Leads	Jonathan Abbot	• Provide holistic business/technical expertise and oversight for their workstream/Programme • Have delegated authority to make decisions on Sponsors behalf for their relevant workstream • Aligns with other Senior Leads/relevant SMEs to assess and understand impact of risks/issues/decisions/dependencies. • Attends exec leadership level governance forums and leadership/delivery forums as required • Lead by example, driving the right behaviours across the programme
Architecture	Danny Sobal (Finance EA) Marta Latuszek (Billing Business)	• Work with squads to define target state technical solutions, identify technology requirements • Gain approval through Design Authority for technical solutions including any security compliance • Identify and monitor architecture & design technical risks and dependencies, oversee necessary mitigation controls • Assurance of HLD and LLD solution designs with CAP Architects for GPAS • Delivery of HLD/LLD solution designs for Beazley dependent elements of the overall solution design • Work with Release train teams to: ▪ Define architectural backlog and technical guardrails ▪ Provide the necessary Inputs to groom the Backlog and Sprint/PI Planning ▪ Ensure architecture compliance with agreed SDLC and Beazley standards ▪ Manage Version Control of architecture related components ▪ Identify dependencies and risks affecting architecture & design

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES – BEAZLEY

Role	Named Resource	Responsibilities
Global PAS Technical/Functional Lead	Jeff Colandrea	• Helps define the PAS Product Strategy, Vision and Roadmaps alongside the Product Owners in the PAS initiative. • Managing and prioritizing the PAS Portfolio Backlog taking care to ensure alignment with business architecture, data teams and existing BAU environments. • Delivering Value by ensuring the PAS solutions are complete from the user perspective (including operations, change etc.) and deliver meaningful business value. • Point of escalation and coaching for squad-level Product Owners.
Product Owners	Carol Hamilton (Billing) Patrycja Kuligowska (Billing) Kerstin Kasdorf (Policy) Jeff Colandrea (Prod Rationalization) Stephen Payne (Migration)	There will be different Product Leads depending on the release/wave of PAS implementation. For example, Cyber and D&O in Foundation release. • Ensuring that the Product Backlog is visible, transparent & clear to all stakeholders • The Product Owner is one voice for their workstream but may represent multiple stakeholders (Operations, Underwriting, Finance and Claims areas) • Understand and be able to describe the end-to-end solution in a high level, the use cases and related business drivers. • Attend decision making sessions, feeding input regarding the product and its interaction with other components, acting as a point of reference for the product required features and behavior. • Understand business demands and requirements and translate these into solutions that are refined iteratively and present them to the team. • Understand impact of the E2E process on People, Process, Technology and data • Engage with various business areas/initiatives to understand impacts upstream/downstream and within Programme delivery • Escalate risks/issues/decisions/dependencies appropriately as per programme governance • Ensure that the individual scope items meet the “definition of done” before acceptance. Clear definition and alignment of “definition of done” for scope items • Prioritize requirements of the product and make adjustments as needed after each release. • Define the future goal of the product (the ‘product vision’) • Aligns/collaborates with other workstream Product Owners to drive right outcome for programme • Maintain and own the product backlog. • Accepting or rejecting suggested improvements. • Report progress, involvement in governance arrangements. • Accountable for traceability of requirements to business outcomes and test scenarios
Change Management Lead	Susan Mascarenhas	• Responsible for managing all types of change • Evaluates the impact of change • Supports development of communications relevant to change initiatives • Accountable for defining success metrics and measuring performance against these
Quality Assurance Testing Lead	Nabil Ahsraf (Beazley) Alagiya Nambi Rajappan (Hexaware)	• Ultimately accountable for the quality of the overall end to end solution • Provides overall QA oversight for test design and execution, striving for commonality where appropriate • Accountable for defining Program level test strategies and approaches for all test phases • Accountable for planning and oversight of all test phases, including UAT • Provides testing oversight and direction, drives execution of testing strategies and manages testing related objectives and issues across the Program
Business Architecture Lead	Subu Ramasundaram (Business Design Framework) Matt Reynolds Marta Latuszek	• Accountable for developing the business architecture strategy • Applying structured business architecture approach and methodology • Drives and facilitates the right discussions with business leaders to identify business capabilities in relation to current and future business objectives • Responsible for presenting recommendations and solutions clearly and concisely • Accountable for a specific LOB, business pillar or multiple segments, and high level of complexity and attributes
Product Manager	TBD	• Aligning to the ITOM the Product Solutions Manager has accountability for the overall solution across its entire lifecycle working collaboratively with the delivery lead, project teams and stakeholders to ensure Beazley gets maximum value from its technology investment.

KEY ROLES – BEAZLEY

Role	Named Resource	Responsibilities
Enterprise Architects	Dean Johnson	• Understanding business goals and objectives across all our value streams. • Defining the technical, process and data outcomes needed to deliver those objectives. • Establishing strong relationships with internal and external users to promote our target state, standards and governance. • Engaging with decision makers to influence their choices. • Understanding our wider business context and support our architecture, technology strategy and innovation within that context. • Advocating across our change landscape for doing the right thing, doing it well, but doing it to meet business goals. • Being entirely agnostic with regard to individual technologies – as an enterprise architect we need to deliver and re-use a collection of technologies, we can't give everyone their particular favourite. • Working with the Enterprise Architecture team to ensure solutions align with enterprise strategy.
Release Quality	Stephen Payne	• Partnering with Product Manager- to ensure the solution deliveries are ready for release meeting all the required technical and business acceptance standards • Assisting in management of risks, issues and any potential roadblocks • Responsible for resolving contingencies and complicated issues, provide leadership to project teams, and act as a consultant/coach to management • Responsible for DevOps and improvement of workflow
Training / Communication	Vivian Sowho Lead	• Responsible for managing all types of change • Evaluates the impact of change • Supports development of communications relevant to change initiatives • Accountable for defining success metrics and measuring performance against these • Coordinating the development, execution, refinement, and measuring the impact of programme outreach, communications, and knowledge management strategies • Responsible for coordinating development of training / learning materials • Accountable for the organization, coordination of workshops and events • Responsible for supporting communications, knowledge management, and training activities • Help the programme define the benefits and OKR's
Data Lead	Nithya Midde	Accountable & Responsible for • Data and Analytics requirement, vision & strategy and approach • Coordinate the creation of a design for data loads and downstream data use • Coordinate with Program stakeholders upstream and downstream to fulfil data reporting requirements
Migration Lead	Andrew Day	Accountable & Responsible for • Project Management of End-to-End Migration strategy and implementation • Leading teams capable of handling data sourcing, profiling, rectification and reconciliation tasks • Finalizing a migration design and business exception handling
Business Analysts	Manuel Suarez (One more to add TBD)	• Support the Product Owners in ensuring traceability of the overall objectives and requirements for GPAS into OKR's and benefit realisation • Support the Product Owners in ensuring completeness of the epics/stories and acceptance criteria (definition of done/definition of ready) to deliver Beazley benefit throughout the delivery cycles • Support the product owners in the adherence to the agreed business design • Ensure that quality standards are achieved throughout the build lifecycle

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES – BEAZLEY

Role	Named Resource	Responsibilities
Data Analyst	Giovanni D'Auria	• Prepare requirements for the programmes SQL, Analysis Services, Power App and Power BI developers. • Prepare clear and concise documentation demonstrating the flow of insurance data from source systems or manual process into the conformed data contract. • Ensure that mapping tables and transformation logic are valid, complete and accurate. • Facilitate discussions between key stakeholders to ensure that data is correctly extracted, transformed and loaded. • Prepare test objectives and scripts for System and End-users, and undertake testing where necessary. • Document and resolve bugs identified promptly and independently. • Prepare training material to End-users in written and video where necessary.
DevOps	Venkatesh Gunnam	• Application and infrastructure planning & testing including integrations • Maintaining CI/CD pipelines and automation • Guidewire Cloud Console configuration • On-call, incident response and incident management • Monitoring the software development process through its entire lifecycle and ensuring adherence to security standards
Data Modeller	Dinyar Cooper	• Gather and own data modelling requirements from business stakeholders to support the implementation of Guidewire Policy Management solution • Evaluation of existing data systems and working with the development team to create conceptual data models, physical data models and data flows • Review modifications of existing systems for cross-compatibility • Update and optimise local and metadata models • Work closely with central data modelling team to ensure consistency within a domain federated organization.
Infrastructure Lead	Simon Fry	• Responsible for the Implementation of the environments plan to support delivery of the overall GPAS/Billing initiative which will require co-ordination between the Vendor(Guidewire), the chosen Systems Integration partner, Security, Networks, DevOps, Enterprise Architecture and cloud solution architecture • Management of the lower environment's within the agreed budget and Guidewire credits • Liaising with the technical lead to assure adherence to the agreed Software Development Lifecycle • Leading all Infrastructure design workshops • Participating in all design workshops that require input from the Infrastructure team
Test Manager	Alagianambi Rajappan	• Deliver E2E quality assurance strategy including performance and operational testing and associated KPI's(E2E, UAT, NFT,OAT and PEN Testing) • Governance monitoring and reporting for e2e defect management • Overall Test assurance and Governance of all Testing phases

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

KEY ROLES - CAPGEMINI

Role	Named resource	Description	
Delivery Executive	Barry Houston	○ Responsible for overall Services quality and delivery ○ Assist in the resolution of issues and change controls	○ Prepare for and support Steering/Policy Executive Advisory Group Meetings ○ Monitor program progress
Program Director	Max Cartwright	○ Responsible for in-scope Program activities ○ Provide Program status reporting on a regular basis to Beazley Program and Executive Leadership	○ Responsible for overall Services quality and delivery of the Program ○ Responsible for day-to-day management and tracking of the in-scope Program activities
Engagement Manager	Ananda Arasu Ponnaiah	○ Manage the detailed Program plan in collaboration with Beazley Leadership Team ○ Provide Program Status reporting on a regular basis to Beazley Program Leadership	○ Facilitate Decisions, Issues and Risk management across the core program and escalate to Beazley in advance of the materialization of potential risks and issues that may delay the program. ○ Assist the resolution of issues and change controls
India Delivery Executive	Natraj Gudla	○ Manage the detailed Program plan in collaboration with Beazley Leadership Team ○ Provide Program Status reporting on a regular basis to Beazley Program Leadership	○ Facilitate Decisions, Issues and Risk management across the core program and escalate to Beazley in advance of the materialization of potential risks and issues that may delay the program. ○ Assist the resolution of issues and change controls
Product Rationalisation	Peter Dixon Kelly Riesling	○ Provide subject matter specialist advice with regard to overall business requirements and product backlog ○ Provide input on solving business problems within the defined application landscape by working with the business and Technical resources.	○ Coordinate with Functional Lead and Technical architect to help define implementation scope of work.
Enterprise Architect	Brett Fabian-Smith	○ Provide leadership and architectural expertise across a broad set of technologies, including integration & middleware technologies ○ Consult with and advise the Program team on technology and strategic decisions	**Responsible for Capgemini's scope of architecture/design deliverables, for deliveries that Capgemini are responsible for:** • Work with Beazley to define target state technical solutions, identify technology requirements • Gain approval through Design Authority for technical solutions including any security compliance • Identify and monitor architecture & design technical risks and dependencies, work with Beazley to oversee necessary mitigation controls • Delivery of HLD/LLD solution designs for GPAS dependent elements of the overall solution design, supported by Beazley architects • Assurance of HLD and LLD solution designs • Work with Capgemini Release train teams to: • Define architectural backlog and technical guardrails • Provide the necessary Inputs to groom the Backlog and Sprint/PI Planning • Ensure architecture compliance with agreed SDLC and Beazley standards • Manage Version Control of architecture related components • Identify dependencies and risks affecting architecture & design
PolicyCenter Functional Lead	Sherezad Contractor	○ Provide Policy subject matter experience ○ Work with Beazley business leadership to drive overall business requirements	○ Provide leadership and direction for elaboration and RSWs ○ Provide joint review and approval of deliverables
BillingCenter Functional Lead	Sriram Jagannathan	○ Provide Billing subject matter experience ○ Work with Beazley business leadership to drive overall business requirements ○ Provide leadership and direction for elaboration and RSWs	○ Provide joint review and approval of deliverables ○ Lead with the high-level implementation approach for complex functional requirements
PolicyCenter Technical Lead	Vamshi Chennamadhavuni	○ Provide subject matter specialist advice with regard to GW PC ○ Conduct configuration option analysis to support business requirements ○ Provide input on GW PC best practices, constraints, and effort during workshops, including pre-work	○ Provide input on effort and impact associated with potential configurations/customizations ○ Support the Policy Functional Lead with the high-level implementation approach for complex functional requirements
BillingCenter Technical Lead	Sriram Jagannathan	○ Provide subject matter specialist advice with regard to GW BC ○ Conduct configuration option analysis to support business requirements ○ Provide input on GW PC best practices, constraints, and effort during workshops, including pre-work	○ Provide input on effort and impact associated with potential configurations/customizations ○ Support the Policy
Integration Lead	Saharsh Gupta Gourab Marik	○ Provide integration and technical architecture guidance for GW ○ Lead analysis effort of interface specification documents	○ Lead the integration design effort for specified integration points ○ Provide direction and technical guidance

KEY ROLES - GUIDEWIRE

Role	Named resource	Description
Delivery Lead	Frederic Brunner Bruno Fauchere	Responsible for Services Engagement, Consults Team Management, Coordination with SI Partner
Guidewire Cloud Principal	Stephan Benet-Weiler	Is a Point of Contact for Transformation Execution for Customer & SI, Partner, Strategic Guidance, Ensures Adoption of cloud standards, architecture and quality
Technical Account Manager	Joel Dupont	Responsible for Enablement and Planning, Guidance on Cloud Capabilities, Prod and NPE Incident Management

KEY ROLES - HEXAWARE


Role	Named resource	Description
Test Manager	Alagianambi Rajappan	Overall responsibility for Hexaware Test Strategy
Automation Architect	Abdul Wahab	Overall responsibility for Hexaware Test Strategy on Automation
Engagement Lead - TMO	Sunil Kumar Srinivasan	Overall Engagement lead for Beazley and Capgemini from Hexaware
NFT Lead	Ganesh Kamalanathan	Overall NFT strategy and execution

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

GOVERNANCE

The overall success of this engagement will be based on close collaboration between all parties, transparency and fact-based decision making. We will also use this Governance process to keep us all collectively honest and true to the Programme objectives.

Note: Under Review

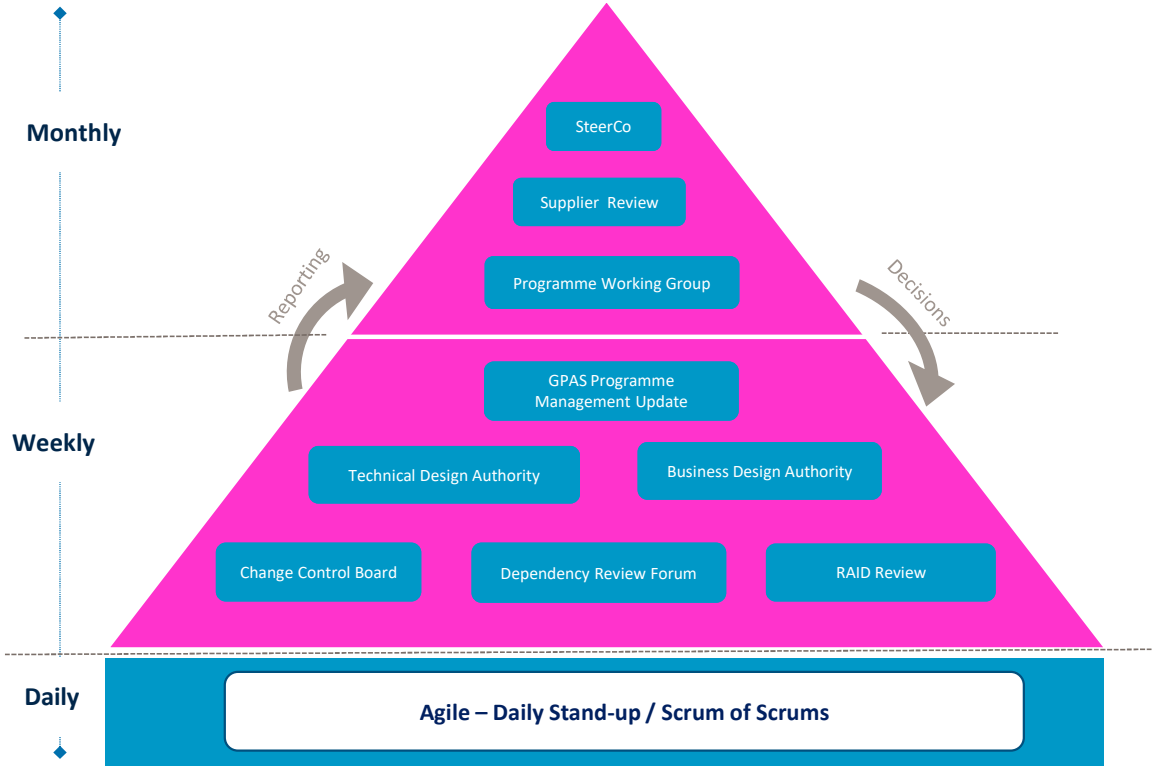

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

PROPOSED PROGRAMME CADENCE

- All Daily stand-ups are ownership of respective Release Train leaders
- All Leadership update Stand-ups (like SOS, Change Board, BDA, TDA etc) are ownership of Beazley to organise, conduct & track. Capgemini to be part of them & provide inputs as per process

Key

Daily | Weekly | Fortnightly | Monthly | Quarterly

*Supplier Review Meeting occurs following Friday of sprint closure

IST	BST	US CTZ	US ETZ	Monday	Tuesday	Wednesday	Thursday	Friday
14:30 - 15:00	9.00 – 9.30	03:00 – 03:30	04:00 – 04:30	Daily Standups	Daily Standups	Daily Standups	Daily Standups	Daily Standups
15:30 – 16:15	10.00 – 10.45	04:00 – 04:45	05:00 – 05:45		• Daily stand ups are within respective Release Train Teams. This includes both Technical & Functional teams from Capgemini in UK & India. • Catch up with Product Owner is planned on a weekly basis to align with UK & US time.			
16:30 – 17:30	11.00 – 12.00	05:00 – 06:00	06:00 – 07:00					
17:30 – 18:30	12.00 – 13.00	06:00 – 07:00	07:00 – 08:00					
18:30 – 19:30	13.00 – 14.00	07:00 – 08:00	08:00 – 09:00					
20:00 – 20:30	14.30 – 15.00	08:30 – 09:00	09:30 – 10:00	Scrum of Scrums	Scrum of Scrums	Scrum of Scrums	Scrum of Scrums	Scrum of Scrums
20:30 – 21:30	15.00 – 16.00	09:00 – 10:00	10:00 – 11:00		• To allow Product Owners to join SoS, it is aligned to US morning. • Capgemini will be represented by Release Train Leads & Functional leads from UK • Release Train Leads and the POs have an opportunity to catch-up on the SoS • Unless required, no India representation available			
21:30 – 22:30	16.00 – 17.00	10:00 – 11:00	11:00 – 12:00					

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

PROPOSED PROGRAMME CADENCE

- All Daily stand-ups are ownership of respective Release Train leaders
- All Leadership update Stand-ups (like SOS, Change Board, BDA, TDA etc) are ownership of Beazley to organise, conduct & track. Capgemini to be part of them & provide inputs as per process

Key

Daily | Weekly | Fortnightly | Monthly | Quarterly

*Supplier Review Meeting occurs following Friday of sprint closure

IST	BST	US CTZ	US ETZ	Monday	Tuesday	Wednesday	Thursday	Friday
14:00- 14:30	8.30 – 09.00	02:30 – 03:00	03:30 – 04:00	Cap/BZ Joint Stand-up	Cap/BZ Joint Stand-up	Cap/BZ Joint Stand-up	Cap/BZ Joint Stand-up	Cap/BZ Joint Stand-up
14:30 - 15:00	9.00 – 9.30	03:00 – 03:30	04:00 – 04:30	• First hr catch-up with Capgemini RTEs to review SoS actions as necessary • RTE, Beazley and Capgemini Program Managers				Program Management Update
15:30 – 16:15	10.00 – 10.45	04:00 – 04:45	05:00 – 05:45			Program Working Group		Supplier Review*
17:30 – 18:30	12.00 – 13.00	06:00 – 07:00	07:00 – 08:00					
18:30 – 19:30	13.00 – 14.00	07:00 – 08:00	08:00 – 09:00					
19:30 – 20:30	14.00 – 15.00	08:00 – 09:00	09:00 – 10:00	Dependency Forum & PMO RAID Review		Change Board	Technical Design Authority	Business Design Authority
20:30 – 21:30	15.00 – 16.00	09:00 – 10:00	10:00 – 11:00			Steer Co	• The TDA and BDA forums are suggested to be GPAS & Billing Program specific to low level design decisions • Those impacting systems outside of GPAS & Billing must be taken up at the wider Modernization authorities (existing forums)	
21:30 – 22:30	16.00 – 17.00	10:00 – 11:00	11:00 – 12:00					

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |


PROPOSED ROLES & CEREMONIES MATRIX

Roles & Ceremonies	Daily Standup (Release train)	Daily Scrum of Scrums (RT Leads)	Cap/BZ Joint Stand-up	Dependency Forum	PMO RAID Review	Supplier Review Meeting	Program Management update	Change Board	Business Design Authority	Technical Design Authority	Program Working Group	Steer Co
Business Sponsors /Delivery Exec									x			x
Programme Director		x	x	x	x	x	x	x	x		x	x
Delivery Leads		x	x	x	x	x	x	x	x	x	x	x
Product Owner	x	x		x	x	x	x	x	x			x
Functional Leads	x	x	x	x	x		x	x	x		X	
Subject Matter Experts		x					x	x	x	x		
Architects	x	x		x	x		x		x	x	x	
Platform Owners		x		x	x	x	x	x	x	x		x
Technical Leads	x	x	x	x	x		x	x		x		
Test Managers	x	x	x	x	x		x	x				
Development Team	x						x					
Product Rationalization Team	x	x		x	x		x		x	x		x
Procurement Team		x		x	x	x	x					
DevOps Team	x	x		x	x		x			x		
PMO Team		x			x	x	x				x	

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

ESCALATION PROCESS

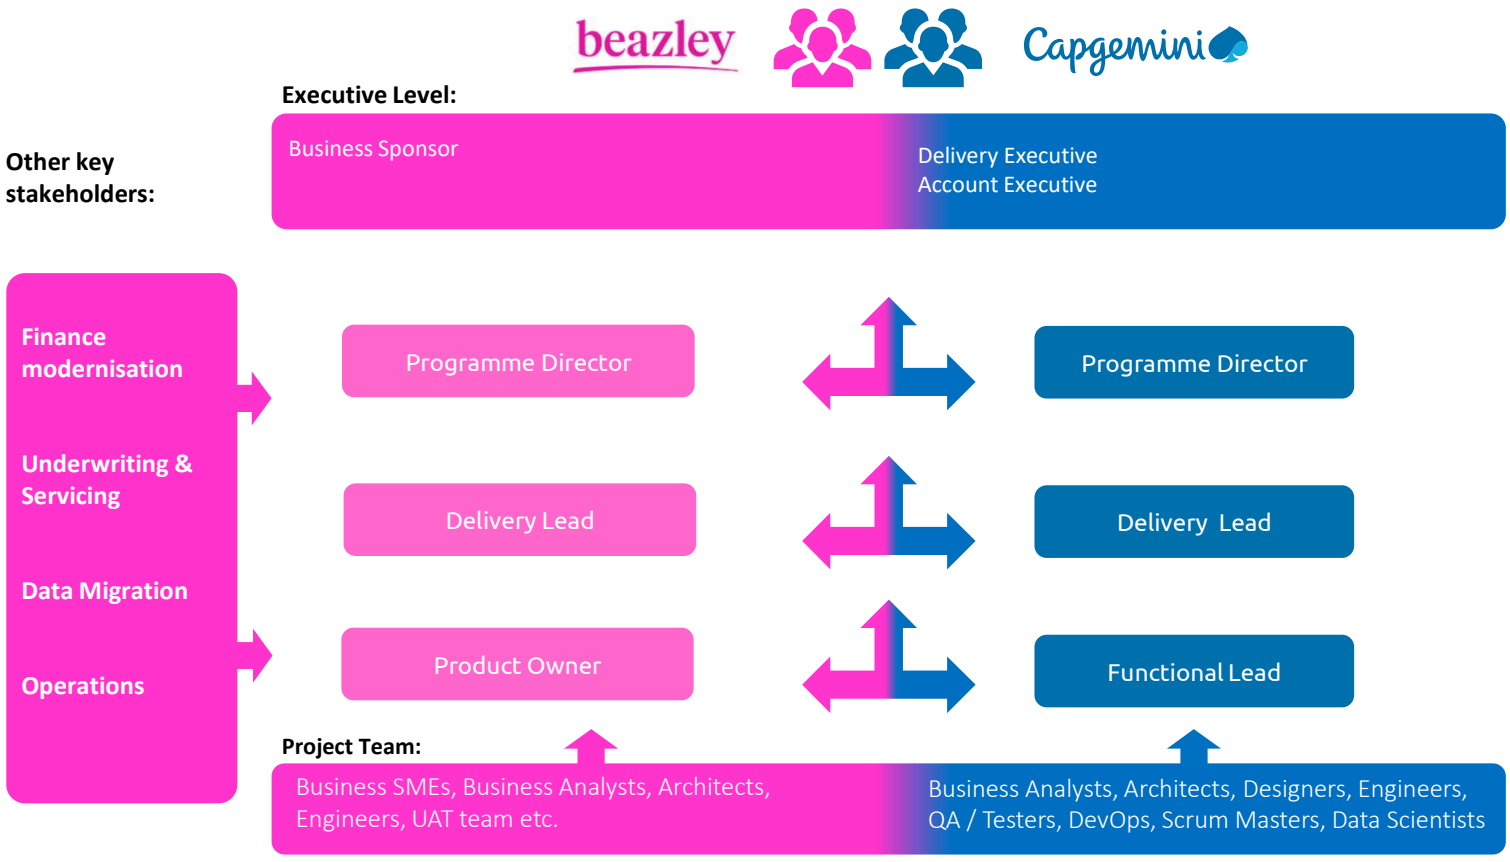

Escalation Etiquette:

Escalations are done jointly from Capgemini and Beazley representatives from one level to Capgemini & Beazley representatives at the next level up.


Prior to escalation, representatives will work together to:

1. Agree what they agree on
2. Agree what they disagree on
3. Prepare for the escalation, making clear:
   - The problem statement
   - The options for resolution and their pros and cons
   - The decision(s) and / or action(s) required
   - The date required by
   - The impact of doing nothing / missing the date

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

CHANGE CONTROL

Controlling change via an agreed process that acknowledges it is needed but manages its impact for the good of delivery is key to the success of this largescale programme delivery.

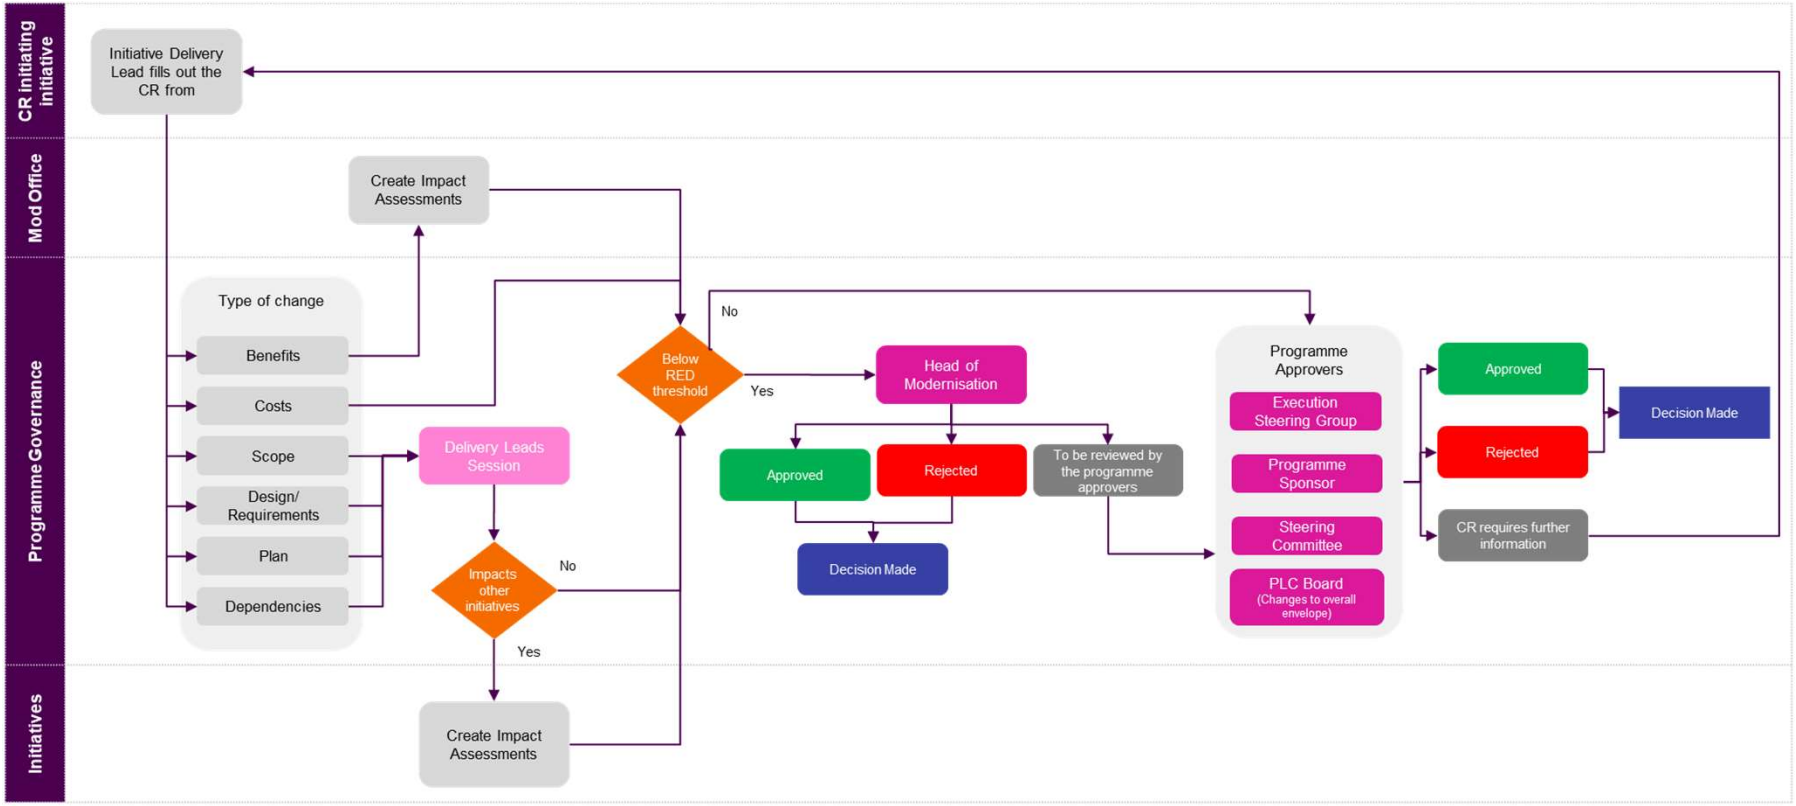

Modernisation Programme - Change Control Process

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

CHANGE CONTROL (THRESHOLD & RELEVANT ACTIONS)

Change Type	Green Threshold	Amber Threshold	Red Threshold
Scope i.e Products, LoBs, features	Scope change is **minor** and does **not** have a costs or plan impact **Action**: Inform Head of Modernisation via the Delivery Lead meeting and update key documentation, including the charter using the relevant version control.	Scope change is **medium**. Costs and/or Plan impact is Amber. **Action**: Fill out the Change Request Form and follow the CR process.	Scope change is **high**. costs and/or Plan impact is Red. **Action**: Fill out the Change Request Form and follow the CR process.
Requirements/Design	Requirements/Design is **minor** and does **not** have a costs or plan impact **Action**: Inform Tim Kelly via the Execution Steering Group meeting and update key documentation, including the charter and the solution design document using the relevant version control.	Scope change is **medium**. costs and/or Plan impact is Amber. **Action**: Fill out the Change Request Form and follow the CR process.	Scope change is **high**. costs and/or Plan impact is Red. **Action**: Fill out the Change Request Form and follow the CR process.
Plan: level 0 or level 1 milestones	**<3 weeks delay** **Action**: Flag delay in the status report i.e milestone is off-track and advise the estimated date at the Delivery Leads meeting.	**3 - 8 weeks delay** **Action**: Fill out the Change Request Form and follow the CR process.	**>8 weeks delay** **Action**: Fill out the Change Request Form and follow the CR process.
Dependencies	**<3 weeks delay** Assisting Dependency will push out Driving Dependency Delivery Date by less than 3 weeks **Action**: Flag delay in the status report i.e milestone is off-track and advise the estimated date at the Delivery Leads meeting.	**3 - 8 weeks delay** ***Action:*** Driving Initiative completes Change Request form and references change is driven by Assisting Initiative	**>8 weeks delay** ***Action:*** Driving Initiative completes Change Request form and references change is driven by Assisting Initiative
Costs (inc resourcing)	**<2.5%** **Action**: Update the forecast, email Modernisation Office and fill out the variance report.	**2.5% - 5%** **Action**: Fill out the Change Request Form and follow the CR process.	**>5%** **Action**: Fill out the Change Request Form and follow the CR process.
Benefits & OKRs	**<$100k and/or <3 months delay** If there is a change to the benefit ($ value) or OKRs baselined by the initiative by less than $100k **Action**: Inform Head of Modernisation via the Delivery Lead meeting and update key documentation, including the charter using the relevant version control.	**$100k - $250k and/or 3- 5 months delay** If there is a change to the benefit ($ value) or OKRs baselined by the initiative by $100k and $250k. **Action**: Fill out the Change Request Form and follow the CR process.	**>$250k and/or >6 months delay** If there is a change to the benefit ($ value) or OKRs baselined by the initiative by over $250k. **Action**: Fill out the Change Request Form and follow the CR process.

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

RAID MANAGEMENT

We will identify, document, and review (fortnightly at least) Risks, Assumptions, Issues and Dependencies (RAID), which we will store in the overall programme RAID log on the Beazley network to ensure one version of the truth and to maintain full transparency. This will cover the following:

- **Risks** (and their mitigation actions, owners and due dates).
- **Assumptions** (and validation actions, owners and due dates).
- **Issues** (and resolution actions, owners and due dates). Note: We also strictly use the daily Scrum of Scrum (SOS) calls to log all blockers (on JIRA for visibility and to drive resolution) to give the necessary visibility across the programme in a bid to drive action.
- **Dependencies** upcoming and – if they exist – any overdue dependencies. Based on our experience, we consider strong dependency management a critical success factor, and so we will be implementing this throughout the Inception phase and beyond.

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

TOOLS FOR INCEPTION

Inception

Technical and Collaboration Tools

- VDIs and software installations
- Outlook, MS Teams
- Project planner
- Microsoft Office tools- word, excel, ppt
- Guidewire sandbox access
- JIRA
- Confluence
- Microsoft Visio/Biz Design/Gliffy
- Guidewire Cloud Console access

<----->

- Lewis Claxton (Beazley PMO)
- Raghava Kanduru (Capgemini PMO)


Managed by

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |


JIRA SETUP

Process to setup projects in Jira with one scheme configuration and upload prioritized backlog during inception phase


Step1 – Create one Schema Configuration for all GPAS projects

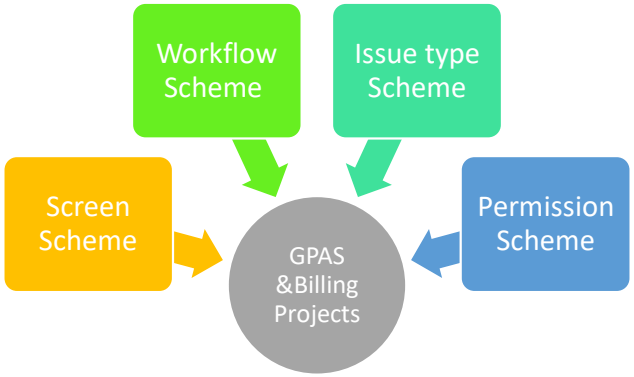

Step2 – Create Projects and set one scheme configuration

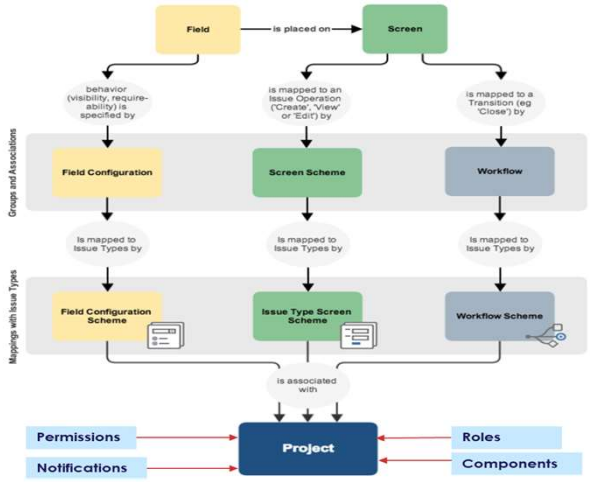

Step3 – Upload the prioritized backlog to GPAS projects

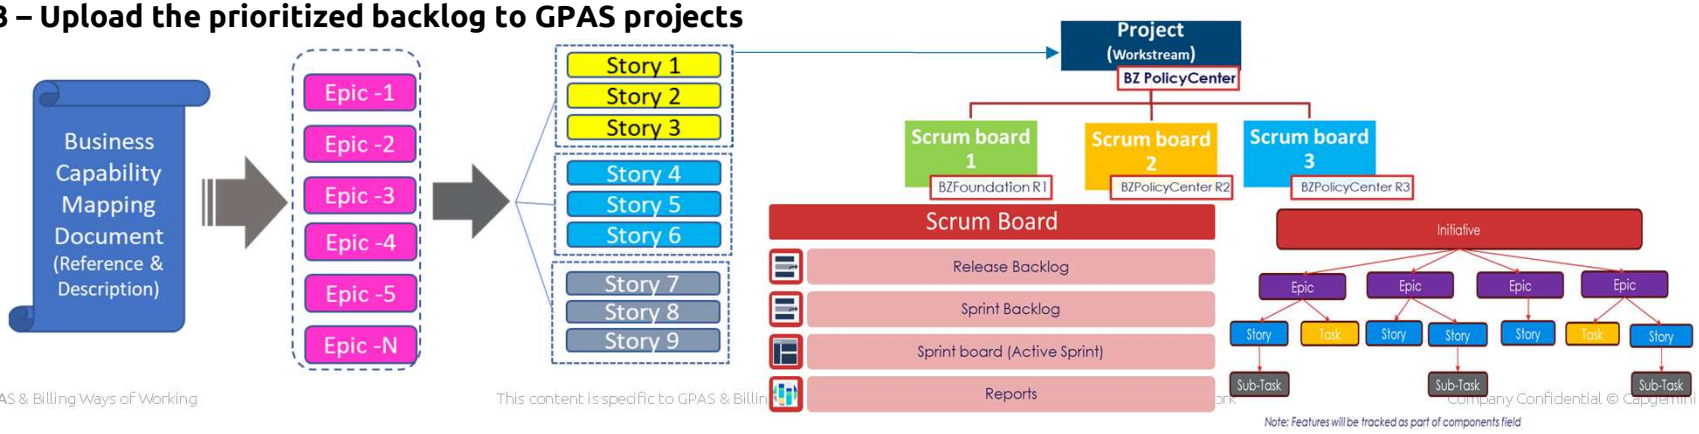

This content is specific to GPAS & Billing
Company Confidential © Capgemini 2024. All rights reserved |

BUILD PHASE UPDATES

1. Sprint construct, ceremonies, reporting
2. Sprint Events and RACI
3. Approval process and SLA
4. User story management – illustration of possible scenarios
5. Key Activities and deliverables – Design & Build
6. A day in a life – Sprint development
7. Definition of Ready & Definition of Done for HLD & LLD, User Stories & Sprint
8. Guidewire – 3 way collaboration, Cloud assessment, Code Branching
9. Testing – Scope, Strategy, Deliverables and RACI, Risks/Issues
10. Third party management & Expectations
11. Metrics

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Sprint Construct
Sprint Ceremonies
Sprint Reporting

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Teams work in 4-week Sprints with Key Events & Activities

User Stories tagged to the Sprint and meeting Definition of Ready identified for planning

A Sprint Planning & Kickoff

Plan what stories the team will develop in the sprint; the Team decides how much to pull and how they will achieve the goal

B Team Stand-up

Daily stand-up to improve coordination through a quick check-in on progress, agreeing action plans for the day and surfacing obstacles.

Daily

Time-boxed working (4-week sprint)

C Scrum of Scrums

Use the Scrum of Scrum platform to get help by highlight cross stream dependencies or other external factors impacting team's progress

Backlog refinement

For any potential missed commitments having an impact on overall Release plan, Continuous focus on Backlog to refinement is critical

D Sprint Demo & Incremental Feature Demo

All user stories are demoed to Business SME for feedback and sign off. An incremental feature demo is done across sprints

E Retrospective

Team meeting to review the completed Sprint to capture learnings and agree plan of action for improvements in future sprints

Future Sprints


Working, tested solutions created based on the Sprint plan

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |


Sprint Structure for Foundation Release

Focusing on execution of current sprint while doing elaboration for next sprint




Elaboration For Sprint 1

Last week has PREP meetings for SPRINT 2 ELABORATION




Development & Testing For Sprint 1



Elaboration For Sprint 2

Last week has PREP meetings for SPRINT 3 ELABORATION



Development For Sprint 2



Elaboration For Sprint 3

Last week has PREP meetings for SPRINT 4 ELABORATION


A sprint is 4 weeks in duration


Each **4 weeks** duration does execution of current sprint while doing elaboration for next sprint

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

Sprint in action on a Timeline

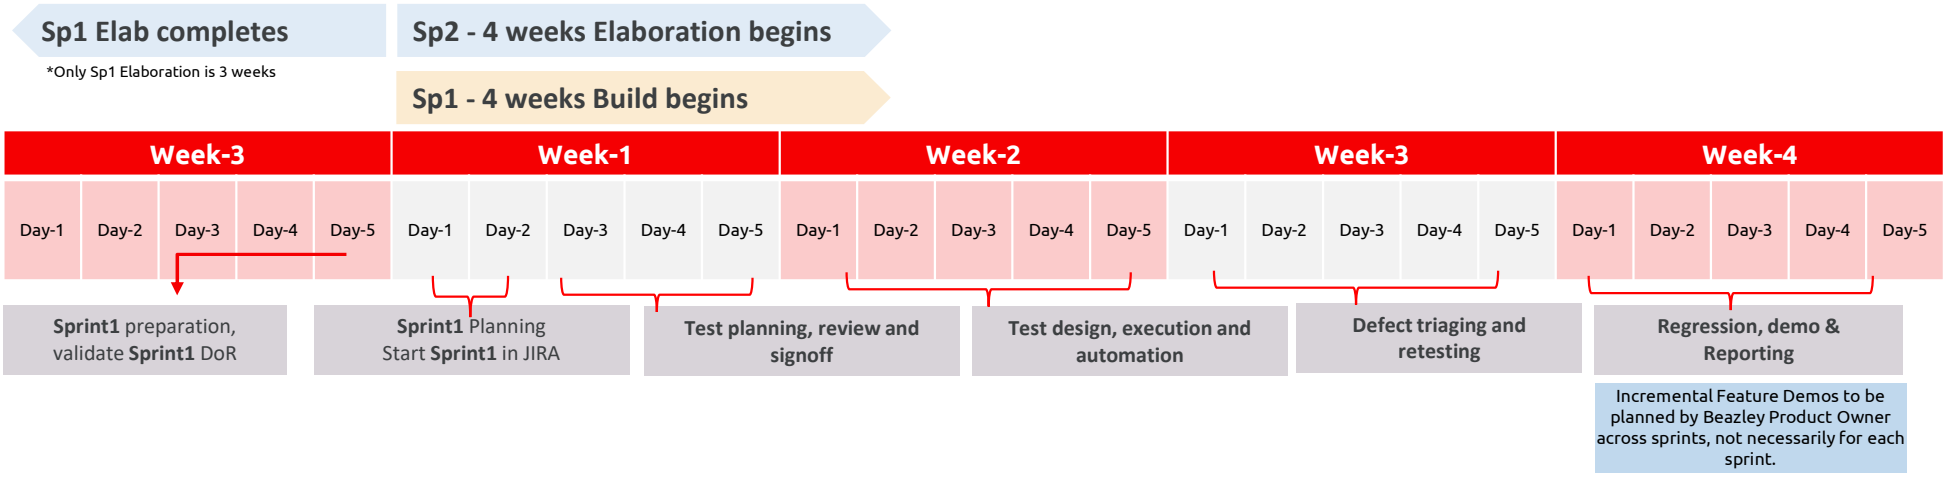

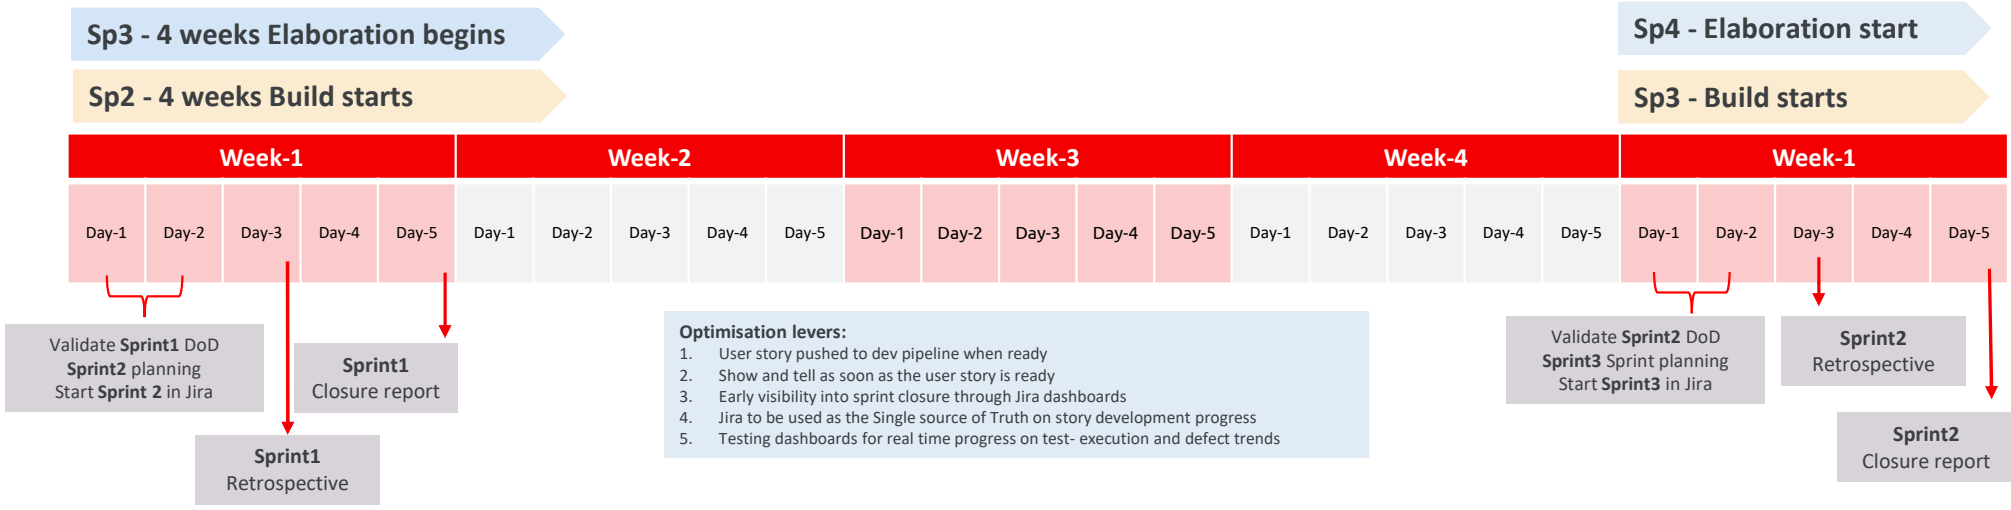

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |


Standard Development team composition

Each Release Train team – Policy, Billing, Integration would consist of cross functional skill

- Release Train lead/Technical lead
- Developers
- Testers

Partial availability of the following groups to help query resolution OR address requirement or design changes

- Business Analysts (Capgemini)
- Architects (Capgeminii)
- Business PO or SME (Beazley)
- DevOps (Beazley)

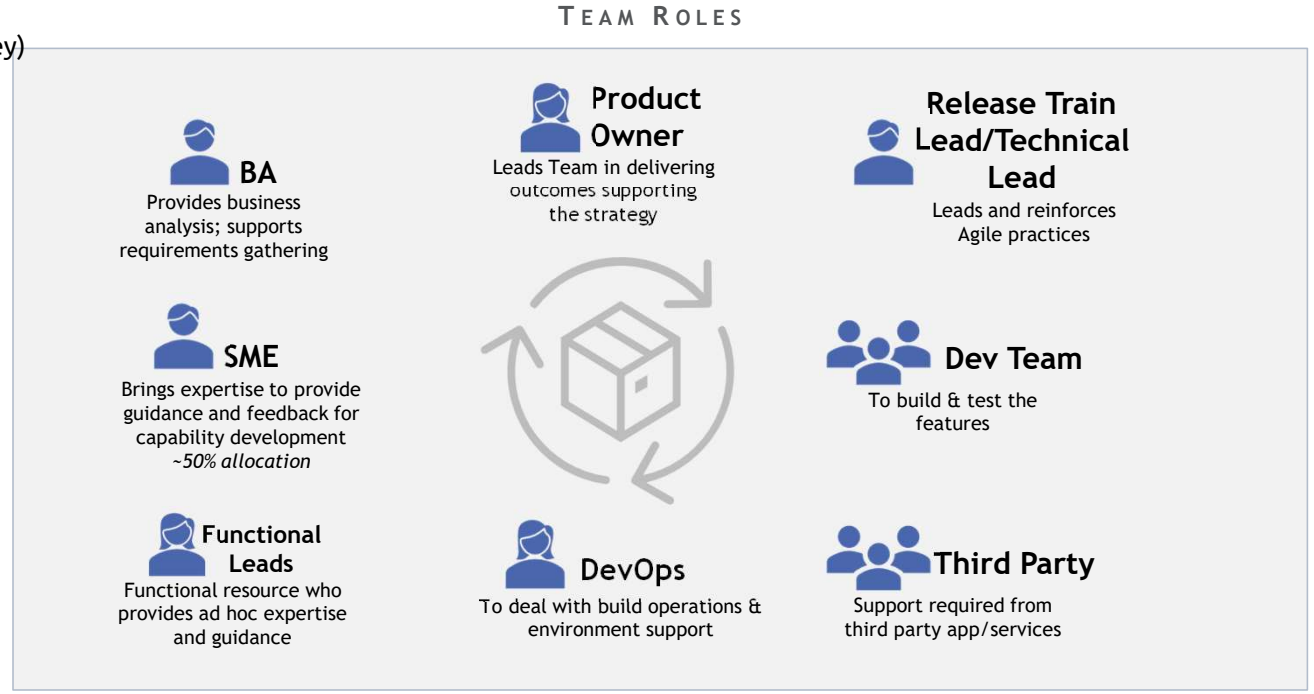

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

USER STORY

Clear User Story standards drive quality delivery

User story structure


User Role
User action
Business Value
Acceptance Criteria

What a user story must be

Independent
Negotiable
Valuable
Estimable
Small
Testable

User story standards must

Follow the INVEST standard
Identify correct personas
Have a clear goal/outcome
Be explicit on pathway/flow – Given this, Then …, So that…
Meet Programme Definition of Ready

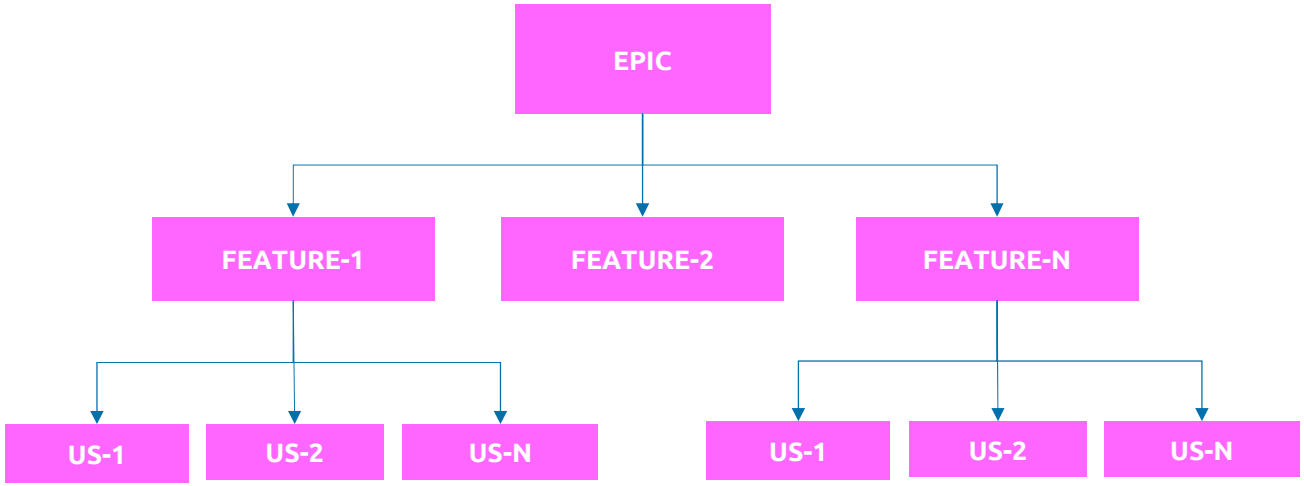

USER STORY TYPEs:


- **A functional user story**
  - A story where you have a user role, action and an outcome
  - Typically associated with user facing screens
  - Very closely associated to the product behaviour

- **A technical user story**
  - Usually linked to a front end functional story
  - Has a technical flow in the background of a functional user story
  - Depends on team composition if you have separate integration team
  - Applies to data and integration layer types of work

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

USER STORY Elaboration Cycle

Each User story through the elaboration phase goes through key phases of requirement capturing, aligning dependencies, conformance, drafting and a final approval

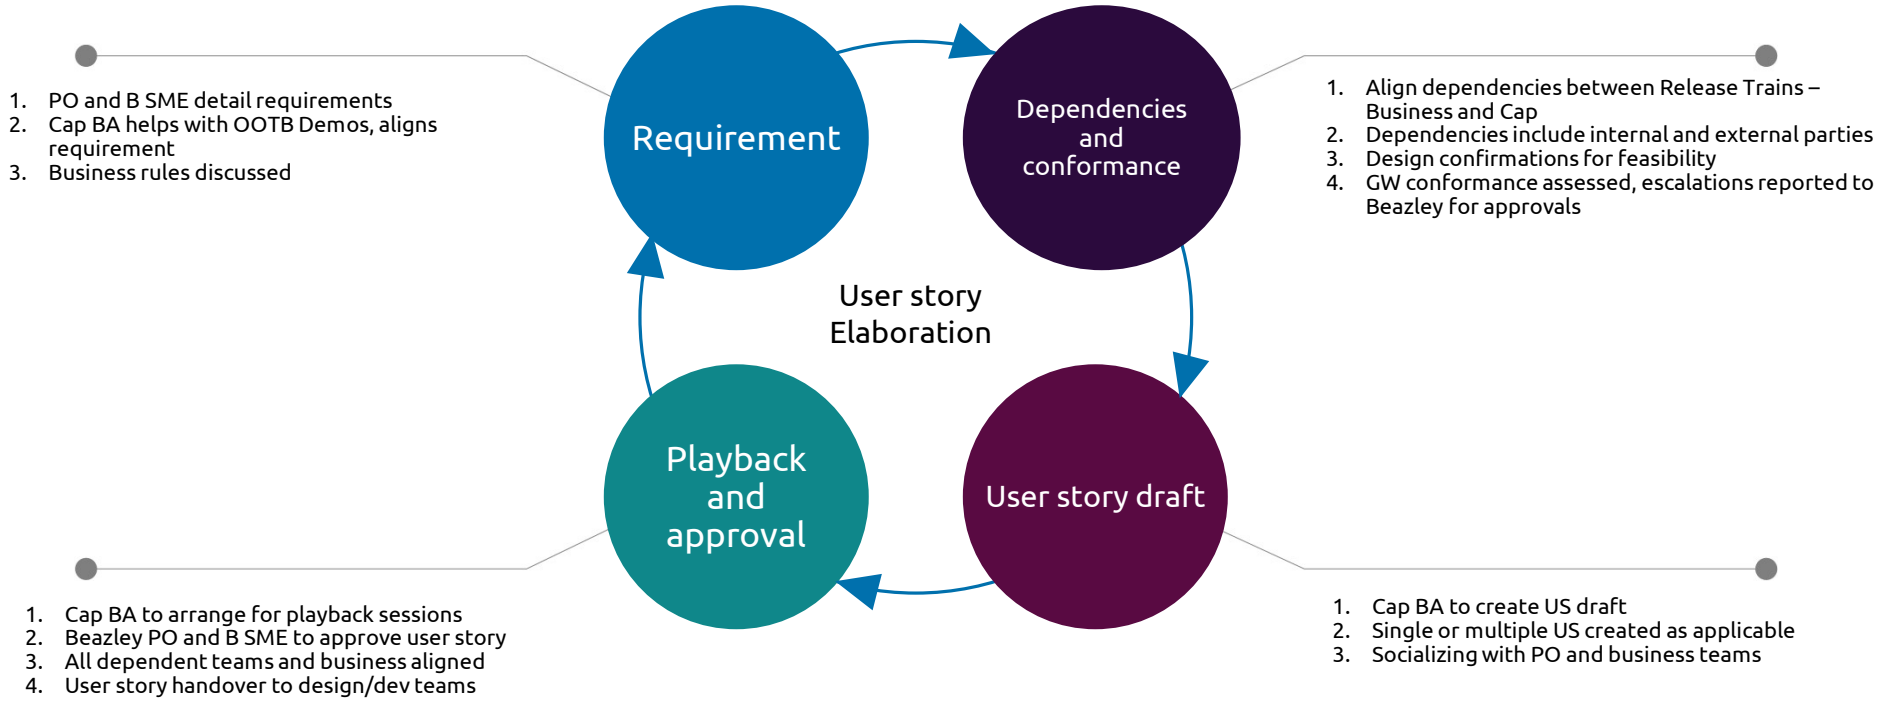

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Sprint Events and RACI

Tasks	Accountable	Accountable Team	Supporting Team	SLA/Expectations
Backlog requirements elaboration	Beazley	Beazley PO, Beazley B SME	Capgemini BA	
Requirements conformance to GW product specs	Beazley	Beazley PO, Beazley B SME	Capgemini BA, Capgemini Technical team	Capgemini BA to escalate to the PO/Business SME if requirement are deviating from product conformance (ex <90%). This happens immediately during the Sprint elaboration sessions much before development begins
Requirements clarification for dependent systems	Beazley	Beazley PO, Beazley B SME	Capgemini BA, Capgemini Technical team	All dependent RT expectations are aligned by the Beazley PO
Business validation definitions	Beazley	Beazley PO, Beazley B SME	Capgemini BA	
Acceptance criteria definition	Beazley	Beazley PO, Beazley B SME	Capgemini BA	
Business Process Maps traceability to GPAS & Billing Backlog Items	Beazley	Beazley PO, Beazley SME	Capgemini BA	L4 Process Maps created by Beazley to be mapped to GPAS & Billing backlog items at Epic/Feature level by Beazley
User story creation	Capgemini	Capgemini BA	Beazley PO, Beazley B SME	
User story creation in JIRA	Capgemini	Capgemini BA	Capgemini RTL, Technical SME, Capgemini BA	
User story sign-off	Beazley	Beazley PO, Beazley B SME	Capgemini BA	All user stories to be signed off by PO within 2 days after issuance
Sprint planning	Capgemini	Capgemini Release Train lead	Beazley PO, Beazley B SME(s)	All Beazley managed Release Train leads, Beazley PO, Beazley Business SME
Playback sessions	Capgemini	Capgemini BA	Beazley PO, Beazley B SME	All Beazley managed Release Train leads, Beazley PO, Beazley Business SME
Backlog adjustments	Capgemini and Beazley	Capgemini PO, RTL Beazley PO	Capgemini Technical team	

Sprint Events and RACI

Tasks	Accountable	Accountable Team	Supporting Team	SLA/Expectations
Validate Sprint Definition of Ready	Capgemini	Capgemini RTL, Capgemini BA	Beazley PO, Beazley B SME	
Validate Sprint Definition of Done and Sprint acceptance	Beazley	Beazley PO, Beazley Programme Manager	Capgemini RTL, Capgemini Technical SME	Beazley Programme team to sign off Sprint Closure report issued by Capgemini within 24 hours after submission 1. A summary of the Sprint DoD status supported by JIRA reports (specifics to be agreed) 2. Time to issue report : Up to One week after Sprint completion
Validate User story definition of ready	Capgemini	Capgemini RTL, Capgemini BA	Beazley PO, Beazley B SME	
Validate User story definition of done	Capgemini	Capgemini RTL, Capgemini BA	Beazley PO, Beazley B SME	
User story show and tell (Demo)	Capgemini	Capgemini RTL, Capgemini BA	Beazley PO, Beazley B SME	Beazley to sign off the stories in JIRA within 24 hours
Incremental Feature Demo	Beazley	Business Product Owners, Business SME	Capgemini BA	Beazley to decide on the timing for an incremental feature demo
JIRA reports for all DoD, DoR	Capgemini	Capgemini JIRA admin		
Sprint start and closure in JIRA	Capgemini	Capgemini RTL, Capgemini RTL, Capgemini JIRA admin	Beazley PO, Beazley B SME, Beazley Programme team	Beazley Programme team to sign off the JIRA report for Sprint start and closure
Technical tasks creation in JIRA	Capgemini	Capgemini Technical leads, RTL		
Updates to JIRA user story progression (dev, test etc)	Capgemini	Capgemini RTL, Capgemini Technical Leads		
Sprint retrospective	Capgemini	Capgemini RTL	Beazley PO, Beazley B SME	

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Traceability from Business Outcomes through to a Test case

Beazley Business Outcomes requirements in GPAS & Billing

- Primary Responsibility lies with Business Design Team to generate the L4 Process Maps that link back to a Business Outcome

Business Process Maps (L4)

- Beazley to map the L4 Process maps to an Epic or Feature (proposed using unique ids for each process map)
- All Epics & Features are uploaded to JIRA

Epic and Feature elaborated in Product Backlog

- GPAS and Billing Product backlog created as Inception phase outcome – lists Epics, Features and User stories
- All Epics, Features and User stories are uploaded to JIRA


User stories for each Epic and Feature

- In the build phase, all test scenarios and test cases created are linked back to user stories in JIRA


Test scenarios and Test Cases for each User story

Illustrative scenario – BillingCenter Delinquency – Business Process Maps to Guidewire Backlog during Inception


L4 Process Maps for Delinquency with different system flows between PAS and Billing



Business Requirements Backlog created by Business SME/PO that becomes input to Inception workshops

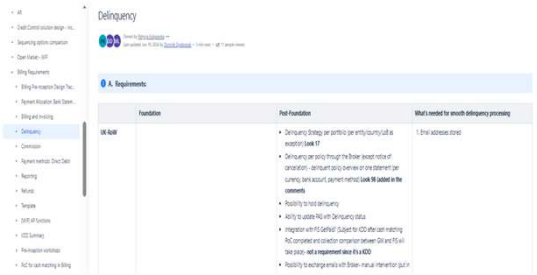

BillingCenter Guidewire Backlog for Deliquency derived with Epics/Features and User stories

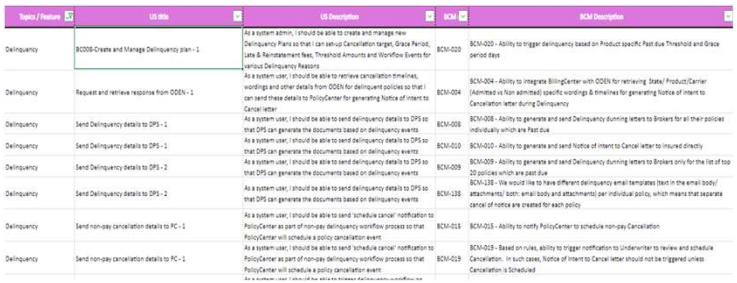

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

Scrum of Scrums (SoS)

What is Scrum of Scrums (SoS)?

A stand-up which is one level above the daily team Scrum stand-ups. SoS is essential in Large programs for leadership to get first-hand view of current impediments or potential future ones that impact the progress teams can make on day-to-day basis. Program leadership is expected to unblock issues for the team to proceed. Example of SoS entries can be - risk of missing a dependency, or a missed dependency, requested test data not being available as per SLA, Demo sign-off pending etc

What is the frequency of SoS?

Ideal is daily at least for initial sprints and later can be reviewed to reduce it to 2 or 3 times a week.

Who are invited to the Scrum of Scrums?

- Release Train Engineers from all Release Train Teams (Cap, Beazley and Hexaware) – ex: Policy, Billing, Migration, Infra, Testing etc
- Program Directors from Capgemini & Beazley
- Program and Delivery Managers from Capgemini & Beazley
- Functional Heads and Business Product Owner(s)

What will be discussed in Scrum of Scrums?

- A JIRA board will be used to log all items eligible for Scrum of Scrum meeting
- Check progress on any unresolved SoS entries
- Review new entries
- Review active risks/issues that have potential impacts to Sprint velocity or the overall Release Goal

Where to raise/create SOS tickets?

Release Train Leads must use JIRA SoS board - "*GPAS & Billing Scrum of Scrum*" to log entries with complete details and assigned them to respective dependent teams/representative

Who runs the Scrum of Scrums:

Beazley is expected to set-up, run and govern the SoS meetings

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Retrospective

Release Train Sprint & Program Sprint Retrospective session are conducted at end of sprint to inspect, adapt & identify next sprint improvements

Release Train Sprint Retrospective



Who runs
- Release Train Lead

Participants
- Product Owner/Business SME
- Development Teams
- Testing Teams

Agenda -
- Sprint team to review what went well & what can improve
- Identify & agree areas of improvement needed going forward
- Agree on applicable action items & mechanism to track

Program Sprint Retrospective



Who runs
- Beazley Program Manager

Participants
- Product Owners
- All Release Train Engineers (RTE)
- Program & Delivery Managers (Cap & BZ)
- Program Directors (Cap & BZ)

Agenda -
- All RTE share the release train sprint retrospective updates
- Identify & agree areas of improvement needed going forward
- Agree on applicable action items & mechanism to track

Note: All retrospective decks are stored in confluence

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

User Story management

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

User story management


Key Scenarios:

1. Elaboration is complete in one sprint, development takes multiple sprints
2. User story development planned for a sprint does not complete within the sprint timeline
3. One Epic requirement developed across multiple Release Trains in the same sprint
4. Elaboration is across multiple sprints and development is across multiple sprints
5. User story Elaboration does not meet definition of ready for sprint development

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Scenario 1 – Imburse - Payment Integration


Elaboration in one sprint, implementation in multiple sprints

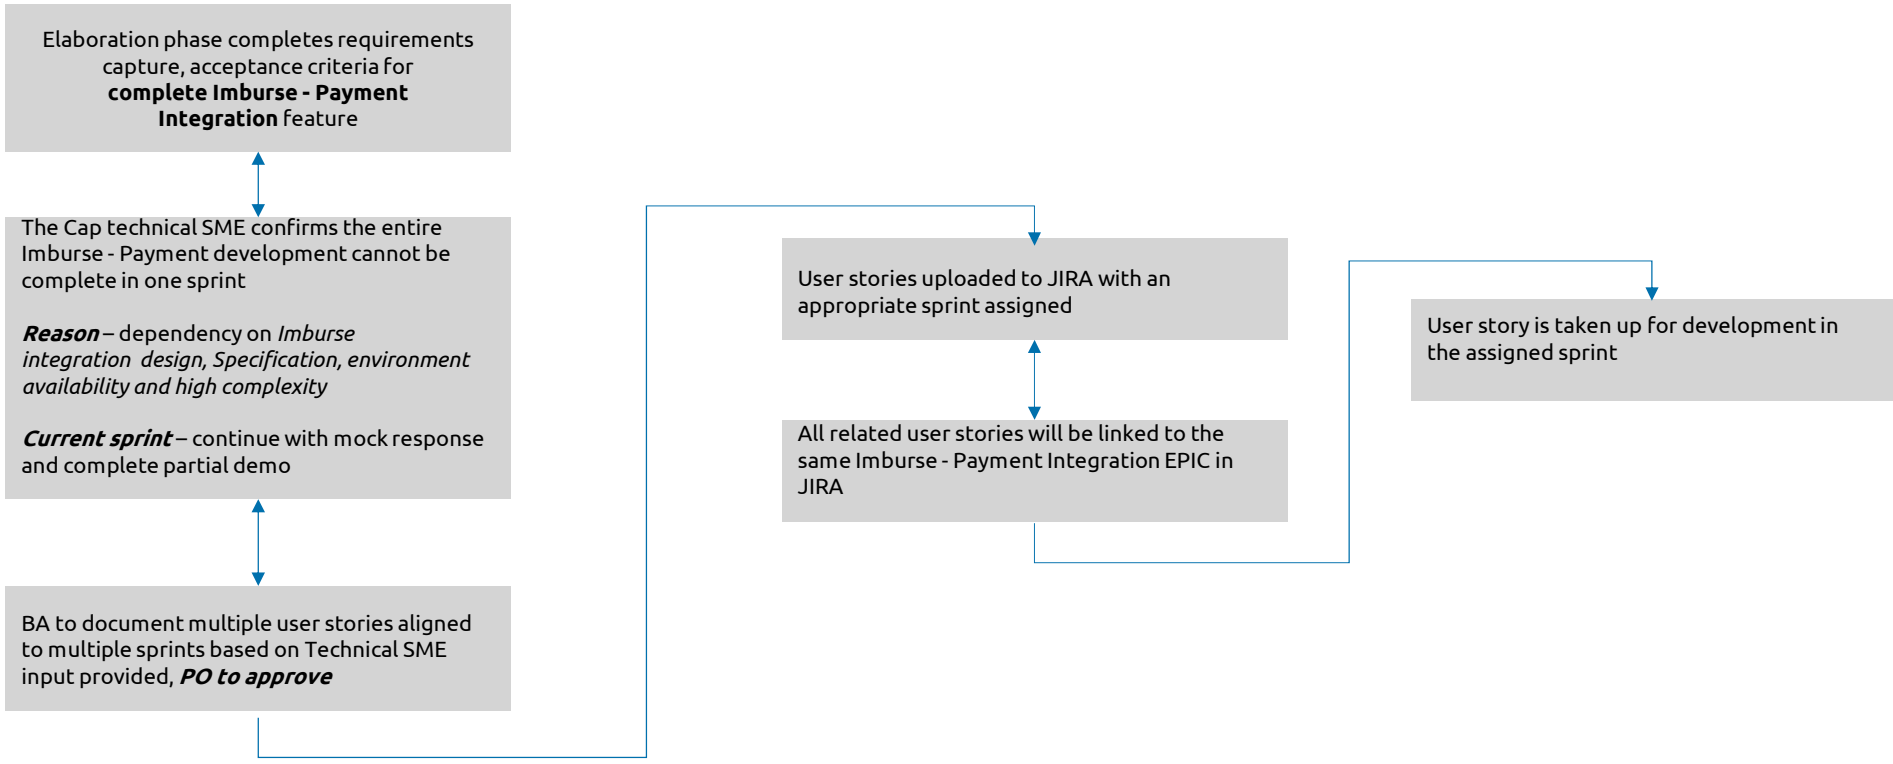

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Scenario 2 – User story spill over

User story planned for a sprint does not complete within the sprint timeline

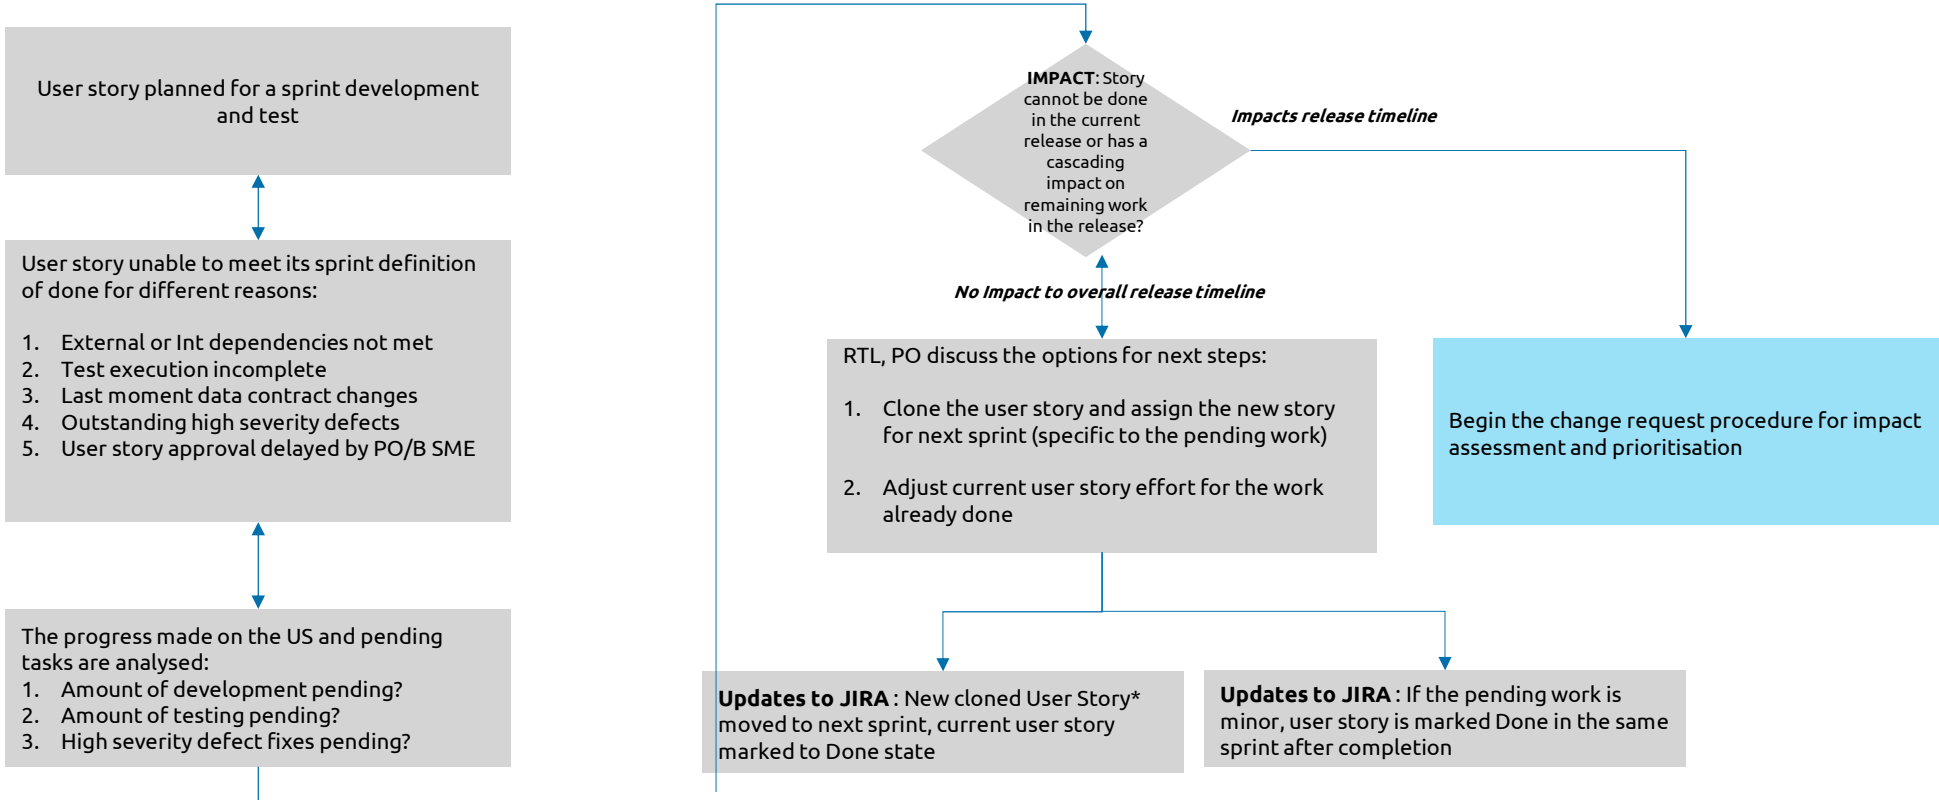


*Cloned story will be automatically linked to the existing story. The cloned story will have pending efforts from existing story as its story points, (Ex- if existing story is 13 SPs after the split, new cloned SPs will be 5 SPs & existing story will be changed to 8 SPs)

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Scenario 3 – User story in multiple streams – Rating Service


One Epic requirement developed across multiple Release Trains in the same sprint

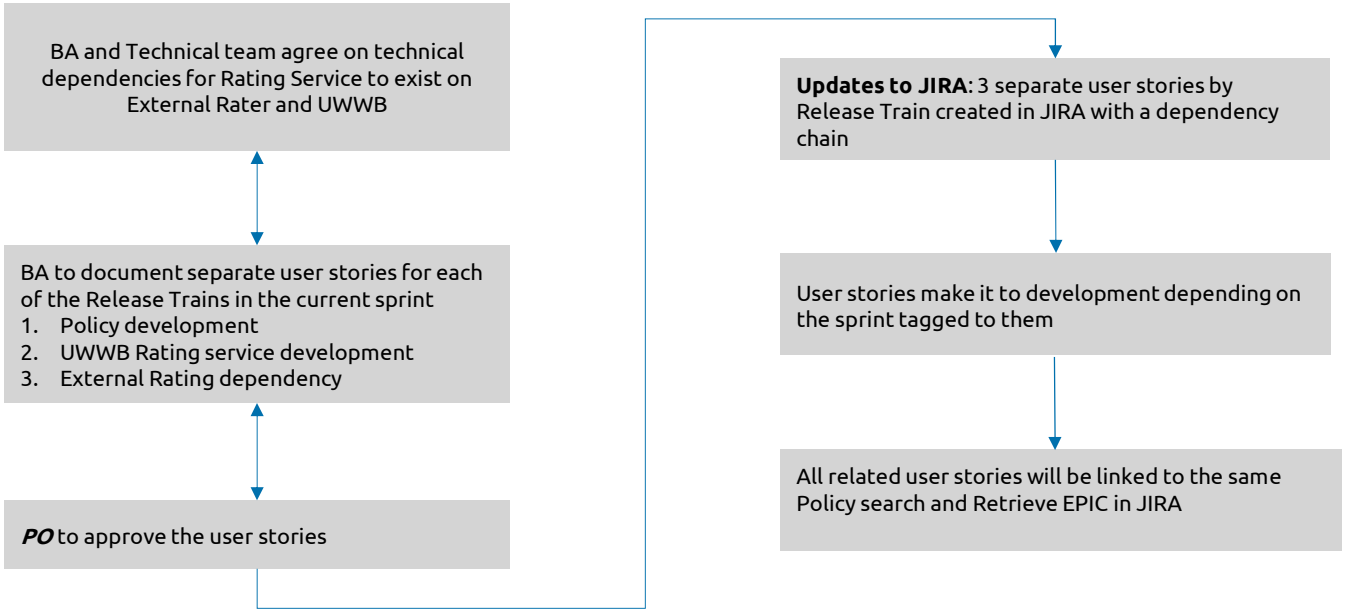

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Scenario 4 – Complex Integrations


Elaboration done in multiple sprints and implementation done in multiple sprints

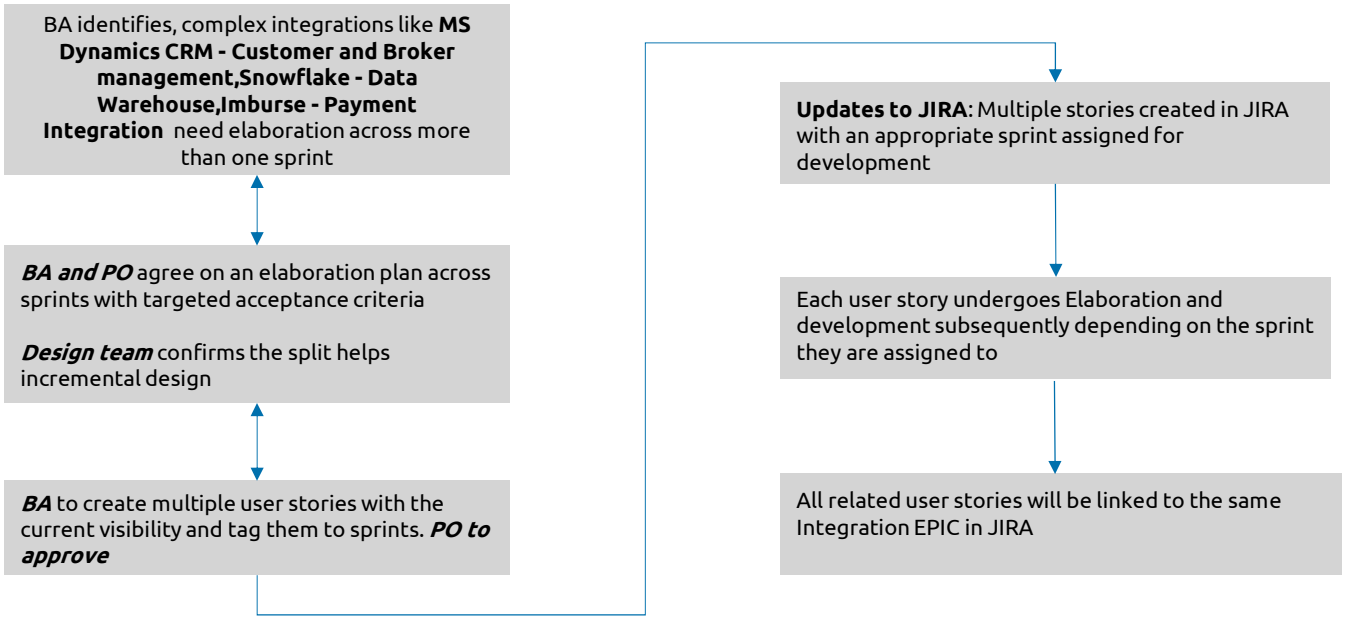

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Scenario 5 – User story does not meet DoR, DoD

User story fail to meet their definition of done or ready at elaboration or execution phases

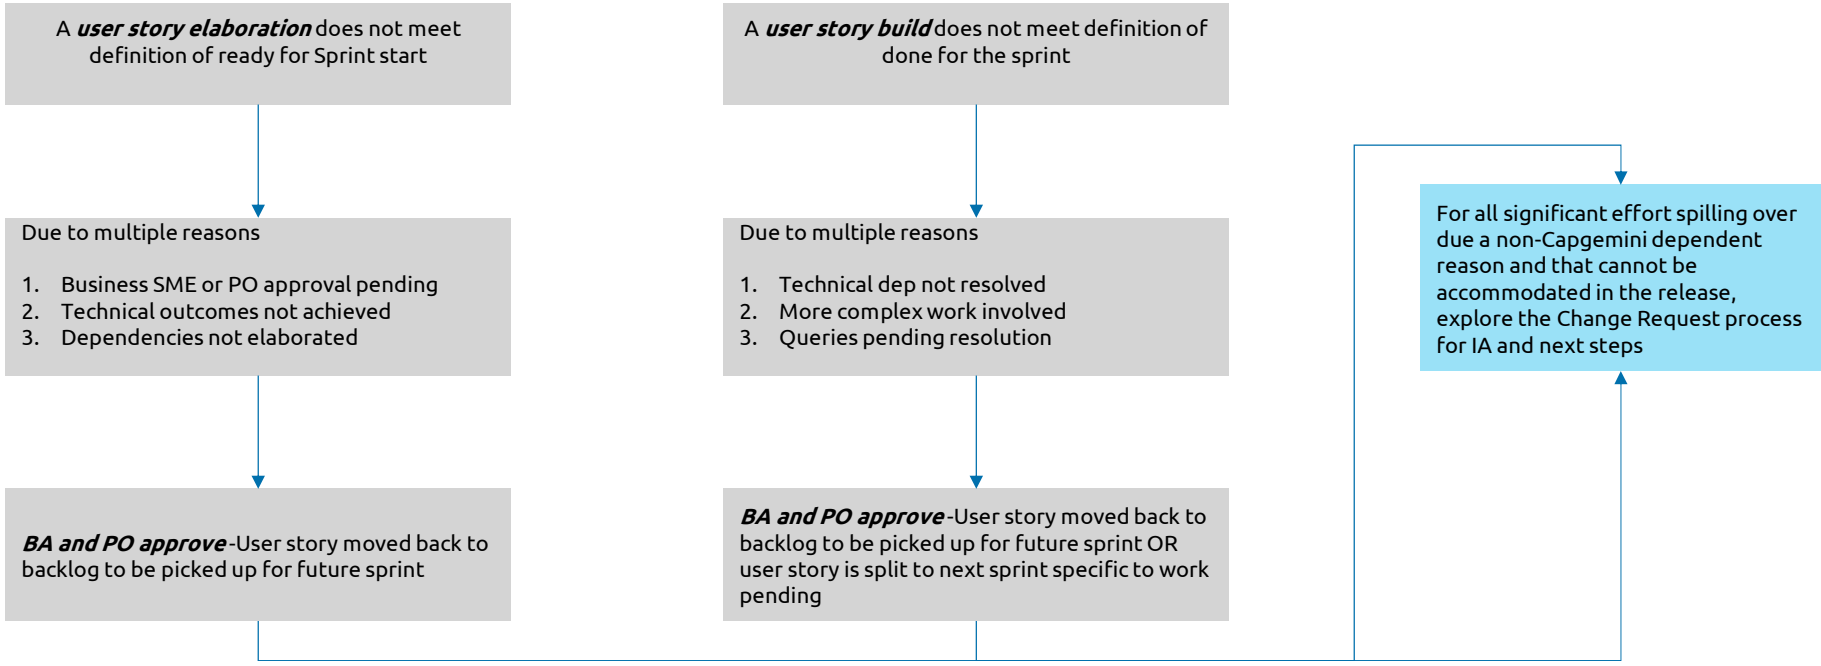

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Activities list

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Elaboration Phase Activities (elaboration + design)

Key activities during Elaboration include:

1. Clear evaluation & review of overall product & release back-log to assess where programme stands compared to the Go-Live
2. Where prep work is required, BAs will work with SMEs, POs and dependent teams to confirm what is needed in the elaboration workshops, based on the User Stories
3. PO and BA will define or identify user stories from the Project (release) backlog for sprint planning
4. At the start of each workshop, BAs will provide an overview of how to break down a User Story and what a good user story looks like
5. User Stories will be elaborated as per Definition of Ready with agreed acceptance criteria
6. Architect will review the User Stories to determine if there are any architectural considerations to be taken into the build
7. Artefacts required for each User Story will be agreed between the Release train team, PO and Architect
8. Sprint backlog and associated documentation is reviewed by PO and agreed to be ready to take into the Design Phase workshop
9. Where Out Of The Box functionality is included in the sprint, the environment should be available for demo

Activities	Overview	Duration	Roles	Inputs	Outputs
Sprint Planning	Sprint planning to review all the items in the backlog, identify all dependencies and any pre-requisites for the Sprint. The opportunity to share the vision and agree the Sprint Goal	4 hours*	RT, PO, BA, SME's, Architect Dependent team Leads	Backlog	Sprint Backlog to be taken into the Design phase Workshops
Stand-ups	Standup to track Sprint N readiness and plan Sprint N+1	Daily 30 minutes	RT, PO, BA's, SME, Architect,	Items on the board	Dependencies and blockers identified with accountable owner and target closure
Workshop	Detailed elaboration of requirement (Design Phase) and user stories	Daily 6 Hours max*	RT, PO, BA, SME, Architect	Backlog	Design Phase deck and detailed user story
Review	Review user story for formal acceptance by PO	3 Hours*	RT, PO, BA, SME, Architect	Backlog	Finalized Sprint Backlog
Retrospective	Part of the overall Sprint retrospective to provide feedback and suggest improvement	1 Hour	RT, PO, BA, SME, Architect	Feedback	Recommendations

**Sprint planning, Workshop and Review frequency and duration will be at the discretion of PO, BA and Stream Lead*

PO – Product Owner
BA – Business Analyst (Cap+Beazley)
SME – Subject Matter Expert

RT – *Release train (Cap+Beazley)*

Beazley here means Beazley other programme Release Trains that are required in the activity

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Build Activities

The objective of Build is to deliver user stories approved for the sprint

Key activities during Build (Sprint Execution) include:

1. Sprint kick off in Jira provided Sprint definition of ready is met.
2. Dev team to manage sprint backlog during sprint execution and will prioritize user stories for build
3. User stories in JIRA updated for remaining effort on frequent basis
4. Update story status, comment and due date in Jira to reflect latest status for reporting build progress, test execution, blockers, defect and dependency
5. Sprint progress will be tracked daily via Jira dashboard(s)
6. Release Train Leads to monitor sprint execution progress on daily basis
7. User stories that meet Definition of Done will be demoed to the PO and , Business SME for sign off
8. Stories that do not meet sprint goal OR Definition of Done will return to the product backlog for further refinement and prioritisation
9. Code merge activities if applicable in parallel release development
10. The desired outcomes of the Sprint and reporting includes:
    1. Unit Test Results
    2. Code Review Results
    3. QA sign off
    4. Daily sprint progress report (Jira dashboard snapshot)
    5. Sprint completion report
    6. Sprint retrospective

Ceremonies	Overview	Duration	Roles	Inputs	Outputs
Stand-up	Stand-up as part of the overall Sprint per Release train	Daily 30 mins	Release train	Items on the board	Dependencies and blockers identified and tracked for target closure
Scrum of Scrum	Standup to track sprint dependencies and blockers across Release Trains	Daily 30 mins	RT Leads	Items on the board	Dependencies and blockers identified and tracked for target closure
Sprint Planning	**Last day of Prev Sprint and First Day of current Sprint -** Review readiness of stories identified for Sprint	2 Hours	Scrum Team	User Stories	User stories ready for development
Demo	**As soon as user story build is complete -** Demo of completed User Story to PO/Business SME	1 Hour	PO, BA, Scrum Team	Product Increment	User story signed off by PO
Retrospective	**After Sprint completion -** Retrospective to provide feedback and suggest process improvements	1 Hour	PO, BA, Scrum Team	Feedback	Recommendations

**Review and Demo frequency and duration will be at the discretion of PO, BA and Stream Lead*

PO – Product Owner
RT – Release Train
SME – Subject Matter Expert

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

‘A day in a life’ during Sprint Development

- All in-scope and signed-off user stories to be handed over to development team
- Cap BA, Architect & Development teams to conduct Sprint Planning to validate DoR for sprint & each story. Sprint goal is agreed.
- Sprint planning sessions also cover – dependencies review, identifying key risks and issues that might impact sprint goal
- Cap BA or Business SME resolve queries raised by Developers or Test analysts against user stories assigned
- Daily stand-ups conducted separately for each Release Train (Policy, Billing, Integration etc). All risks/issues/dependencies are reviewed & logged



- All blockers to development or test execution are raised as SOS (Scrum of Scrum) blockers by Release Train leads, use war rooms to resolve
- User stories completing test execution are demoed to Business SME and signed-off
- JIRA as a single source of truth for the entire team to track user story progress on daily basis
- All unexpected impediments delaying user story completion are taken up for review & backlog refined accordingly
- Continuous review of Sprint progress by Program Management for any impacts on end Release goal

Actors

Product Owner | SMEs | Solution Architect | Team members | Functional Lead / BAs | Test teams

Accelerators / Tools

- All stories in-scope are signed-off, all templates updated
- JIRA for backlog management, development progress tracking
- Dev environments available
- SOS board usage
- Logs for risks, issues, dependencies & actions
- Use war rooms to collaborate

Best Practices

- Raise any blocker immediately on same day – get it to the SOS
- Always review DoR for user stories before start & DoD after completion
- Prg Mgmt to review SOS daily and unblock issues urgently
- Differentiate and report Change requests vs Defects, especially during story demo
- Schedule all demo upfront to block time, Business SME not to delay sign-off
- Keep an eye on the release goal in parallel to highlight risks/issues to the overall timeline

Challenges

- User story sign-off and handover on time before Sprint start
- Business SME time for demo & sign-off, last moment changes during demo
- Missed dependencies always affect critical path
- Delayed decision making across the teams affecting sprint goal – Dev, Design or Business

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Ca

Approach in dealing with Technical Spike Items

- Integration points from the Integration Inventory (manifest) qualifying as a Technical Spike item (to validate flow and connectivity) will be taken up with Capgemini and Beazley architects
- Prior to being taken up, all Technical Spike items must be assessed for impact on the Release effort & timeline
- All Technical Spike items must be small, definite and taken up to provide the necessary insights specific to the problem area and not be an effort to build a full solution
- Technical Spike items must be taken up for completion during inception or sprint elaboration phase of a sprint and not during development weeks in a sprint
- All Technical Spike item that may arise during development phase must be added to the Release backlog to be prioritized as necessary
- Any Technical Spike item that have dependency outside Guidewire PolicyCenter, BillingCenter and Guidewire Integration Gateway will need to be supported by Beazley

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Definition of Ready (DoR) and Definition of Done (DoD)

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

High-level Design – DoR and DoD

HLD Definition of Ready

- Business Requirements: The business requirements are well-documented, clear, and approved by stakeholders.
- Scope Defined: The scope of the project is clearly defined, including what is in and out of scope.
- Architectural Vision: An initial architectural vision is available.
- Stakeholder Alignment: All key stakeholders are identified and aligned with the high-level objectives.
- Resource Availability: Necessary resources (e.g., architects, senior developers) are available and assigned.
- Technical Constraints: Known technical constraints and dependencies are documented.
- Service Provider: Alignment with the service provider with regards to capability, design principles and well documented design

HLD Definition of Done

- Design Documentation: Complete high-level design documentation, including system architecture, data flow diagrams, exception flow and key components.
- Review and Approval: Design has been reviewed and approved by stakeholders, including architects and business SMEs.
- Alignment with Requirements: Design is aligned with business requirements and scope.
- Feasibility: Technical feasibility has been confirmed.
- Compliance: Design adheres to relevant standards, principles, and regulatory requirements.
- Integration Points: Key integration points with other systems are identified and documented.
- Dependencies: Major dependencies are identified and planned for.
- Solution designs must be in Beazley standard template as a minimum.

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Low-level Design – DoR and DoD

LLD Definition of Ready

- High-Level Design Completed: High-level design is completed, reviewed, and signed off by stakeholders i.e. technical and business architects.
- Detailed Requirements: Detailed functional and non-functional requirements are documented and approved.
- Technical Specifications: Low level technical specifications from Service provider and guidelines are available.
- Resource Availability: Necessary resources (e.g., developers, technical leads) are available and assigned.
- Development Tools: Development tools and environments are set up and accessible.
- Interface Definitions: Interface definitions are available for components that will interact with others.
- Acceptance Criteria: Acceptance criteria for low-level design are defined.

LLD Definition of Done

- Detailed Design Documentation: Complete low-level design documentation, including detailed class diagrams, sequence diagrams, database schema, and API specifications. Including Exception flow.
- Standards: Design adheres to GW and Beazley standards and guidelines.
- Review and Approval: Design has been reviewed and approved by technical leads and architects.
- Traceability: Design elements are traceable back to high-level design and requirements.
- Performance Considerations: Performance and scalability considerations are addressed.
- Security: Security requirements and considerations are integrated into the design.
- Testability: Design ensures that the system is testable and includes test cases.
- Documentation: All relevant documentation is updated and accessible. Solution designs must be in Beazley standard template as a minimum.

**LLDs will be developed in parallel with sprints*

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

User story – DoR and DoD

User Story Definition of Ready

- Requirement package is signed-off by Beazley SME which consists of a documented user story and acceptance criteria(s)
- User Stories are elaborated to have detailed functional, non-functional, integration requirements, business rules, FLS, process flows, mockup screens (only if applicable) and well-defined acceptance criteria
- Requirements hand-over is complete by Cap BA to development team
- All known dependencies associated with delivering a story have been resolved or any pending ones have an eta for resolution not affecting the user story development outcome
- Any dependent user story across PC config, integration, policy or billing is already available or has a plan in place not impacting the current story acceptance criteria
- Product dependencies (finalized Xmind map and APD) for story development are available
- User story development does not add customization above permissible guideline of 10%
- Any pre-dev tasks created during elaboration are marked complete in JIRA
- Third party connectivity dependency is resolved and available
- Agreement in place to use stub services or an alternate in absence of a working live integration

User Story Definition of Done

- User story is successfully demonstrated on top of the code built during the Sprint, that meets the acceptance criteria and is signed off by the PO/Business SME
- Unit test result and code review result are uploaded in Jira/Confluence
- Stub routines used to complete unit testing where a third-party service live integration is not available
- Code complies with GW cloud coding and security standards; all valid observations have a plan of action agreed
- Code is ready for deployment to a Test environment
- All sub-tasks of the user story are in DONE status
- Unit test cases to be achieved through Gunits
- Data tracker should be updated for any Data model changes
- Test execution is complete with no ' To Do' test cases pending in Jira OR there is an agreement and ETA for the pending ones
- No outstanding High Priority or Severity defects resolution open on the defects OR for any open ones, there is a conditional sign off with a ETA for fix. The defect priorities and severities will be assigned as per beazley QA defect management process. Ref testing - slide 65. The defects will be tracked in Jira through triage process.
- Test data used to test the scenarios are relevant and sanitized to ensure no production data is used.
- Identified automatable test cases are automation completed and integrated to the pipeline

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Sprint – DoR and DoD

Sprint Definition of Ready

- Sprint backlog hand off (technical and functional clarifications with PO/Business SME) is complete and user stories are in compliance with Definition of Ready
- Sprint backlog is based on the available sprint capacity (Build & QA hours available)
- Product Data Model requirements are finalized any Data requirements are resolved or have a plan in place without impacting Sprint delivery
- HLA is signed-off by the architecture team wherever applicable (applicability of this is determined during elaboration of requirements)
- Other Design items to be in place
  - External API or vendor specification document
  - IP whitelisting completed for any third-party connectivity
  - Service request and response mapping documents
- All dependencies have been resolved. Dependency items are agreed for all third-parties (internal and external)
- Environment configuration completed, and access setup done for Release train members

Sprint Definition of Done

- All user stories and sub tasks within a user story are in Done status
- Completed user stories follow the User Story Definition of Done or any exception is agreed with Beazley
- Stories not in 'Done' status have been moved out of the sprint in agreement with Beazley – Stories not in Done status are discussed with respective Product Owner based giving a visibility of a completion plan or a risk if exists. Story is either moved to subsequent sprint or parked in backlog for further action. (Please refer to User story management section for specific scenario covering this)
- Test execution is complete in Jira with no test cases in 'To Do' status or if any exception is agreed with Beazley
- High priority or severity defects have been either closed or there is a mutually agreed fix plan with Beazley for the open defects
- Code has been checked-in accordance with the DevOps pipeline
- Sprint completion reports has been shared with Beazley stakeholders - Product Owner, Programme management team
- Automation testing (if applicable) has a coverage to the requirement level as defined in the test strategy
- Sprint completion reports have been shared with Beazley stakeholders - Product Owner, Programme management team

PO – Product Owner
HLA – High Level Architecture

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

WORKING WITH GUIDEWIRE

ALIGNMENT, GOVERNANCE AND ASSESSMENTS


This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

THE 3-WAY COLLABORATION FOR SUCCESS

For the success of GPAS & Billing Program, It is critical for Capgemini-Beazley-Guidewire to work in close collaboration across phases of the Program execution.

BEAZLEY

- Finalize & maintain Product contract with Guidewire
- Conform requirements to OOTB
- Timely approvals pending architecture or design considerations
- Review code assessment reports
- Adhering to the Release management prescribed by Guidewire

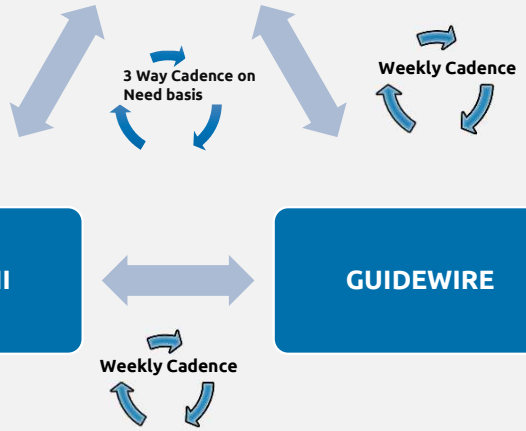

- Deploy certified technical team
- Build GPAS & Billing Code on SaaS platform
- Conform to Guidewire Cloud Coding standards
- Resolve Cloud assessment observations
- Collaborate for all major design decisions

- Provide SaaS platform to deploy GPAS & Billing solution
- Provide Dev and Prod environments
- Perform Code assessments & Design validations
- Updates on new product version releases
- Provide SME support as per the agreements with Beazley & Capgemini

KEY SUCCESS FACTORS

Align requirements to Product | Design and Build to standards | Collaborate on decisions


This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

Guidewire Cloud Assurance Assessment (CAA)

Cloud Assurance Program Goals are:

a. Assess and report adherence to Cloud Standards
b. Enforce remediation of Cloud Standards violations by the implementation team
c. Competency Assurance Periodic reviews conducted to ensure all Developers and Analysts are appropriately trained, certified and each workstream has the required Lead to Associate ratio (1:3). Managed by Guidewire Education team



All three components of Cloud Assurance are mandatory under the Guidewire Cloud Subscription

Overview:

- **Purpose:** Validate if developed code conforms to Guidewire Cloud standards
- **Frequency:** Monthly, at the end of each Sprint/Stabilization/Pre-Go-live

Assessment Methods:

- Automated Cloud Assurance is executed in TeamCity to run inspection on all Cloud Standards that have assessment type "Partial/Fully Automated".
- Additional manual code review of Cloud Standards that have assessment type "manual" are carried out by the Guidewire Cloud Assurance team

Outcome: Is a Cloud Assurance Report:

- GW provides report on custom code that violates Cloud Standards
- Provides suggested remediations in the Guidance section of the Cloud Assurance Report
- Capgemini and Beazley teams are provided access to the report

Review, Resolution & Reporting Process:

- **Issue Identification:**
  - Guidewire team identifies and documents issues in the Cloud Assurance Report
- **Assigning observations to developers**
  - All Cloud Assurance Report items are moved to JIRA board, assigned priority, and assigned to developers for fix
  - Any conversations on reported issues with Guidewire are completed by team ad-hoc and almost immediately
- **Reporting:**
  - The Guidewire observations fix status is reported via JIRA in the Sprint closure review provided to Beazley

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Developer Workflow

Feature Branch Creation and Code Changes

- Developer creates a Feature Branch from the release branch and applies changes to the code.

Developer Code Inspection

- Developer runs the Guidewire Assurance plugin to find deviations from cloud standards.
- If any code standard issues are reported by the plugin:
  - Developer fixes the issues and re-runs the Guidewire Assurance plugin.

Pushing to Bitbucket and CI/CD Pipeline


- Developer pushes the Feature Branch to the Bitbucket repository and waits for the TeamCity CI/CD pipeline to run.

Handling Test Failures

- If server or assurance tests fail in the TeamCity CI/CD pipeline:
  - Developer rectifies the code in Guidewire studio , pushes the changes to the Feature Branch and continues this cycle until the server test and assurance test pass in TeamCity.

Pull Request and Code Review

- Developer raises a Pull Request (PR) to merge the Feature Branch into the release branch.
- Lead developer provides code review comments within the PR and creates a task for the developer to refactor the code.

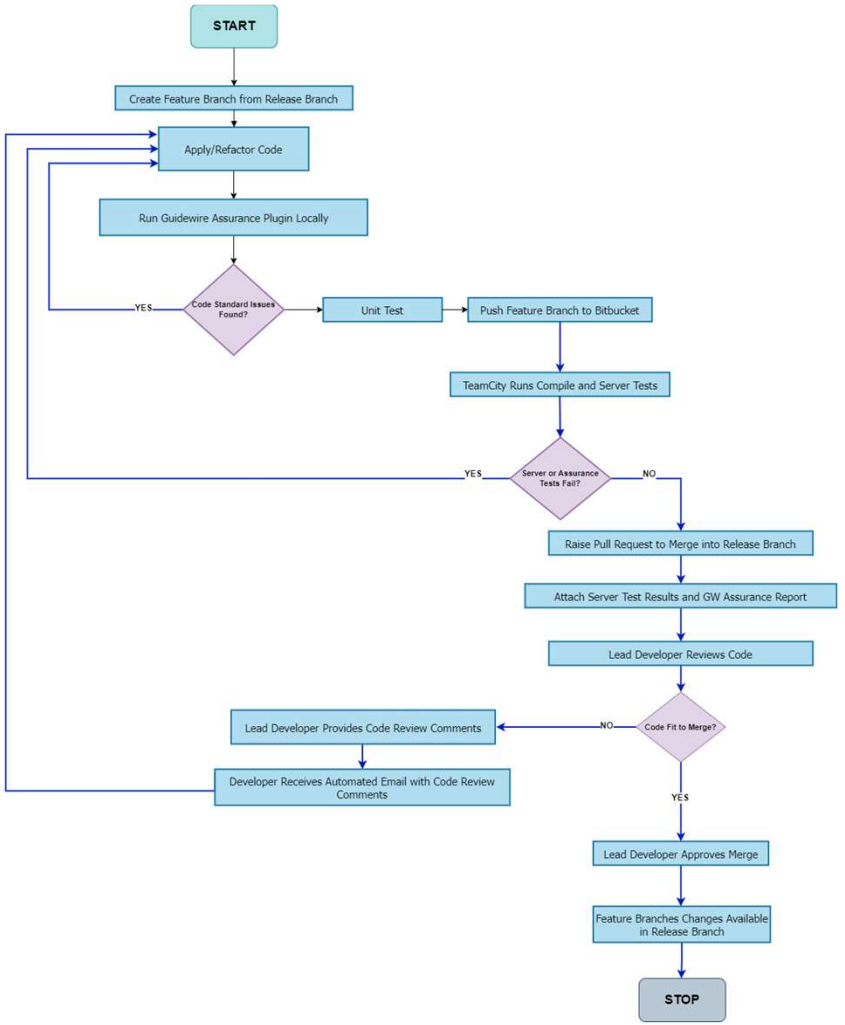


This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Git Branching and Merging Strategy

- **Guidewire Standard**: Follows *"Guidewire GW-MTH-1084 Branching Strategy for Guidewire Implementation Projects."*
  - Ensures robust, consistent process for managing parallel code changes within and across releases.
  - Intended for technical leads and implementation consultants.
  - Uses Git repositories for version control of source code and software artifacts
  - Managed using Guidewire-provisioned Bitbucket Server instance.
  - Implements the branching strategy described in the standard.

- **Branching Strategy Overview**:
  - **Production Branch (master)**:
    - Single production branch named master. Contains out-of-the-box product and configurations at project start.
    - Updated only during release activities or emergency fixes by senior developers.
  - **Product Release Branch (gw-releases)**:
    - Created off master at project start for new product versions and owned by Guidewire Customer and Cloud Operations.
  - **Mainline Branch (develop)**:
    - Single mainline branch named develop, created off master and contains all code across all releases.
    - Accessible to all team developers for merging.
  - **User-Story Branches**:
    - Created off develop or release branch for user stories.

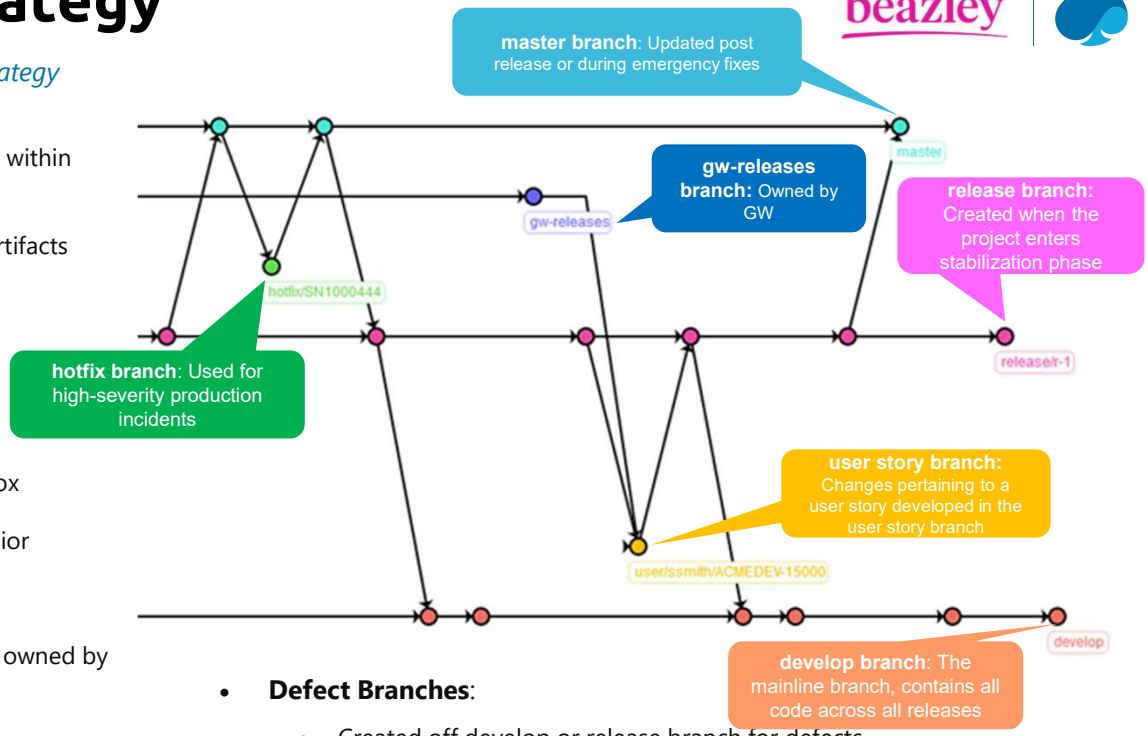

  - **Defect Branches**:
    - Created off develop or release branch for defects.
  - **Project Release Branches (release/r-*)**:
    - Used to stabilize code before moving to production and Named as `release/r-{release_number}`.
  - **Hotfix Branches (hotfix/*)**:
    - For high-severity production incidents and created off master and named `hotfix/{id}` and merged back to master and other branches by authorized developers

Note:

1. Code management strategy will be revisited once the single instance vs multiple instance code base approach is finalized (US region and UK region specific)
2. For the initial foundation release, there will be a single branch (develop)

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

GUIDEWIRE UPDATES PROCESS

Capgemini's GUIDEWIRE UPDATES SCOPE

- Capgemini will Update Beazley's Foundation Release to have the latest GW v10 release of PC and BC components
- To best protect the release delivery timeline, Version Update will be taken-up during Sprint development phase and not in Stabilisation phase (E2E+UAT)
- To keep the Update efforts within the plan, Beazley implementation must stay within 10% customization limit
- Updated code base will undergo regression testing, deployments into higher environments & developer synch-up activities

GUIDEWIRE LAYER AND CUSTOMER LAYER

- The Guidewire layer and customer layer are defined to designate clear ownership of files that are contained within the InsuranceSuite artifact
- For every Version Update cycle, Guidewire will perform the Guidewire Layer update, followed by Capgemini doing the customer layer update and regression testing

Indicative timeline for each Update activity

- Updates by Guidewire – 1 to 2 weeks
- Updates by Capgemini for Beazley code base – 1 to 2 weeks
- Regression testing across dev & test environments within build phase – 1 to 2 weeks
- Final sign-off by development team & developer workspace synch-up – 1 week

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Testing

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

SCOPE

Draft – To be updated once Test Strategy is finalized

In Scope

- **Functional testing** of Guidewire PolicyCenter & BillingCenter which is configured as per the requirements finalized and documented in the Product Backlog. The below scope might change based on the outcome of the architecture discussion which is in progress
  - ✓ Policy life cycle transactions (Example - New Submission, Policy change, Cancellation, Renewal, Rewrite and Reinstatement etc.')
  - ✓ Document triggers only – both out of the box and any customizations requested in requirements.
  - ✓ Business Rules- Underlying policy business rules (Underwriting, extension & renewal)
  - ✓ Roles- Role based testing (Underwriting org structure feed)
  - ✓ Billing lifecycle (Example - Co-insurance management, Delinquency management, Invoicing & commission management)
  - ✓ Batches in Policy Center and Billing Center.
- **Integrations** - Integrations with PAS / Billing through Integration Gateway and/ or direct through Integrations from guidewire. For example: (Authentication, Billing & Delinquency).
- **Test automation** – Sprint level test automation aligning to overall Automation Strategy
- **Product Rationalization** –Product Model will be converted as ADL (Admin Data load) and this will be validated against the relevant user stories.
- **Migration testing** - Policy Migration of D&O product lines from Source (On-prem) to Guidewire cloud

Out of Scope

- End to End Testing with components outside GPAS and Billing during Sprints
- Systems outside Guidewire - Policy Center & BillingCenter
- 3rd Party management – For Example – Scheduling/Planning, agreeing contracts, managing defects etc.
- Documents Testing (DocVault)
- NFT, OAT and UAT. Refer (E2E Test strategy)
- Beazley legacy system & its corresponding integration testing
- Downstream Systems within the Modernization Program
- Any other components that are not part of In Scope


This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

TYPES OF TESTING

Draft – To be updated once Test Strategy is finalized

Build & Test Phase

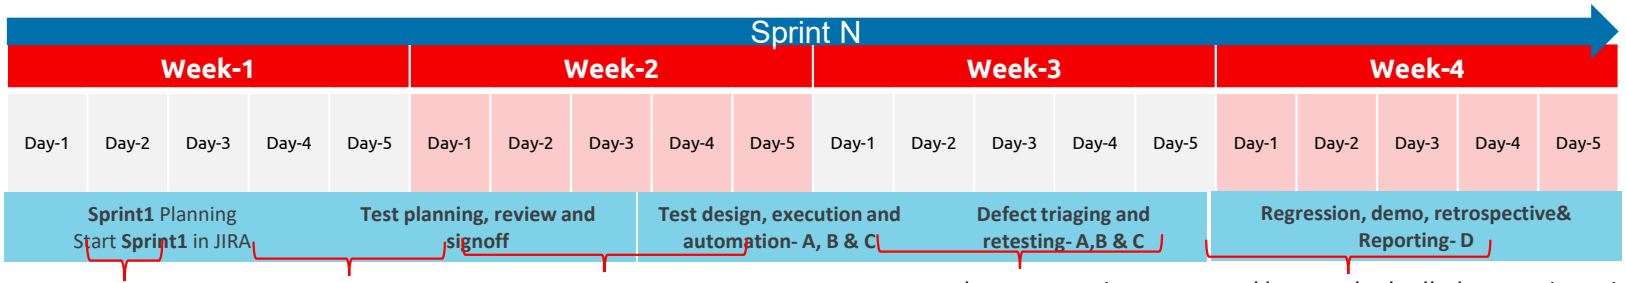

A- Functional testing-

- To test the system has been configured according to the provided acceptance criteria within the User story and this includes validating the Business rules, UI screens and field level validations.
- Requirement Traceability Matrix will be used to reflect the test scenarios coverage for requirements. This will be carried out for every user story as part of sprint for the following areas of capability or functionality such as Account creation & Policy Information
- All the Test scenarios/test cases will be peer reviewed by test leads.
- The test data required to perform the tests with variations will be compiled by the testing team. Data which has dependency from other systems will be coordinated and made ready before test execution.

B-Integration testing-

- To test each component is integrated with each other. Our Integration testing validates the payload of PolicyCenter and BillingCenter integrations through MDA/CDA and dependent systems should validate their own validations. This includes Internal and External Integrations. For Example, Internal Integrations (Authentication, Document Management) & External Integrations – Appian (Workflow Management), Oden, Oanda (Exchange Rate Service).
- These Integrations are tested by a method called API testing using (SOAP UI/POSTMAN) to verify the response with provided request and End point URL.
- This will validate various actions including Authentications, Payloads, response headers and basic schema validations & type lists.
- In-Sprint Integration testing - Integrations finalized in the Integration Manifest, will need to arrive at the sprint schedule in line with the sprint plan. Any deviations to this will need to be impact assessed. If these deviations can be accommodated without impacting the overall in-sprint testing schedule, Capgemini will seek to accommodate them, however, this cannot be guaranteed.
- Dependencies will be aligned to integrate policy center and billing center

C-Regression testing-

- During the end of every sprint, the tester will identify specific test cases to include into regression test suite.
- The regression test suite will be leveraged to ensure the code has not regressed in quality and validate features and functionality are still working as expected.
- This suite is incrementally built with a combination of manual & automated tests throughout the build & test phase

D -Automation Testing-

- Automation Testing approach will be updated based on Program Test Automation strategy.

This content is specific to GPAS & Billing Release Trains delivery only and in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Testing Activities

Draft – To be updated once Test Strategy is finalized

Key activities during In Sprint Testing:

1. Test Plan (Scope, risks, defects). Refer this for detail Test Approach - Test Strategy for Sprint Testing - GPAS & Billing
2. Test design based on acceptance criteria for GPAS and Billing
3. Test review & sign off to ensure coverage, negative sessions, boundary conditions and defect status and mitigation.
4. Test data preparation to ensure right data is used to test the scenario
5. Traceability of test cases to corresponding functional user stories via JIRA
6. Sanity check on In Sprint Testing environments
7. Test execution
8. Regression testing (Automation + Manual)
9. Defect reporting
10. Participation across all Sprint events including user story demo.
11. Test Completion report at the end of Sprint

Test Governance (as per Test Strategy)

1. Daily Testing status meeting with team and Beazley key stakeholders to bring out and resolve impediments
2. Weekly risk & status meeting with leadership for making key decisions

*** JIRA will be single source of truth for all test cases, executions, defects & status reports*

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

TESTING DELIVERABLES

Draft – To be updated once Test Strategy is finalized

Deliverables	Phases	Purpose	Ownership	Reviewed By	Sign off By	Frequency	Format
Test Strategy for Sprint Testing	Inception	This document defines the overall test approach for the program & all types of testing that will be conducted	Capgemini	Natraj Gudla (Cap-India delivery executive) Ananda Ponniah (Cap- Engagement Manager)	Faye Newton (Beazley) Warren Pilkington (Beazley) Nithya Midde (Beazley) Stephen Payne (Beazley) Athik Miah (Beazley) Alagiya Nambi Rajappan (Hexaware) Carol Hamilton / Patrycja Kuligowska (Beazley) Kim Cisco US / Abby Vrendenburg (Beazley)	End of Inception	Word
Test Plan	Build & Test	This document defines the scope, approach, schedule of intended test activities. ·Sprint level Test Plan	Capgemini	Test leads (Hexaware/Beazley)	Capgemini Test Manager	Start of each Sprint	Word/PPT
Test Cases	Build & Test	Test Cases or scripts that will be executed	Capgemini	Capgemini Test Leads	Capgemini Test Manager	Once per release	JIRA
Test Automation Report	Build & Test	Test automation details to understand the efficiency, accuracy, and speed to reduce cycle time	Capgemini	Capgemini Test Leads	Capgemini Test Manager	Once per week	JIRA
Test Completion Report	Build & Test	Provides the summary of Test execution - Sprint summary report -	Capgemini	Capgemini Test Leads	Beazley Program Test Lead	- End of each sprint	Email/JIRA

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

KEY RISKS

Draft – To be updated once Test Strategy is finalized

Risks	Impact	Severity	Likelihood	Mitigation
Test Data- Inadequate or Incorrect Test data	Test Coverage	High	High	Follow test data management procedure before commencing Test execution phase
3rd Party Integration – Delay in engagement with suppliers will result in not getting integration test requirements as per the plan	Schedule	High	High	Early Management & involvement from 3rd parties with clear articulation of test dependencies will mitigate the delay
Defects Volume – If the number of defects in sprint exceeds, this will result in lack of quality and effort	Quality & Cost, Schedule	High	Medium	Effect code reviews and through Unit testing during development will help mitigate this risk
Overlapping Phase – Delay in defect fixes/deployment will impact test deliverables timelines	Schedule Deviation	High	Medium	Establish processes for phase overlapping changes, defect management, resolution and diligent compliance with the SLAs defined
Environment Downtime – Environment downtime during sprints (Build & Test) and SIT will impact test delivery timelines	Schedule Deviation	High	Medium	Testing team should be informed well before, in case of any planned downtime. Infrastructure team should be made available for quick resolution in case of any unplanned or unexpected downtime
Handover Delay – User Story handover delay to QA delay will result in current Sprint testing spill overs	Schedule Deviation	High	Medium	Establish and agree handover timelines with dev & env team

*All the testing dependencies will be included in the programme risk register (In JIRA) periodically for review and closure

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work

Company Confidential © Capgemini 2024. All rights reserved |

KEY ASSUMPTIONS & DEPENDENCIES

Draft – To be updated once Test Strategy is finalized

Phase	Assumptions
In Sprint Testing	• Approved product backlog will be considered as the final scope document • It is assumed that Guidewire OOTB features, and functionality will work as expected

Phase	Dependencies
Start of Build & Test	Availability of test environments (per the defined plan (Confluence Link), Testing tools for QA team -
Start of Build Phase	Review & sign off on the Test strategy
Start of Sprints	Review of the Test scenarios (Peer Review)
All Sprints/Phases	Dependency on the blocker query resolution to enable testing
All Sprints/Phases	Dependency on the test data- Internal systems data load and external support from external vendors on their test environments

Company Confidential © Capgemini 2024. All rights reserved |

TOOLS & FRAMEWORK

Draft – To be updated once Test Strategy is finalized

Test Area	Description	Tools	Phase
Test Management & Defect management	To maintain Test strategy, Plans, Traceability, Test Scenarios, Test data, Reports, Test Cases and Defects	Jira /Sharepoint/ Confluence	Build & Test
Functional Testing	To test the system has been configured according to the provided acceptance criteria	Guidewire Cloud Instance	Build & Test
Integration Testing by API Method	To test the interfaces and Web Services	SOAP UI/POSTMAN	Build & Test
UI Testing	To test the UI components	TBD	Build & Test
Automation	For Automating smoke & release regression scripts	TBD	Build & Test
Test Configuration Management	To store Test Data Libraries, Assets and automation scripts	Bitbucket	All

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Third party Dependencies and Alignment


This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Dependencies – Introduction

For GPAS & Billing Transformation at Beazley, we have differentiated between…

1. Point-to-Point Dependencies e.g. between Release trains within the programme or with another programme.
2. Complex Dependency Chains e.g. passing between Release trains and out to 3rd parties.

The process followed is similar for both, and involves 3 key steps…

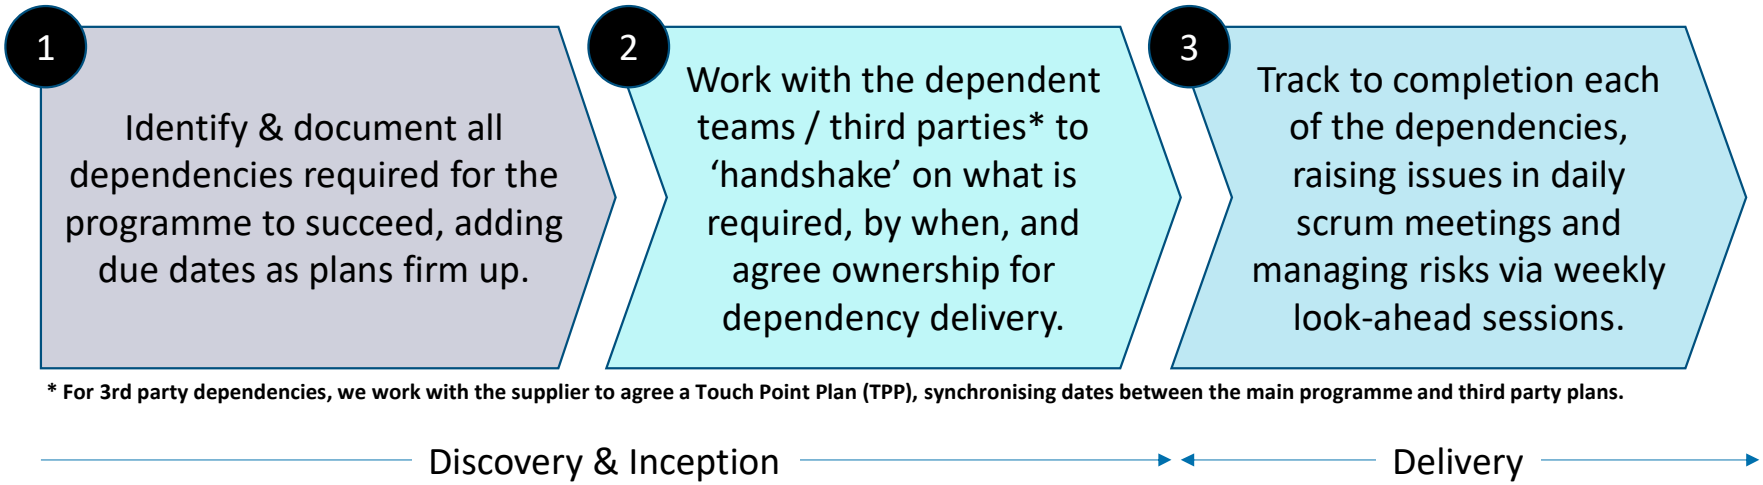

*** For 3rd party dependencies, we work with the supplier to agree a Touch Point Plan (TPP), synchronising dates between the main programme and third party plans.**

This approach is no silver bullet, but it helps us secure on-time delivery of cross-Release train and cross-programme dependencies, and provides visibility of what is required by each team to shore-up the end-to-end delivery.

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

1. Point to Point Dependencies – Within Programme (example data)

Set-up:

Step 1 (Discovery & Inception):
GETTING RT Lead documents the dependencies they have on other Release trains / client programmes.

Step 2 (Discovery & Inception):
GETTING RT Lead aligns with the GIVING Release Train Lead(s) / Other Programme Lead(s) on timeline, marking the date of the 'Handshake'.

Step 3 (Delivery):
Daily Scrum calls to unblock issues. Weekly reviews of coming due dependencies with RT Leads, updating status and agreeing corrective action.

RT#	RT Lead	Release train GETTING the Dependency	Release train / Entity GIVING the Dependency	Required by Sprint (Start of…)	Required by Date	Dependency ID	Dependency Description	Handshake Date	Status
1	Joe Bloggs	RT01-Claims Center	PGM01-Underwriting Workbench Pgm	S1-Build	03-Apr-23	RT01-PGM01-01	Dependency to supply signed off Technical Design Documentation (TDs).	01-Feb-23	Forecast Delay Plan to Recover
1	Joe Bloggs	RT01-Claims Center	PGM02-Aptian Workflow Pgm	S3-Elaboration	01-May-23	RT01-PGM02-01	Dependency to attend and sign-off against Requirements during S3 Elaboration for input into S3 Build.	01-Feb-23	On Track
2	Jane Bloggs	RT02-Data	PGM03-Policy Admin System	S2-Build	01-May-23	RT02-PGM03-01	Dependency to supply signed off Integration Design Documentation for S2 Build.	01-Mar-23	On Track
2	Jane Bloggs	RT02-Data	PGM04-Data Transformation Pgm	S3-Build	29-May-23	RT02-PGM04-01	Dependency to supply signed off Data Dictionary in time to support S3 Build.	None	

MASTER
ıdency Tracker Ten

Reporting:

Release train	Count of Handshakes Missing
2	1
6	34
9	8
12	3
13	2
14	27
19	1
(blank)	
Grand Total	76

An example of the reporting produced to show the number of handshakes that are outstanding.

This is published to drive RT Leads to complete handshakes so that there is a commitment made by the GIVING Release train to the GETTING Release train.

Count of Dependencies Due				
GETTING Release train	06/03/23	10/03/23	13/03/23	17/03/23
2		2		
4	1		4	
7				1
10		1		13
14			1	10
19				1
Grand Total	1	3	5	25

An example of the reporting used to show the number of dependencies coming due.

This is published to drive RT Leads to continually manage their dependencies, ensuring they are on track, and taking appropriate actions where required to avoid impact of any delays.

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

2. Complex Dependency Chains – with 3rd Parties (example data)

Set-up:

	D	I	K	L	Q	S	X	Y	Z	AC	AD	AE	AF	AG	AH	
1		WS17					WS01.1			WS04		WS17		WS13		
2	Integration	SOW Prep Start Date based on Draft TPP	SOW finalised by	Intro contacts with TP	Finalized TPP post elab	Latest date for Interface Spec from WS02/05	High level design	Provisional SRD readiness	SRD Finalized post elab	WS04 Build Start date	WS04 Build end date	Test Data Availability	Date by when WS17 gives the ticket to WS13	WS13 establishes Connectivity to endpoints from WS04, WS02/05 and TP	SFTP Setup	Es conne WS04 t th
3	Address Verification	Not required	Not required	Complete	Complete	Complete	Complete	Complete	Complete	REUSE of existing		Complete	REUSE	REUSE	REUSE	
4	Imburse (single access point to 3rd p	13/02/2023	13/03/2023	Complete	13/03/2023	13/03/2023	13/03/2023	20/02/2023	13/03/2023	01/05/2023	22/05/2023	10/04/2023	06/03/2023	13/03/2023	N/A	13/
5	EFT Payments	02/03/2023	17/03/2023	Complete	10/03/2023	10/03/2023	10/03/2023	13/03/2023	13/03/2023	27/02/2023	27/03/2023	10/04/2023	06/03/2023	13/03/2023	N/A	13
6	Geocoding and Mapping	Not required	Not required	Complete	Complete	Reuse	Complete	Complete	Complete	REUSE of existing		Complete	REUSE	REUSE	REUSE	
7	Government Sanctions	Not required	Not required	Complete	Complete	Reuse	Complete	Complete	Complete	REUSE of existing		Complete	REUSE	REUSE	REUSE	
8	Credit Scoring	10/02/2023	24/02/2023	Complete	13/03/2023	13/03/2023	10/03/2023	13/03/2023	16/03/2023	23/02/2023	13/03/2023	10/04/2023	06/03/2023	13/03/2023	Not required	1
9	FIS GETPAID	10/02/2023	24/02/2023	Complete	13/03/2023	13/03/2023	10/03/2023	22/02/2023	03/03/2023	06/02/2023	13/03/2023	10/04/2023	06/02/2023	13/02/2023	Not required	1
10	Bottomline Legal-X	23/02/2023	08/03/2023	Complete	03/03/2023	13/03/2023	Complete	Complete	06/03/2023	REUSE of existing		13/03/2023	REUSE	REUSE	REUSE	
11	Exchange Rate Service	23/01/2023	13/03/2023	Complete	13/03/2023	13/03/2023	N/A	N/A	N/A	N/A	N/A	10/04/2023	06/03/2023	13/03/2023	13/03/2023	13
12	Oden	16/01/2023	24/02/2023	Complete	13/02/2023	13/02/2023	10/02/2023	30/01/2023	Complete	23/02/2023	13/03/2023	13/03/2023	~~06/03/2023~~	13/03/2023	Not required	13

→ The chain of Proj/Prog is listed out.

→ All activities are listed out in the order they need to take place.

→ The dates by when each activity needs to be completed by each Proj/Prog and for each supplier is documented and forms the input to the TPPs.

Reporting:

#	Third Party	Sprint	R1 Reuse	WS17 PM	Initial Contact	HLD Produced	HLD Shared	TPP (Touch Point Plan) Forecast Date	Notes
1	Address Verification	1	Y	J Bloggs			N/A		No direct TP involvement.
2	Imburse (single access point to 3rd party payment gateways)	~~2~~ 4	Y	T Smith			N/A		20 Feb: CRXX moved this to sprint 4 but work is proceeding in S3. TPP signed off. SOW is with Imburse for signature – expected 24 Feb
3	EFT Payments	2	Y	J Prince			N/A		26th Jan - TPP signed off.
4	Geocoding and Mapping	2	Y	B Lawler			N/A		26th Jan - TPP signed off.
5	Government Sanctions	3-4		F Payne			13/03/2023	03/03/2023	24th Feb – James Kane now back at work and call scheduled 27th Feb. Moving WS02 work to S4 would put pressure on remaining sprints so work is starting at risk in S3 based on assumptions that F Payne is validating. Submit Claim schema sent to Gov Sanctions 23 Feb. PSR schema discussed and awaiting feedback. JIRA Ticket CTPSOS-348 updated.
6	Credit Scoring	3		L Jones					24th Feb – CS shared an updated specification for API on 23/02. This has led to a resubmission of SRD on 23/02. Regular catchup with CS during build taking place. SOW is with FD for signature. TPP approved.
									24th Feb– TPP shared. Meeting scheduled 02 March. Following escalation on [illegible] and to address any

A weekly report showing the status of each supplier integration is produced and reviewed with the programme leadership to ensure quick decisions / corrective action is taken for 'at risk' dependencies.

This is crucial within an agile environment to drive delivery in complex multi Proj/Prog & supplier environments.

Company Confidential © Capgemini 2024. All rights reserved |

Catalogue of Thirdparty dependencies across phases

Sprint Phase	Cap Dependency detail	Cadence Touchpoint	Third Party
Elaboration & Design	• Align integrations in-scope for sprint • Transaction details of integration • Timeline dependency for service availability • Requirement of third-party support • Environment and connectivity detail **Roles: Release Train Leads, Architects, Technical SME**	• Sprint planning meeting • Requirements workshops • Playback sessions	**Roles: Release Train Leads, Architects, Technical SME** • Confirmation of dependencies can be met • Service availability schedule • Highlight challenges with environment
Development	• Service availability, connectivity and stability • Service developed to requirements agreed • Service defect fixes and ETA • Test data requirements • Defects, data validations and environment issues resolved in same day **Roles: Release Train Leads, Architects, Technical SME, Test leads**	• Access to JIRA for all incidents • Defect triage call • Weekly twice touch point meetings • Retrospective meetings	**Roles: Release Train Leads, Architects, Technical SME** • Support and sign-off test case validations • Access to environments • Environment and Escalation support • Support window (Timings in a day that the service is available to be informed • Any maintenance/downtime schedule to be shared
Stabilisation	• Service availability, connectivity and stability • Service defect fixes and ETA • Test data requirements • Defects, data validations and environment issues resolved in same day **Roles: Release Train Leads, Technical SME, Test leads**	• Access to JIRA for all incidents • Defect triage call • Weekly twice touch point meetings	**Roles: Release Train Leads, Architects, Technical SME** • Support and sign-off on business flows • Access to environments • Environment and Escalation support • Support window (Timings in a day that the service is available to be informed • Any maintenance/downtime schedule to be shared

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Third party response time

Phase	Dependency	Expected response time
Elaboration & Design	Sample file format for inbound and outbound feeds	By start of the sprint
	Third party test scenarios which are required for providing sign-off	Week 1 of the sprint
	Document Third party test scenarios (If any) which are required for providing sign-off	1 Week prior to sprint start date
Development	Environment availability, stability and access	1 working day
	Test Data needs	1 or 2 working days
	Sign-off on Data outbound feeds as per sprint plan	5 working days after the test completion
	Data validations	1 working day
	Defects turnaround time	Critical - 2 Hours, High - 1 day, Moderate - 3 days, Manageable - 5 days
Stabilization	Environment availability, stability and access	1 working day
	Test Data needs	1 or 2 working days
	Sign-off on Data outbound feeds as per sprint plan	5 working days after the test completion
	Data validations	1 working day
	Defects turnaround time	Critical - 2 Hours, High - 1 day, Moderate - 3 days, Manageable - 5 days

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Metrics

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Tracking Sprint progress

Each Sprint to have a daily reporting through JIRA dashboards to track velocity numbers by story or story points and other test metrics as applicable. The dashboard designs will be agreed between the RTLs and programme governance teams. Following are some of the standard metrics that are proposed for tracking progress

SPRINT - VELOCITY by stories	• User story burn down tracking. Planned vs Actual on a daily basis • Team to take up corrective action for any lag in the burn down • Burndown charts by Release Trains
SPRINT - VELOCITY by story points	• Story points burn down tracking. Planned vs Actual on a daily basis • Team to take up corrective action for any lag in the burn down • Burndown charts by Release Trains
SPRINT PROGRESS	• User stories progress by Release Train through life cycle (dev vs test) • Reports made available via JIRA dashboards
RELEASE – VELOCITY	• User story or story points burndown. Planned Vs Actual for full release • Reports made available via JIRA dashboards
DEPENDENCISES TRACKING	• A mechanism to be developed to track external dependencies and delays
TEST METRICS	• Coverage metrics – Requirements, User story, Business process during stabilisation • Test metrics – Test execution burndown • Defect metrics – Defects by severity/priority, by Release Train, over time, rejection

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Sprint Closure pack

A Sprint Closure pack will be presented to Beazley for each sprint approximately a week after the sprint is formally closed in JIRA. Assuming sprint X closes formally in JIRA on a Monday, the closure pack will be published by Friday same week.

Sprint Closure Pack contents: All data extracted from JIRA

- Baseline vs Planned vs Delivered Story Points
- Sprint closure stats & Deferred stories data
- Overall active defects
- Guidewire Cloud assessment status
- Release burndown – Orig vs Current
- Potential risks for overall Release plan due to delays (if any)
- Status of DOD, DOR & Retrospective links
- Guidewire conformance summary for user stories

Sample Summary in the Closure Pack showing Planned Vs Delivered stories

Baseline vs Planned vs Delivered SPs

This document summarizes Foundation Sprint 2 closure status for following Capgemini workstreams:

Workstream	Baseline SPs for sprint 2 A	Actual Planned SPs for sprint 2 B	Delta (B-A)	Delivered SPs	Velocity
PolicyCenter	364	401	37	362	90%
Integration	189	190	Sample	178	94%
BillingCenter	258	196	-62	181	92%
	811	787	3	721	**92%**


Reason for Delta

- SOS123 – Billing XYZ stories were not ready at the start of Sprint 2 (62 SPs)
- Policy ABC stories were pulled in from future sprint which were ready to build (37 SPs)


Reason for Spill over

- SOS111 – ABC testing impacted due to delays from third party GZH (complete functionality not delivered (16 SPs)
- SOS222 – Policy XYZ testing is impacted as mapping changes are not yet finalized (13 SPs)

Sample Release Burndown

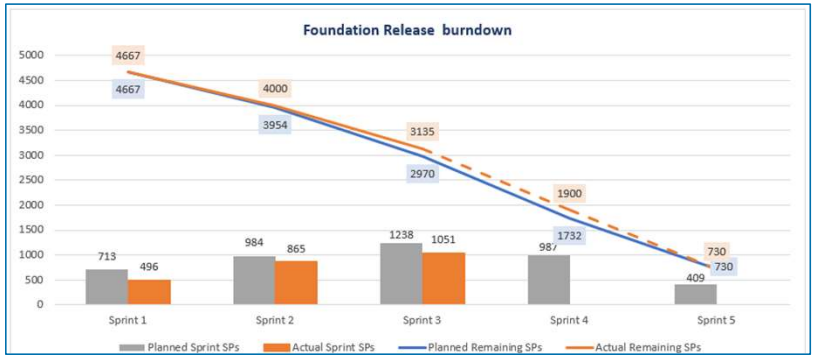

Sample JIRA board showing Guidewire Assessment observations

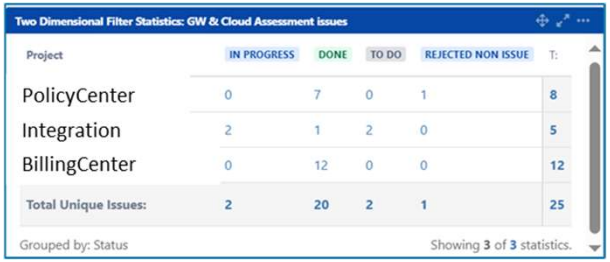

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

Appendix

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |

LESSONS LEARNED FROM UWWB PROJECT

General	• New/change-in scope to be channelled through Change management process • Direct access to Business SMEs by Cap Bas to clear any gaps in requirements • Misalignment between the requirements shared by the Beazley BAs vs Beazley Architect • E2E flow demos to be provided by the business that includes third party systems
Environment	• Environments to be in place before Build phase • Plan test data creation for Testing Team in advance to avoid test execution delay
JIRA Hygiene	• Adhering to DOD & DOR for moving story to next stage/status • Adhering to Sprint DOD & DOR to start the sprint in Jira • Having one workflow scheme configuration across Release trains within the programme • Updating ETA & latest status for dependent stories/task in Jira on regular basis • Adding latest comments to the issue as & when there are changes • Linked Issues to be effectively utilized esp. when dependency is identified
Logistics and Access	• Access to Beazley building & floor to work along with GPAS & Billing team • Access to GPAS & Billing team's calendar to plan meeting better

This content is specific to GPAS & Billing Release Trains delivery only which is in Capgemini's scope of work
Company Confidential © Capgemini 2024. All rights reserved |



About Capgemini

Capgemini is a global leader in partnering with companies to transform and manage their business by harnessing the power of technology. The Group is guided everyday by its purpose of unleashing human energy through technology for an inclusive and sustainable future. It is a responsible and diverse organization of over 325,000 team members more than 50 countries. With its strong 55-year heritage and deep industry expertise, Capgemini is trusted by its clients to address the entire breadth of their business needs, from strategy and design to operations, fueled by the fast evolving and innovative world of cloud, data, AI, connectivity, software, digital engineering and platforms. The Group reported in 2021 global revenues of €18 billion.

Get the Future You Want | www.capgemini.com



This presentation contains information that may be privileged or confidential and is the property of the Capgemini Group.

Copyright © 2023 Capgemini. All rights reserved.
